QUARTERLY EM&A REPORT

The Jockey Club CPS Limited

Central Police Station Conservation and Revitalisation Project: Thirteenth Quarterly EM&A Report (1 November 2014 to 31 January 2015)

Issue Date: March 2015

Environmental Resources Management

16/F Berkshire House 25 Westlands Road Quarry Bay, Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com The Jockey Club CPS Limited

Central Police Station Conservation and Revitalisation Project: Thirteenth Quarterly EM&A Report (1 November 2014 to 31 January 2015)

Issue Date: March 2015

Reference 0095646

For and on behalf of				
EKM-Hong	Kong, Limited			
Approved	by: Frank Wan			
	Warden T.			
Signed:				
Position:	Partner			
Certified by				
(En	vironmental Team Leader – Winnie Ko)			
Date:	24 March 2015			

This report has been prepared by ERM-Hong Kong, Limited with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client.

We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.

This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on the report at their own risk.



阿特金斯 ATKINS 香港九龍尖沙叫

香港九龍尖沙咀海港城 九倉電訊中心十三樓 13/F Wharf T&T Centre Harbour City Tsim Sha Tsui Kowloon Hong Kong

Telephone (852) 2972 1000

Your ref. 0095646_let_Atkins_20150330 Thirteenth Quarterly EM&A Report.doc Facsimile (852) 2890 6343

Our ref. 5121189/17.20/OC080/SO/EK

info.hk@atkinsglobal.com www.atkinsglobal.com

Date: 30 March 2015

By Email and Post

ERM-Hong Kong Limited, 16/F Berkshire House, 25 Westlands Road, Quarry Bay, Hong Kong

Attn: Ms Winnie Ko

Dear Winnie,

Central Police Station Conservation and Revitalization Project Verification of Thirteenth Quarterly EM&A Report

We refer to your letter dated 30 March 2015 regarding the Thirteenth Quarterly EM&A Report. Atkins China Ltd. verifies, in the capacity of Independent Environmental Checker, that the report, in principle, conforms the requirements provided in Section 10.4 of the EM&A Manual.

Yours sincerely, For Atkins China Ltd.

Sharifah Or

Independent Environmental Checker

c.c. HKJC – Mr. Kenneth Lee Rocco Design Architect – Mr. Charles Kung By Email By Email

CONTENTS

	EXECUTIVE SUMMARY	1
1	INTRODUCTION	1
1.1	PURPOSE OF THE REPORT	1
1.2	STRUCTURE OF THE REPORT	1
2	PROJECT INFORMATION	3
2.1	BACKGROUND	3
2.2	SITE DESCRIPTION	3
2.3	CONSTRUCTION ACTIVITIES	3
2.4	CONSTRUCTION PROGRAMME	5
2.5	PROJECT ORGANISATION AND MANAGEMENT STRUCTURE	6
2.6	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	6
3	ENVIRONMENTAL MONITORING REQUIREMENTS	9
3.1	Noise Monitoring	9
3.2	CULTURAL HERITAGE	11
3.3	LANDSCAPE AND VISUAL MONITORING	12
4	IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES	1 13
5	MONITORING RESULTS	14
5.1	Noise	14
5.2	LANDSCAPE AND VISUAL MONITORING	14
5. 3	CULTURAL HERITAGE	15
5.4	WASTE MANAGEMENT	19
5.5	EFFECTIVENESS OF MITIGATION MEASURES AND MONITORING	19
6	ENVIRONMENTAL SITE INSPECTION	20
7	ENVIRONMENTAL NON-CONFORMANCE	22
8	REVIEW OF THE EM&A DATA AND EIA PREDICTIONS	24
8.1	NOISE	24
8.2	Waste Management	24
8.3	SUMMARY OF REVIEW	25
9	CONCLUSIONS	26

LIST OF TABLES

Summary of Construction Activities undertaken in this Reporting Period
Summary of Environmental Licensing, Notification and Permit Status
Construction Phase Noise Monitoring Locations
Noise Monitoring Equipment
Action and Limit Levels for Construction Noise Monitoring
Alert, Alarm and Action (AAA) Levels for Vibration Monitoring
Event and Action Plan for vibration monitoring
Status of Required Submissions
Findings of Monthly Tree Inspection in the Reporting Period
Quantities of Waste Generated from the Project
Comparison of Construction Noise Standard and Noise Monitoring Results
Quantity of Actual Amount of C&D Materials, General Wastes and Chemical
Wastes Generated and EIA Estimation

LIST OF ANNEXES

Annex A	Locations of Works Areas and the Surroundings
Annex A1	Project Location
Annex A2	Declared Monuments within the Project Site
Annex A3	Site Layout Plan marked with Works
Annex B	Project Organization Chart and Contact Detail
Annex C	Locations of Noise Monitoring Stations and Noise Sensitive Receivers
Annex D	Monitoring Schedule of the Reporting Period
Annex E	Calibration Reports for Calibrators and Sound Level Meters
Annex F	Event/Action Plans for Noise
Annex G	Summary of Implementation Status
Annex H	Noise Monitoring Results
Annex I	Construction Programme of the Project
Annex J	Waste Flow Table
Annex K	Environmental Complaint, Environmental Summons and Prosecution Log
Annex L	Records of Vibration Monitoring for Trial Piling and Pipe / Bored Piling Works
Annex M	Records of Vibration Monitoring for Other Construction Works
Annex N	A Summary of Current Condition of Character Defining Elements

EXECUTIVE SUMMARY

The construction works of **Central Police Station Conservation and Revitalisation Project** commenced on 24 October 2011. This is the thirteenth quarterly Environmental Monitoring and Audit (EM&A) summary report presenting the EM&A works carried out during the period from 1 November 2014 and 31 January 2015 in accordance with the EM&A Manual.

Environmental Monitoring and Audit Progress

A summary of the monitoring activities undertaken in this reporting period is listed below:

•	 Construction Noise Monitoring during normal weekdays at 			
	each monitoring station	16 times		
•	Joint Environmental Site Inspection	3 times		
•	Heritage Site Inspection	59 times		
•	Landscape & Visual Monitoring	3 times		
•	Tree Inspection	3 times		
•	Vibration monitoring for piling works	380 times		
•	Vibration monitoring for other construction works	228 times		

Noise

16 sets of 30-minute construction noise measurements were carried out at each of the monitoring stations (NM2 and NM6) during normal weekdays of the reporting period. No exceedance of the Action or Limit Level of construction noise was recorded during the reporting period.

Cultural Heritage

Trial Piling and Piling works

Vibration monitoring carried out for the trial piling and piling works during the reporting period are listed below:

- 76 vibration monitoring measurements for the basement construction at Parade Ground;
- 76 vibration monitoring measurements at Block 8;
- 76 vibration monitoring measurements at Old Bailey Wing (Block 50);
- 76 vibration monitoring measurements at Block 51; and
- 76 vibration monitoring measurements at Block 17.

Other Construction Works

Vibration monitoring carried out for other construction works during the reporting period are listed below:

- 76 vibration monitoring measurements for the structural addition and alteration works at Block 1;
- 76 vibration monitoring measurements for the structural addition and alteration works at Block 14; and
- 76 vibration monitoring measurements for the structural addition and alteration works at Block 11.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

59 heritage site inspections were conducted and the Contractor has generally implemented the necessary protection measures as recommended.

Landscape & Visual

Landscape and visual monitoring has commenced since October 2011 on a monthly basis. Three monthly tree inspections have been conducted by the arborist during the reporting period. Most recommended actions have been performed by the Contractor as advised in the reporting period.

Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. 3,041.52 tonnes of inert C&D materials and 819.22 tonnes of non-inert C&D materials were generated during the reporting period. The non-inert C&D materials and general refuse generated from the Project were disposed of at the SENT Landfill. 21,740 kg of metal and 68 kg of paper/cardboard packaging were produced and sent to recyclers for recycling. No plastics waste was generated during the reporting period. No chemical waste was produced during the reporting period.

Environmental Site Inspection

Three joint environmental site inspections were carried out by the representatives of the Contractor, the IEC and the ET during the reporting period. The Contractor has generally implemented the mitigation measures as recommended.

Environmental Exceedance/Non-conformance/Compliant/Summons and Prosecution

No exceedance of the Action or Limit Level of construction noise was recorded at designated monitoring stations during the reporting period.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

No enquiry was received during the reporting period.

No non-compliance event was recorded during the reporting period.

No complaint was received during the reporting period.

No summons/prosecution was received in this reporting period.

1 INTRODUCTION

ERM-Hong Kong, Limited (ERM) was appointed by the Jockey Club CPS Limited (the CPS Ltd) as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the **Central Police Station Conservation and Revitalisation Project** (the Project).

1.1 Purpose of the Report

This is the thirteenth quarterly EM&A summary report, which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from 1 November 2014 and 31 January 2015.

1.2 STRUCTURE OF THE REPORT

The structure of the report is as follows:

Section 1: **Introduction**

details the scope and structure of the report.

Section 2: **Project Information**

summarises background and scope of the Project, site description, project organization and contract details, construction programme, the construction works undertaken and the status of Environmental Permit(s)/License(s) during the reporting period.

Section 3: Environmental Monitoring Requirements

summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event/Action Plans, environmental mitigation measures as recommended in the EIA report, and relevant environmental requirements.

Section 4: Implementation Status on Environmental Mitigation Measures

summarises the implementation of environmental protection measures during the reporting period.

Section 5 : **Monitoring Results**

summarises the monitoring and waste management results obtained in the reporting period.

Section 6: **Environmental Site Inspection**

summarises the audit findings of the monthly site inspections undertaken within the reporting period.

Section 7: **Environmental Non-conformance** summarises any monitoring exceedance, environmental complaints and environmental summons received within the reporting period.

Section 8: **Review of the EM&A Data and EIA Predictions** compares the monitoring data and waste quantity against predictions in the approved Project EIA report.

Section 9: Conclusions

2 PROJECT INFORMATION

2.1 BACKGROUND

The Chief Executive (CE)'s 2007-2008 Policy Address highlighted revitalisation as the guiding principle of heritage conservation and the Project was among one of the specific proposals put forward by the CE in the same Policy Address. At the meeting of the Executive Council (ExCo) on 15 July 2008, the ExCo advised and the CE ordered that Government should enter into a partnership with the Hong Kong Jockey Club (HKJC) in the form of an agreement (or agreements) to take forward the conservation and revitalisation of the CPS project based on various guiding parameters. The Project is now being undertaken in partnership with the Development Bureau of the HKSAR Government. The HKJC has taken on board the decision at the ExCo meeting and further investigated the design and implementation of the Project. The Project is now implemented by the CPS Limited.

2.2 SITE DESCRIPTION

The location of the Project Site is shown in *Annex A1*. The Site is bounded by Hollywood Road to the north, Arbuthnot Road to the east, Chancery Lane to the south and Old Bailey Street to the west.

The Site comprises three Declared Monuments designated under the *Antiquities and Monuments Ordinance* in 1995. They are:

- Central Police Station;
- Former Central Magistracy; and
- Victoria Prison Compound.

They are collectively named the Central Police Station (CPS). *Annex A2* shows the location of the Declared Monuments within CPS and the buildings within the CPS.

2.3 CONSTRUCTION ACTIVITIES

A summary of the major construction activities undertaken in this reporting period is shown in *Table 2.1* and illustrated in *Annex A3*.

Table 2.1 Summary of Construction Activities undertaken in this Reporting Period

Construction Activities Undertaken

November 2014:

- Structural addition and alteration works at Blocks 2, 3, 4, 9, 10, 11, 13 and 17;
- Underpinning at Blocks 4 and 6;
- Excavation at Block 17;
- Roof repair works at Blocks 8, 9, 10, 19 and link bridge between Blocks 3 and 9;
- Demolition works at Blocks 3, 4, 9 and 14;
- New RC structure construction at Blocks 3 and 9;
- Construction of new roof at Block 14;
- Demolition of concrete block at Block 8;
- Conceal conduit construction and E&M installation at Blocks 1, 2, 6 and 7;
- E&M opening at Blocks 1, 6 and 7;
- Underground drainage at Block 2;
- Builders work in basement plant room;
- Timber doors and windows repair works at Blocks 1 and 3;
- Paint stripping and plaster works at Blocks 1, 3, 6, 7, 11, 14 and 15;
- Façade works at Blocks 3, 4, 6, 7, 8, 10 and 14;
- Structural timber floor repair at Blocks 6 and 7;
- New balcony construction at Block 6;
- Balcony repair at Blocks 6, 7 and 8;
- Underpinning at Zone L2;
- Excavation of M3;
- Construction of site wide terminal manhole at Zone M5;
- Arbuthnot Road West works;
- Excavation works for HEC power cable laying at Old Bailey Street east;
- Final reinstatement of traffic island at junction between Arbuthnot Road East and Wyndham Street;
- Core wall construction at Arbuthnot Wing;
- Basement construction at Old Bailey Wing; and
- R22, R24, R54, R174 and R177 upgrading.

December 2014:

- Structural repair works at Blocks 11, 12 and 17;
- Underpinning at Blocks 3, 4, 6 and 7;
- Roof repair works at Blocks 4, 8, 19 and link bridge between Blocks 3 and 9;
- Demolition works at Blocks 3 and 9;
- New RC structure construction at Blocks 2, 3, 4, 9, 10, 13 and 14;
- Paint stripping and plaster repair at Blocks 2, 3, 6, 7, 8, 11, 14 and 15;
- E&M installation and Builders work in basement plant room;
- Timber doors and windows repair works at Blocks 2, 3 and 8;
- Transformer delivery and installation in Block 8;
- E&M installation at Blocks 1, 7 and 8;
- Structural timber floor repair at Blocks 3, 6, 7, and 14;
- Façade works at Blocks 2, 3, 4, 8, 9, 10, 11, 12, 14, 15 and 17;
- New balcony construction at Block 6;
- Balcony repair at Blocks 8 and 9;
- Metal works repair at Block 15;
- Underground drainage at Blocks 3 and 7;
- Service trench and draw pit construction at Zone L2;
- Construction of site wide terminal manhole at Zone M5;
- Old Bailey Street works;
- Core wall structure construction at Arbuthnot Wing;
- Basement construction at Old Bailey Wing; and
- R19, R22 and R24 upgrading.

January 2015:

- Structural addition and alteration works at Blocks 2, 3, 6, 9, 10, 11, 13, 14 and 17;
- Roof repair works at Blocks 8 and 19;
- Balcony repair at Blocks 8, 9 and 10;
- Paint stripping and plaster repair at Blocks 1, 2, 3, 11, 14 and 15;
- Timber doors and windows repair works at Blocks 2, 3, 4, 9 and 14;
- Structural timber floor repair at Blocks 3, 6 and 14;
- Metal works repair at Blocks 3, 11 and 13;
- Façade works at Blocks 3, 4, 8, 9, 10, 12, 14 and 15;
- Arbuthnot Wing structure construction;
- Old Bailey Wing structure construction;
- E&M opening at Blocks 3, 10, 11, 12 and 14;
- E&M installation at Blocks 1, 7, 8 and basement plant room;
- Underground drainage at Blocks 3, 7 and 14;
- R19, R22 and R24 upgrading;
- Site wide underground services L2, L5 and M5; and
- Road works at Old Bailey Street.

2.4 CONSTRUCTION PROGRAMME

The most updated construction programme for the Project is presented in *Annex I*.

2.5 PROJECT ORGANISATION AND MANAGEMENT STRUCTURE

The Project organization chart, hotline number and contact details are shown in *Annex B*.

2.6 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since the granting of the EP in April 2011 is presented in *Table 2.2*.

Table 2.2 Summary of Environmental Licensing, Notification and Permit Status

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Environmental Permit (EP)	EP-408/2011	-	Superseded on 10 January 2012
	EP-408/2011/A	-	Superseded on 22 March 2012
	EP-408/2011/B	Throughout the Contract	Permit granted on 22 March 2012
Notification of Construction Works as required under <i>Air</i> <i>Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i>	Ref. No. 332920	Throughout the Contract	-
Registration of Waste Producer under <i>Waste</i> <i>Disposal Ordinance</i>	Waste Producer No.: 5213-122-G2347-25	Throughout the Contract	-
Effluent Discharge License under Water Pollution Control Ordinance	License No. WT00010633-2011	21 Oct 2011 – 31 Oct 2016	_
Notification of Commencement of Asbestos Abatement Work under Air Pollution Control Ordinance	-	Throughout the Contract	EPD's letter (EPD's ref.: (5) in EPAC/A/4/000/23 3 II) dated 2 December 2011 satisfied that the content of the asbestos abatement plan (Report No.: 0210/11/ED/0078A) is in accordance with the APCO
Approval of Asbestos Abatement Work (Phase 2)	-	Earliest commencement date on 26 January 2012	EPD's letter (EPD's ref:() in EPAC/A/4/000/23 3) dated 18 January 2012.
Construction Noise Permit (CNP)	GW-RS0734-12	11 July 2012 at 0200 hours to 2 August 2012 at	Expired.

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
110411441011		0400 hours	
	GW-RS0839-12	13 August 2012 at 1900 hours to 31 December 2012 at 0700 hours	Expired.
	GW-RS1162-12	1 December 2012 at 0000 hours to 28 March 2013 at 0600 hours	Expired.
	GW-RS0113-13	1 February 2013 at 0200 hours to 31 May 2013 at 0400 hours	Expired.
	GW-RS1301-12	2 January 2013 at 1900 hours to 29 June 2013 at 2300 hours	Expired.
	GW-RS0084-13	24 January 2013 at 1900 hours to 29 June 2013 at 0700 hours	Expired.
	GW-RS0638-13	16 June 2013 at 0700 hours to 15 September 2013 at 1900 hours	Expired.
	GW-RS0901-13	14 August 2013 at 0000 hours to 31 October 2013 at 0600 hours	Expired.
	GW-RS0714-13	29 June 2013 at 1900 hours to 28 December 2013 at 2400 hours	Expired.
	GW-RS0745-13	5 July 2013 at 1900 hours to 30 December 2013 at 2300 hours	Expired.
	GW-RS1110-13	7 October 2013 at 0200 hours to 31 December 2013 at 0400 hours	Expired.
	GW-RS1205-13	4 November 2013 at 0000 hours to 30 January 2014 at 2400 hours	Expired.
	GW-RS1275-13	13 November 2013 at 0000 hours to 30 April 2014 at 2400 hours	Expired.
	GW-RS1461-13	29 December 2013 at 0000 hours to 28 June 2014 at 2400 hours.	Expired.
	GW-RS0062-14	10 February 2014	Expired.

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
		at 0000 hours to 31 March 2014 at 2400 hours.	
	GW-RS0271-14	1 April 2014 at 0100 hours to 30 June 2014 at 0600 hours	Expired.
	GW-RS0434-14	8 May 2014 at 0000 hours to 30 September 2014 at 2400 hours	Expired.
	GW-RS0651-14	28 July 2014 at 0000 hours to 26 September 2014 at 2400 hours	Expired.
	GW-RS0658-14	29 June 2014 at 0000 hours to 28 December 2014 at 2400 hours	Expired.
	GW-RS0749-14	1 August 2014 at 0000 hours to 31 January 2015 at 2400 hours	Expired.
	GW-RS0918-14	29 September 2014 at 0000 hours to 31 December 2014 at 2400 hours	Expired.
	GW-RS0086-15	1 February 2015 at 0000 hours to 30 June 2015 at 2400 hours	-

3

3.1 Noise Monitoring

3.1.1 Monitoring Location

The construction noise monitoring locations are given in *Table 3.1* and shown in *Annex C*.

 Table 3.1
 Construction Phase Noise Monitoring Locations

Monitoring Location	Proposed Construction Noise Monitoring Station			
	ID in EM&A Manual	ID	Type of Measurement	Remark
Rooftop of Ho Fook Building	N2	NM2	Façade	-
Rooftop of Chancery Mansion		NM6	Façade	Accesses to the original proposed monitoring location in the EM&A Manual, Chancery House (N5), were rejected; alternative location of Chancery Mansion (N6), were therefore proposed and approved by the Authorised Person (AP), the Independent Environmental Checker (IEC) and EPD.

The noise sensitive receivers are also shown in *Annex C*.

3.1.2 Monitoring Parameters, Frequency and Programme

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. The monitoring programme for this reporting period is shown in *Annex D*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level ($L_{\rm eq}$) in decibels dB(A). $L_{\rm eq\,(30min)}$ were used as the monitoring parameter for the time period in between 0700 – 1900 hours on normal weekdays. Supplementary information for data auditing, two statistical sound levels L_{10} and L_{90} ; the levels exceeded for 10 and 90 percent of the time respectively, were also recorded during the monitoring for reference. The measured noise levels were logged in every 5 minutes throughout the impact monitoring period.

3.1.3 Monitoring Equipment and Methodology

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures* of *Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM)* issued under the *Noise Control Ordinance (NCO)* (Cap 400).

The sound level meters and calibrator used for the noise measurement, as listed in *Table 3.2*, complies with IEC 651: 1979 and 804:1985 (Type 1) specification. The calibration certificates of the sound level meters are included in *Annex E*.

Table 3.2 Noise Monitoring Equipment

Monitoring Stations	Monitoring Equipment (Sound Level Meter and Calibrator)
NM2, NM6	Calibrator
	Rion NC-73 (S/N 10486660; S/N 10786708)
	CEL 120 (S/N 3421612)
	Sound Level Meter
	Rion NL-52 (S/N 00131627)
	CEL 633A (S/N 3521757)

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

Measurements were accepted as the calibration level from before and after the noise measurement agree to within 1.0 dB.

3.1.4 Event / Action Plan

Table 3.3 Action and Limit Levels for Construction Noise Monitoring

Noise Monitoring Location	Action Level	Limit Level, L _{eq(30mins), dB(A)}	Remark
NM2, NM6	When one documented complaint is received from any one of the sensitive receivers	75 (note)	Applicable during 0700 – 1900 hours on normal weekdays.

Notes:

- a) Acceptable Noise Levels for Area Sensitivity Rating of A/B/C. Limit Level is reduced to 70dB(A) for schools and 65dB(A) during school examination periods.
- b) If works are to be carried out during restricted hours, the conditions stipulated in the CNP issued by the NCA have to be followed.

The Event / Action Plan (EAP) for noise monitoring is presented in *Annex F*.

3.1.5 Mitigation Measures

The mitigation measures in accordance with the EP, EIA and EM&A Manual and their implementation status are presented in *Annex G*.

3.2 CULTURAL HERITAGE

3.2.1 Vibration Monitoring

In accordance with the EM&A Manual, vibration monitoring is required and the vibration control limits and vibration monitoring proposal are defined by a specialist for AMO's approval.

Baseline Monitoring

A set of initial readings should be recorded prior to commencement of each stage of demolition works or trial piling works. The baseline vibration monitoring should be conducted for duration of 5 minutes on the measurement day(s) at each vibration monitoring location.

Vibration Monitoring for Demolition Works

There are five phases/stages of vibration monitoring to be carried out for demolition works, namely Initial Reading Phase, Monitoring Stage 1, Monitoring Stage 2, Monitoring Stage 3 and Monitoring Stage 4. The monitoring location is shown in *Annex L*. The vibration monitoring should be conducted for duration of 5 minutes on the days with demolition works at each vibration monitoring location.

Vibration Monitoring for Trial Piling and Pipe/Bored Piling Works

Vibration monitoring for trial piling works and pipe/bored piling works is required. The monitoring location is shown in *Annex L*. The vibration monitoring should be conducted for duration of 5 minutes on the days with trial piling works or pipe/bored piling works at each vibration monitoring location.

Vibration Monitoring for Other Construction Works

Vibration monitoring for specific construction works other than demolition works, trial piling works and pipe/bored piling works is also required in accordance with Building Department's requirement. The monitoring location is shown in *Annex M*. The number and location of monitoring location will depend on the location of the specific construction works. The vibration monitoring should be conducted for duration of 5 minutes on a daily basis (working day) at each vibration monitoring location.

Alert, Alarm and Action Levels

The Alert, Alarm and Action (AAA) Levels are to be implemented during the vibration monitoring and shown in *Table 3.4*.

Table 3.4 Alert, Alarm and Action (AAA) Levels for Vibration Monitoring

Instrument Type	Item Monitored	Alert Level	Alarm Level	Action Level
Vibration Monitoring	Horizontal Movement	2.0 mm/s	2.5 mm/s	3.0 mm/s

The Event / Action Plan (EAP) for vibration monitoring is shown in *Table 3.5*.

Table 3.5 Event and Action Plan for Vibration Monitoring

Events	Action
Exceedance of Alert Level	Notify Management Contractor
Exceedance of Alarm Level	Notify Authorised Person/Resident Engineer
Exceedance of Action Level	Cease Works and submit mitigation

3.2.2 Mitigation Measures

Cultural heritage mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

3.3 LANDSCAPE AND VISUAL MONITORING

In accordance with the EM&A Manual, inspections of affected trees were conducted by an experienced and appropriately trained arborist. All irregularities that deviate from the recommended tree protection measures or could impose deleterious impacts on the protected trees were reported. Besides, implementation of mitigation measures for landscape and visual resources recommended in the EIA Report were also monitored during the site inspection.

3.3.1 Mitigation Measures

Landscape and visual mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

3.4 ENVIRONMENTAL REQUIREMENTS IN CONTRACT DOCUMENTS

The environmental requirements as specified in the contract documents were reviewed and were covered in the EIA's requirements.

4 IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES

The Contractor has generally implemented the environmental mitigation measures (including those for archaeology) and requirements as stated in the EIA Report, EM&A Manual, EP and the contract documents. The implementation status during the reporting period is summarised in *Annex G*.

Status of required submissions under the EP during the reporting period is presented in *Table 4.1*.

Table 4.1 Status of Required Submissions

Submission		Submission Date
EP Condition		
Conditions 3.4	Thirty-sixth Monthly EM&A Report	14 November 2014
	Thirty-seventh Monthly EM&A Report	15 December 2014
	Thirty-eighth Monthly EM&A Report	14 January 2015

5.1 Noise

A total of 16 sets of 30-minute construction noise measurements were carried out at each monitoring station, NM2 and NM6, during normal weekdays of the reporting period. The monitoring results together with graphical presentations are presented in *Annex H*. The local impacts observed near the monitoring stations of NM2 and NM6 were summarised below:

- NM2: construction noise from activities in the Project Site and traffic noise from Old Bailey Street.
- NM6: construction noise from activities in the Project Site and traffic noise from Chancery Lane.

No exceedance of the Action or Limit Level of construction noise was recorded during the reporting period.

5.2 LANDSCAPE AND VISUAL MONITORING

Three monthly tree inspections were conducted by the arborist during the reporting period on 4 November 2014, 4 December 2014 and 5 January 2015 and key findings and recommendations are summarised in *Table 5.1*.

Table 5.1 Findings of Monthly Tree Inspections in the Reporting Period

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observation / Recommendations
4 Novembe	r 2014		
Tree -5	Mangifera indica	Fair	No further action required.
Tree -6	Aleurites moluccana	Fair	No further action required.
Tree-7	Aleurites moluccana	Fair	No further action required.
Tree-8	Plumeria rubra	Fair	No further action required.
Tree-9	Araucaria cunninghamia	Fair	No further action required.
Tree-11	Dracaena marginata	Fair	No further action required.
4 December	· 2014		
Tree -5	Mangifera indica	Fair	• No further action required.
Tree -6	Aleurites moluccana	Fair	No further action required.
Tree-7	Aleurites moluccana	Fair	No further action required.
Tree-8	Plumeria rubra	Fair	No further action required.
Tree-9	Araucaria cunninghamia	Fair	No further action required.
Tree-11	Dracaena marginata	Fair	No further action required.
5 January 2	2015		
Tree -5	Mangifera indica	Fair	 Renovation works were being carried out near the tree. Some white paint due

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observation / Recommendations	
			to nearby renovation works was observed on some leaves of the tree. The Contractor was reminded that the tree should be well protected from nearby construction works at all times.	
Tree -6	Aleurites moluccana	Fair	No further action required	
Tree-7	Aleurites moluccana	Fair	No further action required	
Tree-8	Plumeria rubra	Fair	No further action required	
Tree-9	Araucaria cunninghamia	Fair	No further action required	
Tree-11	Dracaena marginata	Poor	 Withered leaves were observed on the tree; 	
			To keep close monitoring on the growth of the tree.	

Follow-up actions needed to be implemented were recommended to the Contractor and the status of the follow-up actions was reviewed during the subsequent monthly site inspections. Recommendations have generally been implemented by the Contractor during the reporting period.

5.3 CULTURAL HERITAGE

5.3.1 Vibration Monitoring

Trial Piling and Piling works

Vibration monitoring carried out for the trial piling and piling works during the reporting period are listed below:

November 2014:

- 25 vibration monitoring measurements for the basement construction at Parade Ground;
- 25 vibration monitoring measurements at Block 8;
- 25 vibration monitoring measurements for piling works at Old Bailey Wing (Block 50);
- 25 vibration monitoring measurements for piling works at Block 51; and
- 25 vibration monitoring measurements at Block 17.

December 2014:

- 25 vibration monitoring measurements for the basement construction at Parade Ground;
- 25 vibration monitoring measurements at Block 8;

- 25 vibration monitoring measurements at Old Bailey Wing (Block 50);
- 25 vibration monitoring measurements at Block 51; and
- 25 vibration monitoring measurements at Block 17.

January 2015:

- 26 vibration monitoring measurements for the basement construction at Parade Ground;
- 26 vibration monitoring measurements at Block 8;
- 26 vibration monitoring measurements at Old Bailey Wing (Block 50);
- 26 vibration monitoring measurements at Block 51; and
- 26 vibration monitoring measurements at Block 17.

The monitoring results are presented in *Annex L*.

Other Construction Works

Vibration monitoring carried out for other construction works during the reporting period are listed below:

November 2014:

- 25 vibration monitoring measurements for the structural addition and alteration works at Block 1;
- 25 vibration monitoring measurements for the structural addition and alteration works at Block 14; and
- 25 vibration monitoring measurements for the structural addition and alteration works at Block 11.

December 2014:

- 25 vibration monitoring measurements for the structural addition and alteration works at Block 1;
- 25 vibration monitoring measurements for the structural addition and alteration works at Block 14; and
- 25 vibration monitoring measurements for the structural addition and alteration works at Block 11.

January 2015:

• 26 vibration monitoring measurements for the structural addition and alteration works at Block 1;

- 26 vibration monitoring measurements for the structural addition and alteration works at Block 14; and
- 26 vibration monitoring measurements for the structural addition and alteration works at Block 11.

The monitoring results are presented in *Annex M*.

All monitoring results were below the Alert/Alarm/ Action Levels during the reporting period.

5.3.2 Heritage Site Audit

Heritage site audits were conducted on 3-7, 10-14, 17-21 and 24-27 November 2014; 1-5, 8-12, 15-20 and 29-31 December 2014; 2, 5-9, 12-16, 19-23 and 26-30 January 2015 by the Heritage Checker during the reporting period. Follow-up actions were undertaken as reported by the Contractor and observed in the subsequent monthly site inspections conducted in the reporting period. Key site audit findings and recommendations are summarised below.

3 November 2014

 It was observed that the historic painted sign and facing brickwork had been damaged by concrete pouring down from the first floor window.
 The Contractor was informed to follow up.

6 November 2014

- It was observed that the painted sign to Block 4 south elevation had been sprayed with red paint. The painted sign should be protected and the Contractor was informed to follow up.
- It was observed that the existing infill brickwork to Block 4 windows and doors were not supported after the removal of the window and door frames. The Contractor was informed to follow up.

25 November 2014

 Cigarette ends were observed on first floor of Block 2. The Contractor was reminded to remove the cigarette ends and that smoking is not allowed in buildings.

3 December 2014

• It was observed that the brick infills to Block 1 light well timber louvre locations were not carried out in accordance with the contract documents. The Contractor was informed to follow up.

8 December 2014

 It was observed that some new openings in Block 3 did not have adequate end bearing supporting for lintels. The Contractor was informed to follow up.

10 December 2014

• Debris and cigarette ends were found in Block 9. The Contractor was reminded to remove the cigarette ends and that smoking is not allowed in buildings.

16 December 2014

It was observed that the Block 8 west scaffold was built by fixing into the
existing facing brickwork wall, causing damage to the historic fabric.
The Contractor was informed to rectify.

12 January 2015

• Improvement is required for the window putty application, metal work brackets, bolts, protection and grouting workmanship in general. The Contractor was informed to follow up.

21 January 2015

• It was observed that the works package contractor was painting the interior brickwork in Block 1 when instructed not to do so. The Contractor was informed to follow up.

23 January 2015

• It was observed that the ceiling was being decorated without rectifying all the repair defects. The Contractor was informed to follow up.

27 January 2015

- It was observed that the finish of tiling was very irregular and did not comply with the specifications. The Contractor was informed to follow up.
- It was observed that the sunken slabs to Block 9 first floor were filled with water. The Contractor was reminded to remove the stagnant water.

29 January 2015

• It was observed that the surface finish to new handrail of Block 1 did not comply with contract documents. The Contractor was informed to rectify.

30 January 2015

• The new base plate fixings to Block 1 Staircase 02 new balustrades were observed to be using a different type of bolt which did not comply with contract document. The Contractor was informed to rectify.

A summary of the current condition of character defining elements, historic buildings and structures is contained in *Annex N*.

5.4 WASTE MANAGEMENT

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. Non-inert C&D materials were made up of wastes such as general refuse. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarised in *Table 5.2*. The summary of Waste Flow Table prepared by the Contractor is shown in *Annex J*. The non-inert C&D materials and general refuse generated from the Project were disposed of at the SENT Landfill. 21,740 kg of metal and 68 kg of paper/cardboard packaging were produced and sent to recyclers for recycling. No plastics waste was generated during the reporting period. No chemical waste was produced during the reporting period.

Table 5.2 Quantities of Waste Generated from the Project

Month / Year	Quantity						
	C&D	C&D	Chemical		Recycled materials		s
	Materials	Materials	Waste				
	(inert)	(non-inert)	Liquid	Solid	Paper/	Plastics	Metals
	(tonnes) (a)	(tonnes) (b)	(L)	(kg)	cardboard (kg)	(kg)	(kg)
November 2014	1,249.55	336.57	0	0	0	0	6,660
December 2014	1,177.63	260.33	0	0	68	0	12,080
January 2015	614.34	222.32	0	0	0	0	3,000
Total	3,041.52	819.22	0	0	68	0	21,740

Notes:

- (a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil.
- (b) Non-inert C&D materials include wastes such as general refuse which were disposed of at SENT Landfill and recyclable materials are paper, cardboard, plastics and metals. The figure presented under non-inert C&D materials represents quantities of non-recyclable materials. Recycled materials are reported separately.

5.5 EFFECTIVENESS OF MITIGATION MEASURES AND MONITORING

The mitigation measures recommended in the EIA report and required by the EP are considered effective in minimising environmental impacts.

The EM&A for the Project was conducted as scheduled during the reporting period. No non-compliance events were observed during site inspections and no exceedances of limit level were recorded during the reporting period. The EM&A programme is considered effective.

6 ENVIRONMENTAL SITE INSPECTION

Three monthly environmental site inspections were conducted on 17 November 2014, 15 December 2014 and 19 January 2015 during the reporting period. There was no non-compliance recorded during the site inspections. Key site audit findings and recommendations are summarised below. Monthly recommendations and observations were implemented and rectified by the Contractor in the subsequent monthly site inspections.

17 November 2014

• Nil.

15 December 2014

• Chemical waste containers were observed without drip tray near Block 17. The Contractor was reminded to remove the chemical waste containers.

19 January 2015

• Nil.

This page is deliberately left blank

7 ENVIRONMENTAL NON-CONFORMANCE

7.1.1 Summary of Monitoring Exceedance

No exceedance of the Action or Limit Level of construction noise or Alert, Alarm and Action Level of vibration was recorded during the reporting period.

7.1.2 Summary of Enquiry

No enquiry was received during the reporting period.

7.1.3 Summary of Environmental Non-Compliance

No non-compliance event was recorded during the reporting period.

7.1.4 Summary of Environmental Complaint

No complaint was received during the reporting period.

The cumulative number of complaints is presented in *Annex K*.

7.1.5 Summary of Environmental Summons and Successful Prosecution

No summons was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex K*.

This page is deliberately left blank

8.1 NOISE

A comparison was made between the monitoring results in this reporting period and the Noise Standard for general construction works during 0700 – 1900 hrs on normal weekdays (*Table 8.1*).

Table 8.1 Comparison of Construction Noise Standard and Noise Monitoring Results

Reporting Month	Monitoring Stations	Corresponding NSR in EIA	Noise Limit Level	Predicted Construction Noise Level (With Mitigation) in EIA	Measured Construction Noise Level
			L _{eq, 30 min} dB(A)	L _{eq, 30 min} dB(A)	L _{eq, 30 min} dB(A)
Nov 2014	NM2	N2	75	67 - 72	63.8 – 70.1
	NM6	N6	75	73 - 75	64.3 – 69.7
Dec 2014	NM2	N2	75	67 - 72	66.1 – 71.9
	NM6	N6	75	73 - 75	67.1 – 70.6
Jan 2015	NM2	N2	75	67 - 72	64.8 – 71.1
	NM6	N6	75	73 - 75	66.9 – 73.7

The monitoring results recorded since the commencement of the construction works have been below the Limit Level and comparable to the predicted construction noise level in the approved EIA. Recommended mitigation measures in *Section 5.9.1* of EIA will continue to be implemented throughout the construction stage.

8.2 WASTE MANAGEMENT

The estimated amount of waste generated in the approved EIA and the accumulated quantities of waste generated up to this reporting period are presented in *Table 8.2*. The accumulated amount of inert and non-inert C&D materials is higher than the estimated amount in EIA. The major chemical waste generated on site was primarily asbestos which was not estimated in the approved EIA and hence no data is available for comparison. Recommended mitigation measures in *Section 8.5.1* of the EIA will continue to be implemented throughout the construction stage.

Table 8.2 Quantity of Actual Amount of C&D Materials, General Wastes and Chemical Wastes Generated and EIA Estimation

Type of Material	Estimated Amount of Waste in EIA	Accumulated Actual Amount of Waste Recorded (a) (b)
Amount of C&D Materials (Inert) Arising	16,440 m ³	30,069.0 m ³
Amount of C&D Materials (Non-inert) Arising	890 m ³	6,527.6 m ³
General Refuse	130 kg per day	_ (c)
Chemical Waste	Less than 100L per month	57 L (liquid)395 kg (solid)7,000 kg of asbestos generated

Notes:

- (a) The accumulated actual amount of C&D Materials and chemical waste were recorded since the commencement of construction works.
- (b) The volume of waste materials are provided by the Contractor based on the updated waste record in January 2015.
- (c) The amount of general refuse generated was not recorded.

8.3 SUMMARY OF REVIEW

The EIA predictions and the monitoring results since the commencement of construction works have been reviewed. The EIA concluded that the Project would not cause adverse impacts to the environment and the monitoring results have also indicated the same so far. Mitigation measures (including those for archaeology) recommended in the EP, EIA and EM&A Manual were implemented by the Contractor as far as practicable and were considered effective. The recommended mitigation measures will continue to be implemented throughout the construction phase of the Project.

The effectiveness of the monitoring programme has been exhibited therefore change to the programme is not considered to be necessary.

9 CONCLUSIONS

This thirteenth Quarterly EM&A Report presents the EM&A works undertaken during the reporting period from 1 November 2014 to 31 January 2015 in accordance with EM&A Manual and the requirements under EP-408/2011/B.

No exceedance of the Action or Limit Level of construction noise was recorded at designated monitoring stations during the reporting period.

Tree inspections were conducted in this reporting period. Most of the necessary landscape and visual mitigation measures recommended in the EIA Report were implemented by the Contractor.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

No enquiry was received during the reporting period.

No non-compliance event for heritage and environmental site inspections was recorded during the reporting period.

No complaint was received during the reporting period.

No summons/prosecution was received during the reporting period.


The monitoring programme was considered effective in reflecting the environmental conditions at the designated representative sensitive receivers. The monitoring results also indicate that the Project have not caused adverse impacts on the environment with implementation of appropriate mitigation measures. Change to the monitoring programme is not considered to be necessary. The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures in the coming periods.

Annex A

Location of Works Areas and the Surroundings


Annex A1

Project Location

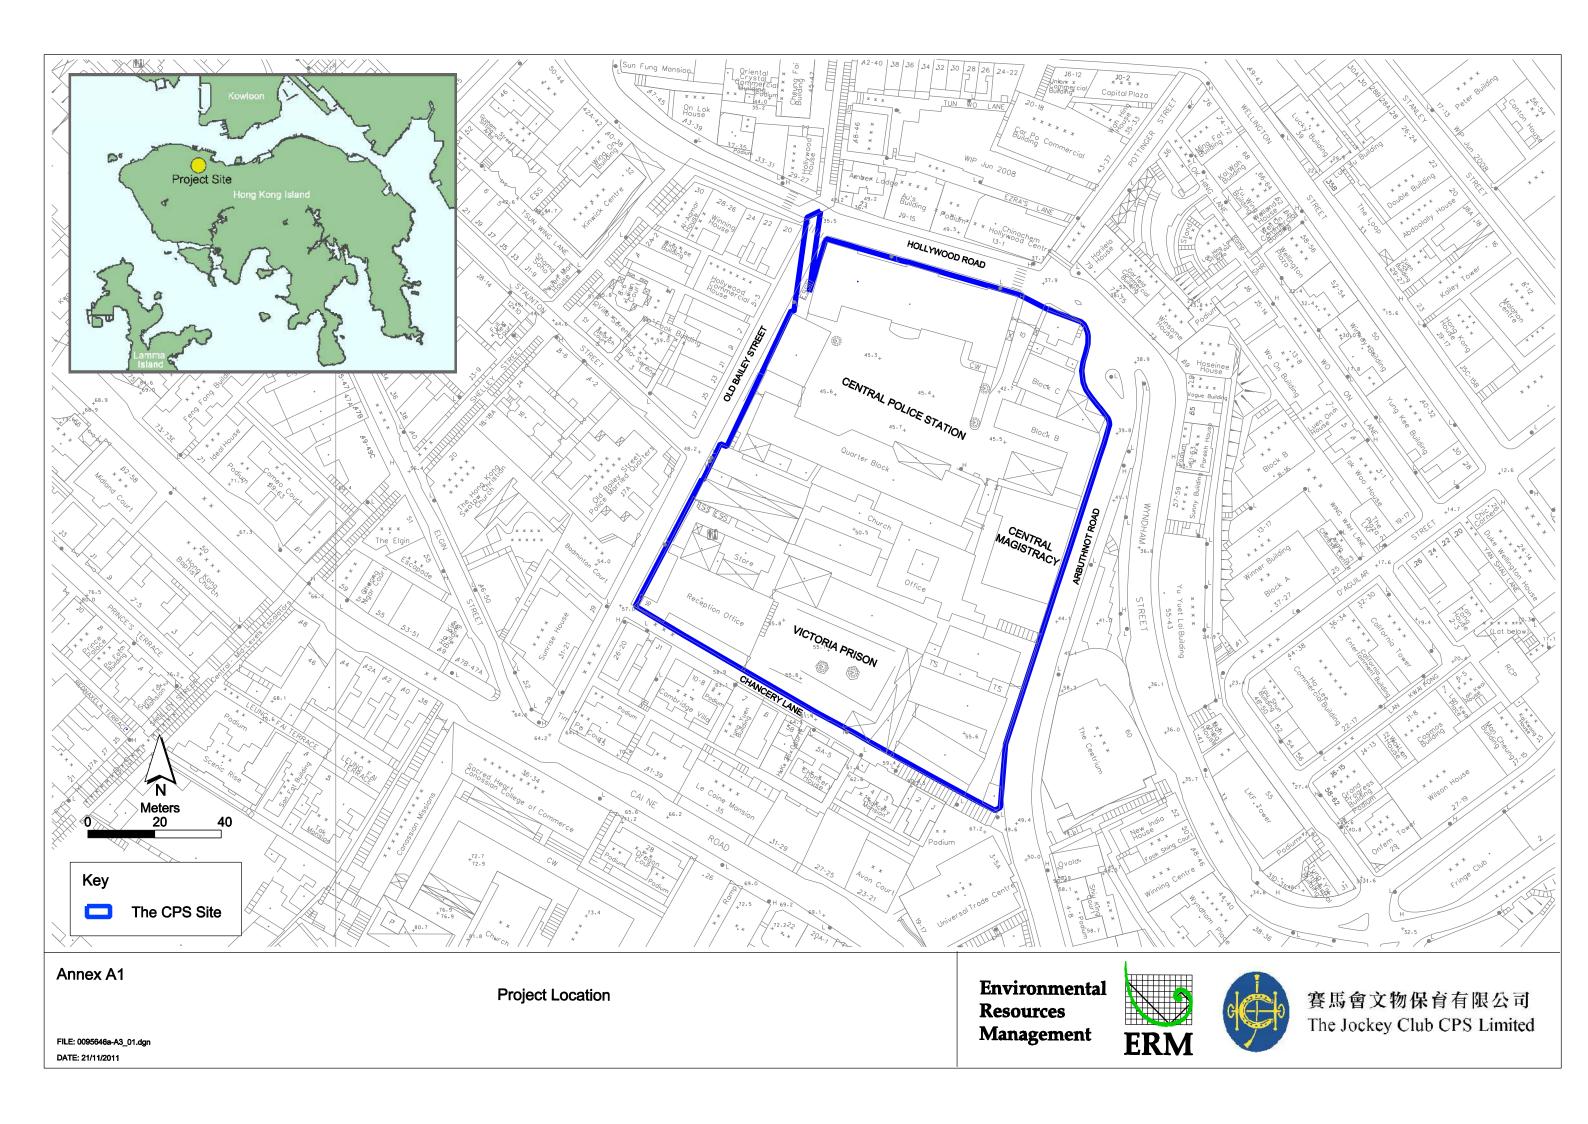

Annex A2

Declared Monuments within the Project Site

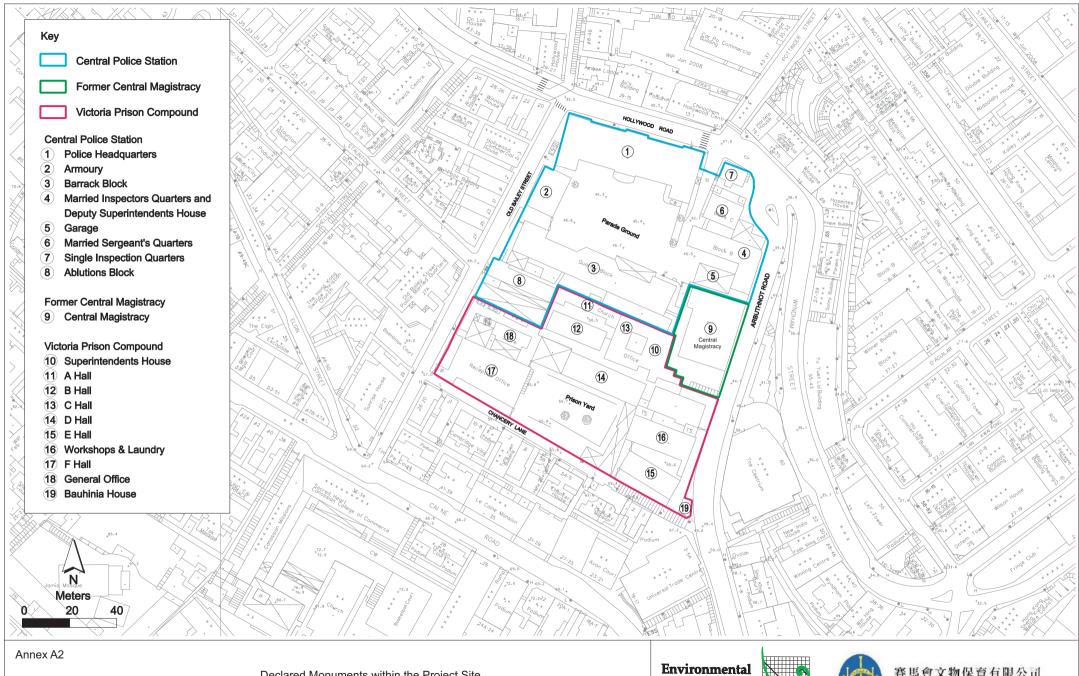

FILE: 0095646b1-A3.dgn DATE: 07/12/2011

Declared Monuments within the Project Site


Resources Management






Annex A3


Site Layout Plan marked with Works

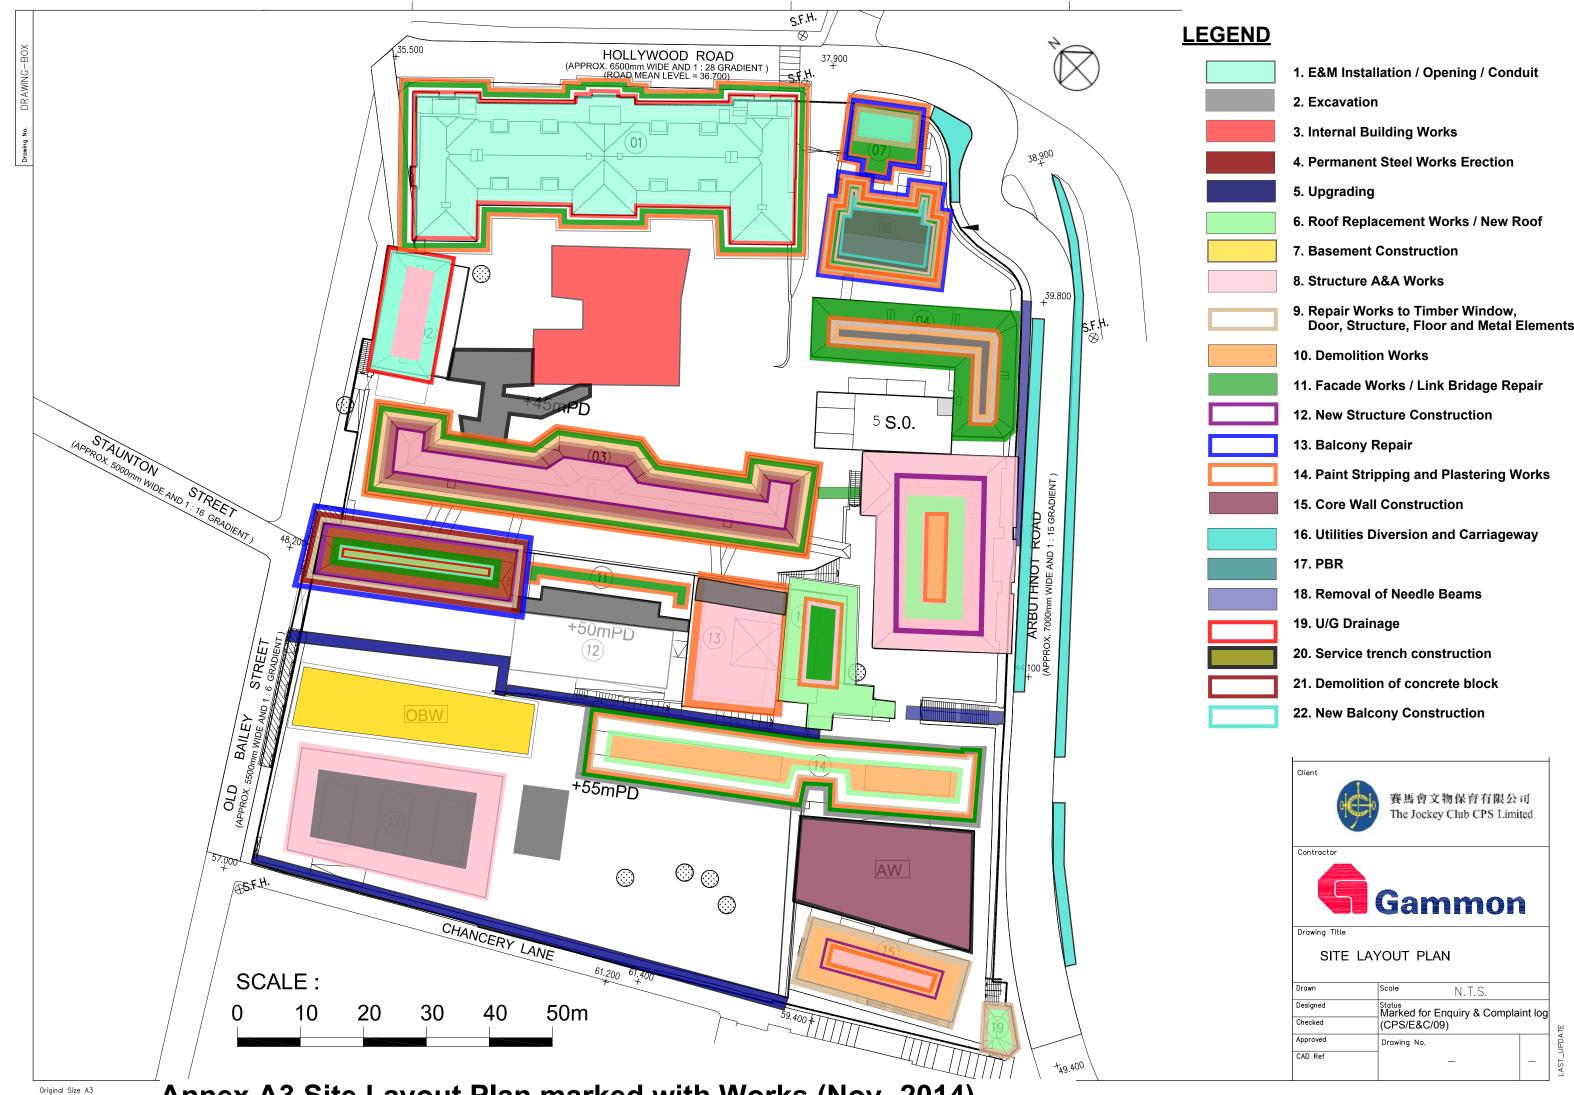

Annex A3 Site Layout Plan marked with Works (Nov- 2014)

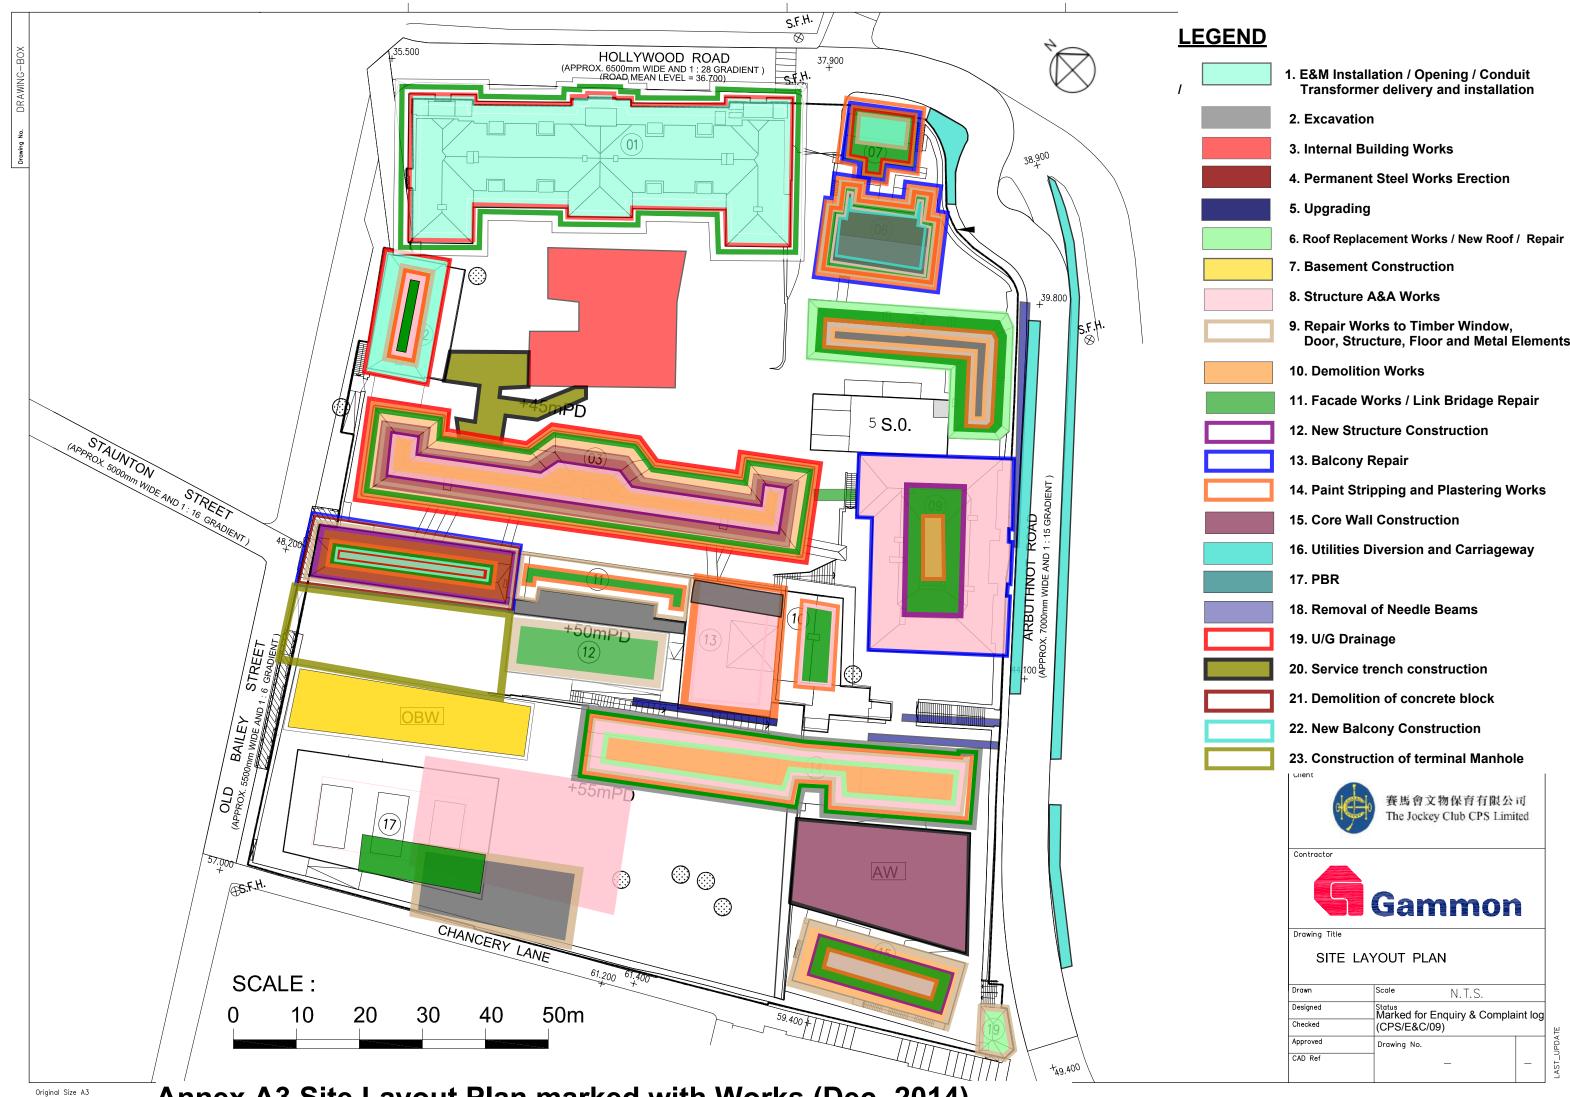


Annex A3 Site Layout Plan marked with Works (Dec- 2014)

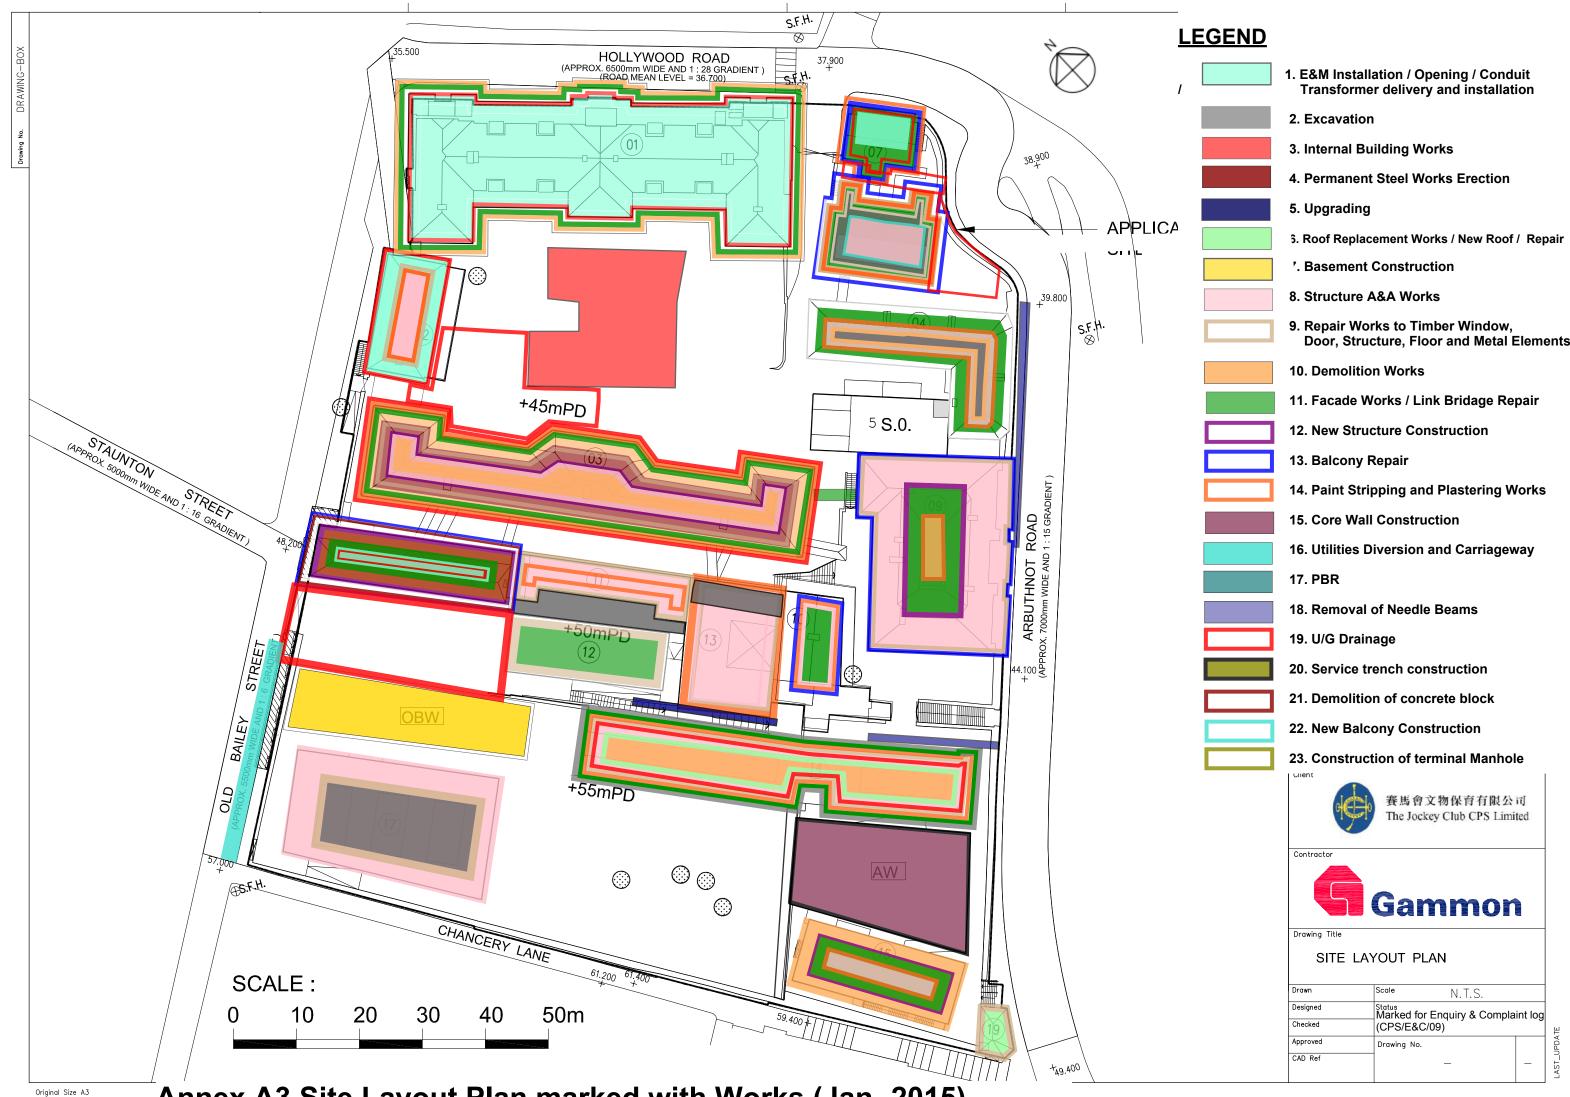

Annex A3 Site Layout Plan marked with Works (Jan- 2015)


Annex B

Project Organization Chart and Contact Detail

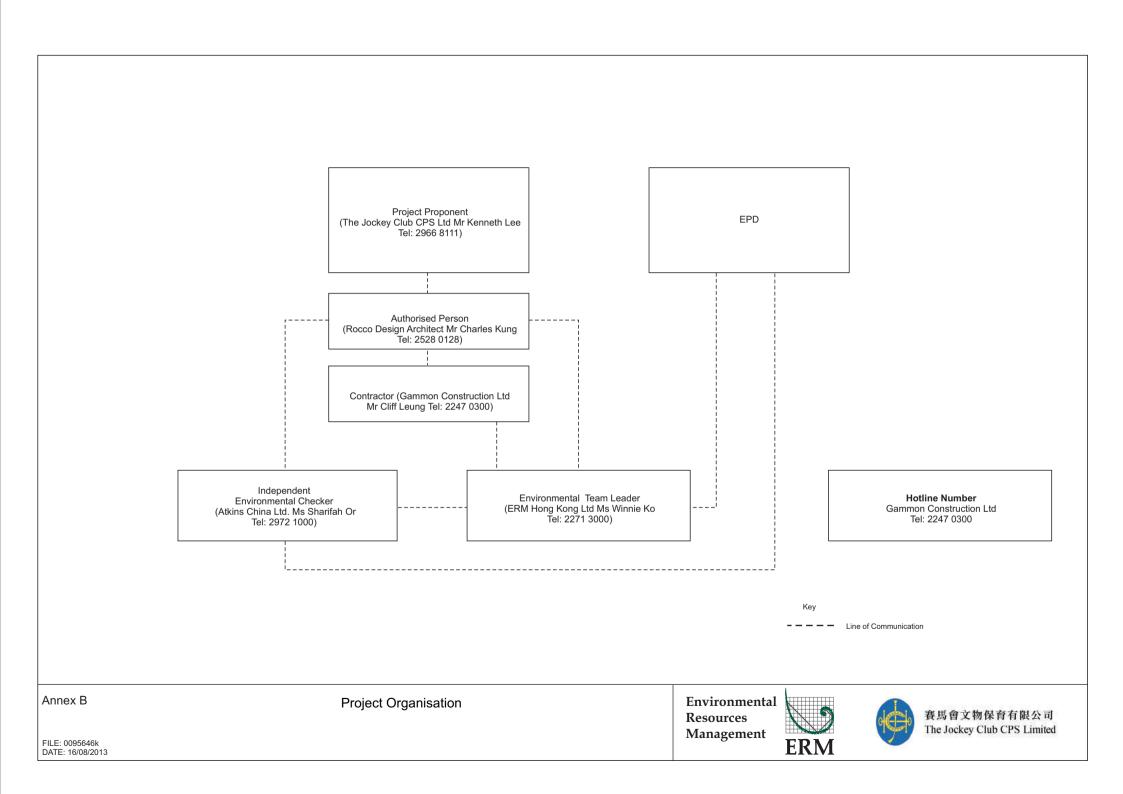

Annex C

Locations of Noise Monitoring Stations and Noise Sensitive Receivers

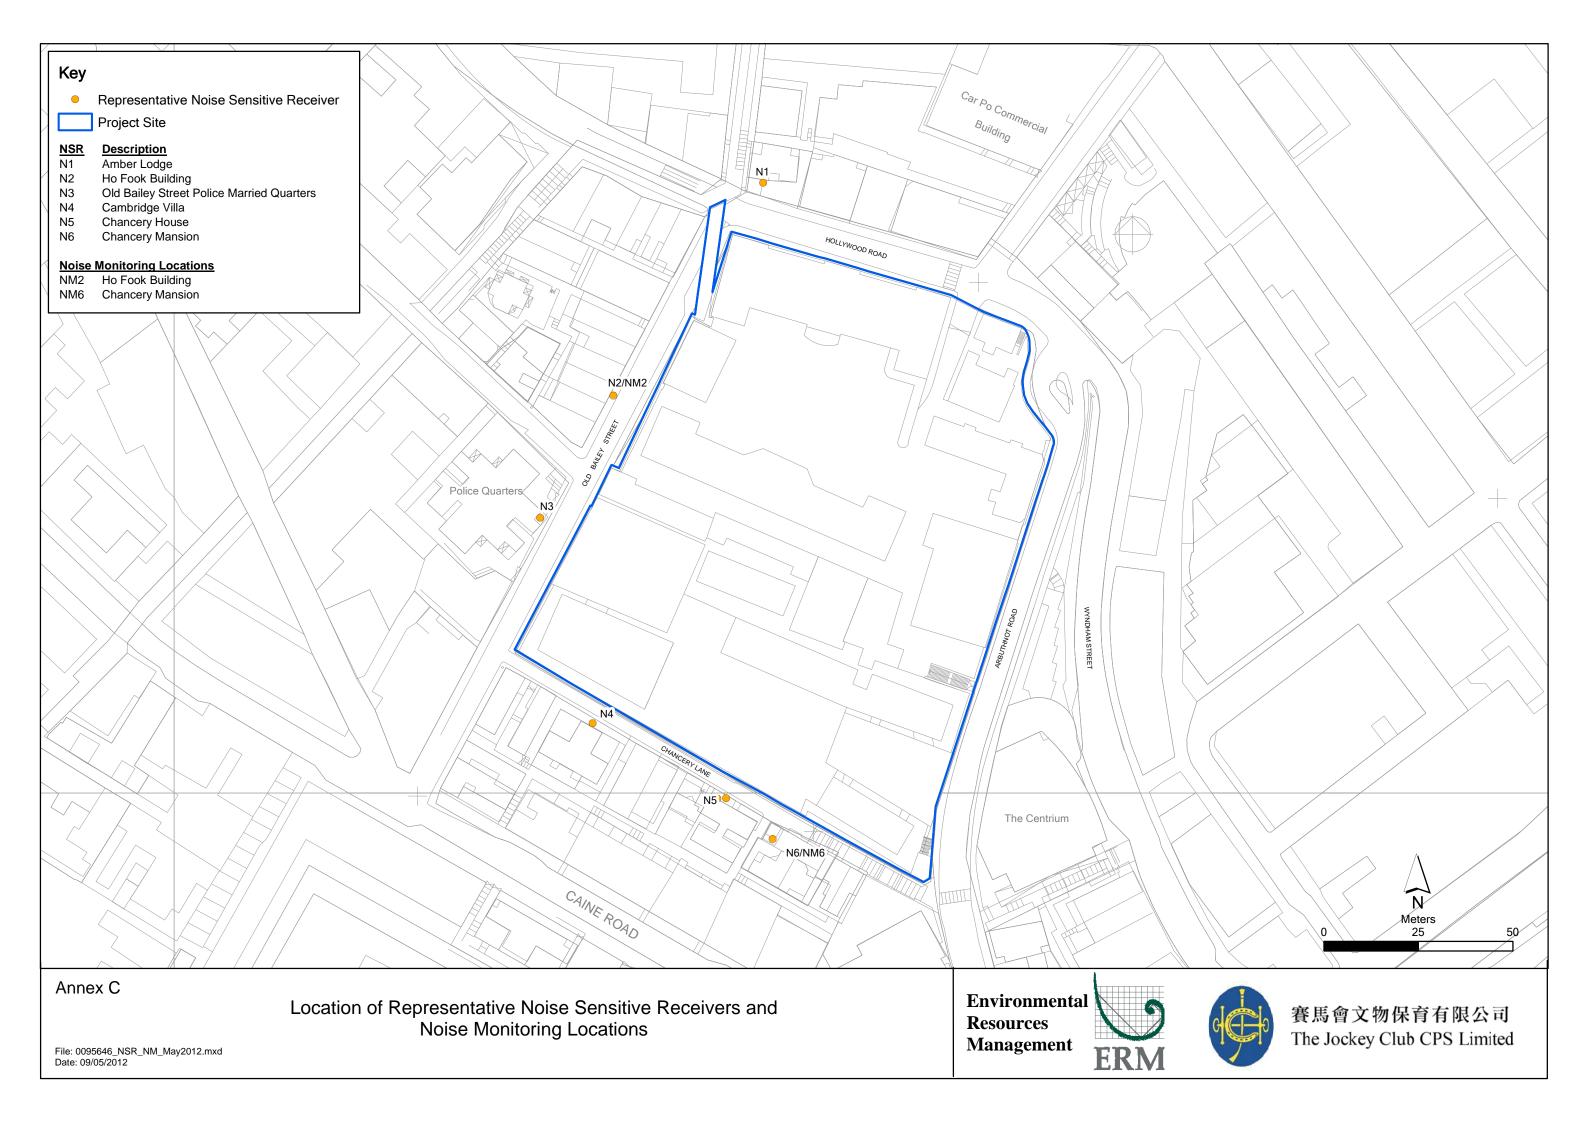

Annex D

Monitoring Schedule of the Reporting Period

Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - November 2014

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						01-Nov
02-Nov	03-Nov	04-Nov	05-Nov	06-Nov	07-Nov	08-Nov
02-1100	03-INOV	04-1100	03-1404	00-1100	07-1100	UO-INUV
				Noise Monitoring at NM2 & NM6		
09-Nov	10-Nov	11-Nov	12-Nov	13-Nov	14-Nov	15-Nov
001101	10 1404	11 1407		10 110	141404	10 1404
			Noise Monitoring at NM2 & NM6			
16-Nov	17-Nov	18-Nov	19-Nov	20-Nov	21-Nov	22-Nov
		Noise Monitoring at NM2 & NM6				
23-Nov	24-Nov	25-Nov	26-Nov	27-Nov	28-Nov	29-Nov
	Noise Monitoring at NM2 & NM6					Noise Monitoring at NM2 & NM6
30-Nov						

Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - December 2014

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	01-Dec	02-Dec	03-Dec	04-Dec	05-Dec	06-Dec
					Noise Monitoring at NM2 & NM6	
07-Dec	08-Dec	09-Dec	10-Dec	11-Dec	12-Dec	13-Dec
				Noise Monitoring at NM2 & NM6		
14-Dec	15-Dec	16-Dec	17-Dec	18-Dec	19-Dec	20-Dec
			Noise Monitoring at NM2 & NM6			
21-Dec	22-Dec	23-Dec	24-Dec	25-Dec	26-Dec	27-Dec
	Noise Monitoring at NM2 & NM6			Public Holiday	Public Holiday	Noise Monitoring at NM2 & NM6
28-Dec	29-Dec	30-Dec	31-Dec			

Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - January 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	j	,	·	01-Jan	02-Jan	03-Jan
					Noise Monitoring at NM2 & NM6	
04-Jan	05-Jan	06-Jan	07-Jan	08-Jan	09-Jan	10-Jan
				Noise Monitoring at NM2 & NM6		
11-Jan	12-Jan	13-Jan	14-Jan	15-Jan	16-Jan	17-Jan
			Noise Monitoring at NM2 & NM6			
18-Jan	19-Jan	20-Jan	21-Jan	22-Jan	23-Jan	24-Jan
		Noise Monitoring at NM2 & NM6				
25-Jan	26-Jan	27-Jan	28-Jan	29-Jan	30-Jan	31-Jan
	Noise Monitoring at NM2 & NM6					Noise Monitoring at NM2 & NM6

Annex E

Calibration Reports for Calibrators and Sound Level Meters



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration

校正證書

Certificate No.:

C137683

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC13-3109)

Description / 儀器名稱

Sound Level Calibrator

Manufacturer / 製造商

Rion

Model No. / 型號 Serial No./編號

NC-73 10486660

Supplied By / 委託者

Envirotech Services Co.

Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,

Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

 $(23 \pm 2)^{\circ}C$

Relative Humidity / 相對濕度 :

 $(55 \pm 20)\%$

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

3 December 2013

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

All results are within manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By 測試

Certified By 核證

Date of Issue

4 December 2013

簽發日期

te test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior

1.證書所載校正用之測試器材均可測源至國際標準。 局部獲印本證書需先獲本實驗所書面批准。

n Creation Engineering Limited - Calibration & Testing Laboratory

香港新界屯門萬安里一號青山灣機樓四樓

7.17世話: 2927 2606 Fax 傳真: 2744 8986



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 松工終事

Certificate No.: C137683

證書編號

校正證書

 The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID CL130 CL281 TST150A Description
Universal Counter
Multifunction Acoustic Calibrator
Measuring Amplifier

Certificate No. C133632 DC130171 C120886

Test procedure : MA100N.

5. Results:

5.1 Sound Level Accuracy

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	93.8	± 0.5	± 0.2

5.2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	0.991	1 kHz + 2 %	+ 1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

S. n Creation Engineering Limited - Calibration & Testing Laboratory

C 4 F. Ising Shan Wan Exchange Building, I Hing On Lune, Tuen Mun, New Territories, Hong Kong

計劃工程有限公司 - 校正及檢測實驗所

。 香港新界屯門舞安里一號青山灣機樓四樓

T. 電話: 2927 2606 Fax 傳真: 2744 8986 E-mail 電郵: eallab a suncreation

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior witten approval of this laboratory.

公園書所載核正用之劃試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書而批准。



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

:

Certificate No.:

C144214

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC14-1719)

Date of Receipt / 收件日期: 9 July 2014

Description / 儀器名稱

Sound Level Calibrator

Manufacturer / 製造商

Rion

Model No. / 型號

NC-73

Serial No./編號

10786708

Supplied By / 委託者

Envirotech Services Co.

Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,

Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(55 \pm 20)\%$

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

15 July 2014

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

All results are within manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By

測試

H C Chan

Engineer

Certified By

核證

Date of Issue

16 July 2014

K K Wong

Engineer

簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, I Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司-校正及檢測實驗所 c/o 香港新昇屯門與安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax/傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C144214

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement
of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID CL130 CL281 TST150A

Description Universal Counter

Multifunction Acoustic Calibrator Measuring Amplifier Certificate No. C143868 DC130171 C141558

4. Test procedure: MA100N.

5. Results:

5.1 Sound Level Accuracy

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value (dB)
Nominal Value	(dB)	(dB)	
94 dB, 1 kHz	93.9	± 0.5	± 0.2

5.2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	0.990	1 kHz ± 2 %	± 1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

Tel/電話: 2927 2606

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited — Calibration & Testing Laboratory c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司—校正及檢測實驗所 c/o 香港新界屯門與安里—號青山灣機樓四樓

Fax/傳真; 2744 8986

E-mail/電郵: callab(a) suncreation.com Website/網址: www.suncreation.com



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C147473

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC14-3079) Date of Receipt / 收件日期: 5 December 2014

Description / 儀器名稱 :

Acoustic Calibrator

Manufacturer / 製造商

Casella

Model No./型號 Serial No./編號

CEL-120/1 3421612

Supplied By / 委託者

Envirotech Services Co.

Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,

Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}$ C Relative Humidity / 相對濕度 :

 $(55 \pm 20)\%$

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST/測試日期

14 December 2014

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

All results are within manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By

測試

Project Engineer

Certified By

核證

KK Wong

Date of Issue 簽發日期

17 December 2014

Engineer

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所

c/o 香港新界屯門興安里一號青山灣機樓四樓

Fax/傳真: 2744 8986 Tel 電話: 2927 2606

E-mail 電郵: callab(a suncreation.com

Website 網址: www.suncreation.com

Page 1 of 2



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C147473

Certificate No.

C143868

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement
of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID CL130 CL281 TST150A <u>Description</u>
Universal Counter
Multifunction Acoustic Calibrator

Multifunction Acoustic Calibrator DC130171
Measuring Amplifier C141558

Test procedure : MA100N.

5. Results:

5.1 Sound Level Accuracy

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	94.0	± 0.25	± 0.2
114 dB, 1 kHz	114.1		

5.2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value (Hz)
(kHz)	(kHz)	Spec.	
.1	1.000 0	$1 \text{ kHz} \pm 5 \text{ Hz}$	± 0.1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration

校正證書

Certificate No.: C141622

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC14-0645)

Date of Receipt / 收件日期: 11 March 2014

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Rion

Model No. / 型號 Serial No./編號

NL-52 00131627

Supplied By / 委託者

Envirotech Services Co.

Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,

Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

Line Voltage / 電壓 :

Relative Humidity / 相對濕度 : $(55 \pm 20)\%$

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 17 March 2014

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

All results are within manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies, USA
- Fluke Everett Service Center, USA
- Rohde & Schwarz Laboratory, Germany

Tested By

測試

Project Engineer

Certified By

核證

KM Wu Engineer Date of Issue

20 March 2014

簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testir g Laboratory

c o 4F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司-校正及檢測實驗所

co香港新界屯門與安里一號青山灣機模四樓

Tel 電話: 2927 2606 Fax 傳真: 2744 8986 E-ma /電郵: callab@suncreation.com Website 網址: www.suncrea on.com

Page 1 of 3



Sun Creation Engineering Limited

Calibration and Test ng Laboratory

Certificate of Calibration 校正證書

Certificate No.: C141622

證書編號

 The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

Self-calibration was performed before the test.

3. The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment:

Equipment ID CL280 CL281

<u>Description</u>
40 MHz Arbitrary Waveform Generator
Multifunction Acoustic Calibrator

Certificate No. C140016 DC130171

5. Test procedure: MA101N.

6. Results:

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting		Applied Value		UUT	IEC 61672		
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	LA	A	Fast	94.00	1	94.1	± 1.1

6.1.2 Linearity

UUT Setting			Applied Value		UUT		
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	
30 - 130	L _A	A	Fast	94.00	1	94.1 (Ref.)	
				104.00		104.1	
				114.00		114.1	

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting			Applied Value		UUT	IEC 61672	
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L_A	A	Fast	94.00	1	94.1	Ref.
			Slow			94.1	± 0.3

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書而批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

o 4 F. Tsing Shan Wan Exchange Building, 1 Hing On Line, Tuen Mun, New Territories, Hong Kong

亚創工程有限公司 – 校正及檢測實驗所

。 香港新界屯門興安里一號青山灣機樓四樓

Tel 電話: 2927 2606 Fax 傳真: 2744 8986 E-mail 電郵: callab@suncreation.com Website 網址: www.suncreatic t.com

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate s all not be reproduced except in full, without the prior stritten approval of this laboratory.



耀創工程有限公司

Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration

校正證書

Certificate No.: C141622

證書編號

Frequency Weighting 6.3

6.3.1 A-Weighting

	UUT	Setting		Appl	ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _A	A	Fast	94.00	63 Hz	67.8	-26.2 ± 1.5
	1000				125 Hz	77.8	-16.1 ± 1.5
					250 Hz	85.4	-8.6 ± 1.4
					500 Hz	90.8	-3.2 ± 1.4
					1 kHz	94.1	Ref.
					2 kHz	95.3	$+1.2 \pm 1.6$
					4 kHz	95.1	$+1.0 \pm 1.6$
					8 kHz	93.0	-1.1 (+2.1; -3.1
					12.5 kHz	89.6	-4.3 (+3.0 ; -6.0

6.3.2 C-Weighting

,, organing	UUT Setting			Appl	ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	0 - 130 L _A C Fast 94.00	63 Hz	93.2	-0.8 ± 1.5			
			V.S. #5821		125 Hz	93.8	-0.2 ± 1.5
					250 Hz	94.0	0.0 ± 1.4
					500 Hz	94.1	0.0 ± 1.4
					1 kHz	94.1	Ref.
					2 kHz	93.9	-0.2 ± 1.6
					4 kHz	93.3	-0.8 ± 1.6
					8 kHz	91.1	-3.0 (+2.1; -3.1
					12.5 kHz	87.7	-6.2 (+3.0 ; -6.0

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 04663

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value: 94 dB: 63 Hz - 125 Hz $: \pm 0.35 \, dB$

250 Hz - 500 Hz : ± 0.30 dB 1 kHz : ± 0.20 dB 2 kHz - 4 kHz $: \pm 0.35 \text{ dB}$ 8 kHz $: \pm 0.45 \text{ dB}$ 12.5 kHz $: \pm 0.70 \text{ dB}$

104 dB: 1 kHz $: \pm 0.10 \text{ dB (Ref. 94 dB)}$

114 dB: 1 kHz $\pm 0.10 \text{ dB (Ref. 94 dB)}$

- The uncertainties are for a confidence probability of not less than 95 %.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

sun Creation Engineering Limited - Calibration & Testing Laboratory

o 4 F, Tsing Shan Wan Exchange Building, 1 Hing On Lune, Tuen Mun, New Territories, Hong Kong

軍創工程有限公司-校正及檢測實驗所

。香港新界屯門與安里一號青山灣機樓四樓

Tel 電話: 2927 2606 Fax 傳真: 2744 8986

E-mail 電郵: callab@suncreation.com Website 網址: www.suncreatic i.com

he test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate still not be reproduced except in full, without the prior



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C147474

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC14-3079)

Date of Receipt / 收件日期: 5 December 2014

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Casella

Model No. / 型號 Serial No. / 編號 CEL-633A 3521757

Supplied By / 委託者

Envirotech Services Co.

Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,

Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 温度 : (23 ± 2)°C

Relative Humidity / 相對濕度 : (5

 $(55 \pm 20)\%$

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

14 December 2014

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

All results are within manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By

測試

Project Engineer

Certified By

核證

K K Wong

Date of Issue

17 December 2014

Yong 簽發日期

Engineer

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗所

c/o 香港新界屯門興安里一號青山灣機機四樓 Tel/電話: 2927 2606 Fax/傳真: 2744 8986

986 E-mail/電郵: callaba suncreation.com

Website 網址: www.suncreation.com

Page 1 of 3



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C147474

證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration using the Casella Acoustic Calibrator CEL-120/1, S/N: 3421612 was performed before the test.
- 3. The results presented are the mean of 3 measurement at each calibration point.
- 4. Test equipment:

Equipment ID CL280

Description

Certificate No.

CL281

40 MHz Arbitrary Waveform Generator Multifunction Acoustic Calibrator

C140016

DC130171

- 5. Test procedure: MA101N.
- 6. Results:
- 6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT	Setting	Applie	d Value	UUT	IEC 61672 Class 1
Time Weighting	Frequency Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Spec. (dB)
L_{F}	A	114.00	1	113.9	± 1.1

6.1.2

UUT	Setting	Applie	UUT		
Time Weighting	Frequency Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	
$L_{\rm F}$	A	114.00	1	113.9 (Ref.)	
		104.00		103.9	
		94.00		93.9	

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

Time Weighting 6.2

UUT Setting		Applie	d Value	UUT	IEC 61672 Class 1	
Time Weighting	Frequency Weighting	Level Freq. Reading (dB) (kHz) (dB)			Spec. (dB)	
L _F	A	114.00	1	113.9	Ref.	
Ls				113.9	± 0.3	
L				113.9		

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 — 核正及檢測實驗所

c/o 香港新界屯門與安里一號青山灣機樓四樓 Tel 電話: 2927 2606 Fax 傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website 網算: www.suncreation.com



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C147474

證書編號

6.3 Frequency Weighting

6.3.1 'A-Weighting

UUT Setting		App	lied Value	UUT	IEC 61672 Class 1
Time Weighting	Frequency Weighting	Level (dB)	Freq.	Reading (dB)	Spec. (dB)
$L_{\rm F}$	A	94.00	63 Hz	87.6	-26.2 ± 1.5
* .			125 Hz	97.7	-16.1 ± 1.5
			250 Hz	105.2	-8.6 ± 1.4
			500 Hz	110.6	-3.2 ± 1.4
			1 kHz	113.9	Ref.
			2 kHz	115.1	$+1.2 \pm 1.6$
			4 kHz	114.7	$+1.0 \pm 1.6$
			8 kHz	112.4	-1.1(+2.1; -3.1)
			12.5 kHz	108.3	-4.3(+3.0; -6.0)

6.3.2 C-Weighting

UUT	Setting	App	lied Value	UUT	IEC 61672 Class 1
Time Weighting	Frequency Weighting	Level (dB)	Freq.	Reading (dB)	Spec. (dB)
$L_{\rm F}$	C	94.00	63 Hz	113.0	-0.8 ± 1.5
ð.			125 Hz	113.7	-0.2 ± 1.0
			250 Hz	113.8	0.0 ± 1.0
			500 Hz	113.9	0.0 ± 1.0
			1 kHz	113.9	Ref.
			2 kHz	113.7	-0.2 ± 1.0
			4 kHz	112.9	-0.8 ± 1.0
			8 kHz	110.5	-3.0 (+1.5; -3.0)
			12.5 kHz	106.4	-6.2 (+3.0; -6.0)

Remarks: - UUT Microphone Model No.: CEL-251 & S/N: 1950

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 114 dB : 63 Hz - 125 Hz : \pm 0.45 dB

12.5 kHz : $\pm 0.80 \text{ dB}$

104 dB : 1 kHz : \pm 0.10 dB (Ref. 114 dB) 94 dB : 1 kHz : \pm 0.10 dB (Ref. 114 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可測源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所

c/o 香港新界屯門與安里 - 號青山灣機樓四樓

Tel 電話: 2927 2606 Fax 傳真: 2744 8986 E-mail 電郵: callab a suncreation.com Website 網址: www.suncreation.com

Annex F

Event/Action Plans for Noise

Annex F Event and Action Plan for Noise

Event			Ac	tion			
	Environmental Team (ET)		dependent Environmental hecker (IEC)	A	uthorised Person (AP)	C	ontractor
Action Level	 Notify IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, AP at Contractor; Discuss with the Contractor at formulate remedial measures; Increase monitoring frequency check mitigation effectiveness 	nd 3. ; y to	Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the AP accordingly; Supervise the implementation of remedial measures.	 2. 3. 4. 	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to proposed remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented.	1.	Submit noise mitigation proposals to IEC; Implement noise mitigation proposals.
Limit Level	 Identify source; Inform IEC and AP; Repeat measurements to confifindings; Increase monitoring frequency Carry out analysis of Contractor's working proceduto determine possible mitigatito be implemented; Inform IEC, AP and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and AP informed of the results; If exceedance stops, cease additional monitoring. 	2. y; ures ion 3.	Discuss amongst AP, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the AP accordingly; Supervise the implementation of remedial measures.	 1. 2. 3. 4. 5. 	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	 1. 2. 3. 4. 5. 	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the AP until the exceedance is abated.

Annex G

Summary of Implementation Status

Annex G Implementation Schedule for Environmental Protection Measures (1 November to 30 November 2014)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Culturi	al Heritag	ge			
	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	No field work in the reporting month.
S3.9.2	S3.3.1	Vibration Monitoring A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	√
S3.9.2	S3.3.3	Compliance of the Approved Measures and Auditing Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	Archival Recording An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of asbuilt drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	General Construction Methods Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be	Whole site	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure.			
\$3.7.1 & 3.7.2	-	Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the cross referenced location plans and photo records. One set of updated CMP shall be submitted to the AMO for approval before the operation stage of the project.	Whole site	During detailed design, construction, post-construction and operation	√ - CMP was implemented during the reporting month. There were no updates for the CMP.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
	ъре & Visı	ıal			
S4.7.27	-	In-situ Tree Protection - Cordon Zone (CZ) Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.	Whole site	During construction	√ - Part of the cordon zone of Tree-5 has been used as a worker storage room. The Contractor was recommended to pay utmost attention to potential land pollution at the worker storage room at all times. Scaffolding has been set up close to Tree-5 within the cordon zone. The Contractor was reminded to perform proper measures to protect Tree-5 during the carrying out of works within the cordon zone.
S4.7.2	-	In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.	Whole site	During construction	N/A – no root pruning has been conducted yet
S4.7.2	-	In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the tree or at a suitable location on an adjacent building to provide the	Whole site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			
S4.7.2	S4	In-situ Tree Protection - Monthly inspection Monthly inspection of affected trees by an experienced and	Whole site	During construction	\checkmark
		appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.			
S4.7.2	-	<u>Light Control</u> Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	$\sqrt{}$
S4.7.2	S4	Compensatory Tree Planting A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10. The existing tree site will be enlarged to become a wide tree strip to accommodate at least six trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	N/A – Compensatory Tree Planting will be conducted at later stage.
		pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil underneath so that fertilizers and conditioners could be added on a			

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.			
		Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. T10 has a DBH of 20 cm (<i>Table 4.3</i>), and it is proposed that six trees of heavy standard size be planted, each with a DBH of around 10 cm and root balls of not less than 0.75 m diameter and 0.75 m depth,. Since the aggregate DBH of the new trees would be 60 cm, the rate of compensation is equivalent to three times the DBH of T10, far beyond the requirements			
		The six replacement trees should be planted in the new tree strip in two staggered rows, maximising distance between each tree to avoid mutual interference in the future. It is recommended that the species selected should have a small final dimension of less than 10 m height given the proximity to built structures such as the retaining wall and buildings. Two each of the outstanding and related flowering tree species connected to local natural history are suggested::			
		 Bauhinia 'Blakeana' a native evergreen species with deep mauve flowers and an exceptionally long flowering period from late autumn to early spring. 			
		- <i>Bauhinia purpure,</i> a native evergreen with lighter purple flowers from late autumn to early winter.			
		 Bauhinia variegata, an exotic deciduous species, with pale pinkish flowers in spring to early summer often when the tree has little or no leaves. 			
S4.7.2	S4	Vertical Greening	Inner Southern Wall	During detailed design and	N/A – No vertical greening was conducted during the reporting month.
		Within the limitations of the conservation of the CPS character, greening of vertical structures should be provided where possible.		construction	
		As such it is recommended that the inner southern wall of the Site be planted as a green wall. The plantings should be inserted in between each of the large protruding piers and an offset be made from both the			

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		top and bottom edge so that old and new are equally visible. An independent frame should be strategically positioned in order to ensure minimal disturbance to the original wall, and provide the main structural support and planting surface for the green wall. The frame on to which the new green will be planted should contain its own irrigation system so that moisture for the plants will remain mainly on the planting surface and not the exiting wall behind. The planting chosen should be appropriate to the Hong Kong climate, requiring relatively little maintenance to sustain the quality of both plants and wall.			
S4.7.2	-	New Custom Paving New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	N/A – No custom paving was conducted during the reporting month.
S4.7.2	S4	In-situ Tree Protection - Quarterly inspection Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction.	Whole site	During post construction and operation	N/A – The quarterly inspection will be conducted at later stage.
Noise					
S5.9	-	 The following site practices should be followed during the construction of the Project: Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase; Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase; Mobile plant, if any, will be sited as far away from NSRs as possible; 	Whole Site	During construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		 Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum; Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 			
S5.9	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	√ ·
S5.9	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps.	Whole Site	During construction	√
S5.9	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	$\sqrt{}$
S5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	√ ·
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage.	Whole Site	During construction	√ ·
Air Qu S6.8.1	ality -	Dust control measures stipulated in the <i>Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	√ ·

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	V
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	V
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	√
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	√ ·
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	V
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	V
S6.8.1	-	Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	V
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	V
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if required, from the ground floor level of building for construction of superstructure of the new buildings.	Whole Site	During construction	V
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	N. Control of the con
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	V
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	V
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A – Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	√
Water (Quality		I		
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	V
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A – Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	V
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	V
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	V
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A – Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A – Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	√
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	√
Waste N	Manageme	nt			
S8.5	\$6.3.1 & Table 6.1	General The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	√
S8.5	-	Management of Waste Disposal The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	√
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket system will be included as one of the contractual requirements and implemented by the contractor.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	V
S8.5	S6.3	Reduction of Construction Waste Generation C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	√
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	V
S8.5	S6	 Containers used for storage of chemical waste shall: Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>. 	Whole Site	During construction and operation	V
S8.5	S6	 Storage areas for chemical waste shall: Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and Be arranged so that incompatible materials are appropriately separated. 	Whole Site	During construction and operation	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	√
S8.5	S6 & Table 6.1	General Refuse General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	V
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	√
S8.5	S6	Staff Training At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	√ ·
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	√

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period

Annex G Implementation Schedule for Environmental Protection Measures (1 December to 31 December 2014)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Cultura	al Heritag	ge			
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	No field work in the reporting month.
S3.9.2	S3.3.1	Vibration Monitoring A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	√
S3.9.2	S3.3.3	Compliance of the Approved Measures and Auditing Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	Archival Recording An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of asbuilt drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	General Construction Methods Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be	Whole site	During construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S3.7.1 & 3.7.2	-	checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the	Whole site	During detailed design, construction, post-construction and operation	√- CMP was implemented during the reporting month. There were no updates for the CMP.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
	ъре & Visı	ıal			
S4.7.27	-	In-situ Tree Protection - Cordon Zone (CZ) Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.	Whole site	During construction	√ - Part of the cordon zone of Tree-5 has been used as a worker storage room. The Contractor was recommended to pay utmost attention to potential land pollution at the worker storage room at all times. Scaffolding has been set up close to Tree-5 within the cordon zone. The Contractor was reminded to perform proper measures to protect Tree-5 during the carrying out of works within the cordon zone.
S4.7.2	-	In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.	Whole site	During construction	N/A – no root pruning has been conducted yet
S4.7.2	-	In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the tree or at a suitable location on an adjacent building to provide the	Whole site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			
S4.7.2	S4	In-situ Tree Protection - Monthly inspection Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree	Whole site	During construction	√
S4.7.2	-	expert within two days. Light Control Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	√
S4.7.2	S4	Compensatory Tree Planting A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10. The existing tree site will be enlarged to become a wide tree strip to accommodate at least six trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil underneath so that fertilizers and conditioners could be added on a	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	N/A – Compensatory Tree Planting will be conducted at later stage.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.			
		Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. T10 has a DBH of 20 cm (<i>Table 4.3</i>), and it is proposed that six trees of heavy standard size be planted, each with a DBH of around 10 cm and root balls of not less than 0.75 m diameter and 0.75 m depth,. Since the aggregate DBH of the new trees would be 60 cm, the rate of compensation is equivalent to three times the DBH of T10, far beyond the requirements			
		The six replacement trees should be planted in the new tree strip in two staggered rows, maximising distance between each tree to avoid mutual interference in the future. It is recommended that the species selected should have a small final dimension of less than 10 m height given the proximity to built structures such as the retaining wall and buildings. Two each of the outstanding and related flowering tree species connected to local natural history are suggested::			
		 Bauhinia 'Blakeana' a native evergreen species with deep mauve flowers and an exceptionally long flowering period from late autumn to early spring. 			
		- <i>Bauhinia purpure,</i> a native evergreen with lighter purple flowers from late autumn to early winter.			
		 Bauhinia variegata, an exotic deciduous species, with pale pinkish flowers in spring to early summer often when the tree has little or no leaves. 			
S4.7.2	S4	Vertical Greening	Inner Southern Wall	During detailed design and	N/A – No vertical greening was conducted during the reporting month.
		Within the limitations of the conservation of the CPS character, greening of vertical structures should be provided where possible.		construction	
		As such it is recommended that the inner southern wall of the Site be planted as a green wall. The plantings should be inserted in between each of the large protruding piers and an offset be made from both the			

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		top and bottom edge so that old and new are equally visible. An independent frame should be strategically positioned in order to ensure minimal disturbance to the original wall, and provide the main structural support and planting surface for the green wall. The frame on to which the new green will be planted should contain its own irrigation system so that moisture for the plants will remain mainly on the planting surface and not the exiting wall behind. The planting chosen should be appropriate to the Hong Kong climate, requiring relatively little maintenance to sustain the quality of both plants and wall.			
S4.7.2	-	New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	N/A – No custom paving was conducted during the reporting month.
S4.7.2	S4	In-situ Tree Protection - Quarterly inspection Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction.	Whole site	During post construction and operation	N/A – The quarterly inspection will be conducted at later stage.
Noise	•			1	
S5.9	-	 The following site practices should be followed during the construction of the Project: Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase; Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase; Mobile plant, if any, will be sited as far away from NSRs as possible; 	Whole Site	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		 Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum; Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 			
S5.9	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	√ ·
S5.9	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps.	Whole Site	During construction	√
S5.9	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	√
S5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	√ ·
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage.	Whole Site	During construction	√ ·
Air Qu S6.8.1		Dust control measures stipulated in the <i>Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	V
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	V
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	√
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	√ ·
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	V
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	V
S6.8.1	-	Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	V
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	V
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if required, from the ground floor level of building for construction of superstructure of the new buildings.	Whole Site	During construction	V
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	N. Control of the con
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	V
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	V
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A – Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	√
Water (Quality		•		
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	V
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A – Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	V
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	V
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	V
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A – Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A – Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	√
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	√
Waste N	Manageme	nt			
S8.5	\$6.3.1 & Table 6.1	General The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	√
S8.5	-	Management of Waste Disposal The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	√
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket system will be included as one of the contractual requirements and implemented by the contractor.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	V
S8.5	S6.3	Reduction of Construction Waste Generation C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	√
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	V
S8.5	S6	 Containers used for storage of chemical waste shall: Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>. 	Whole Site	During construction and operation	V
S8.5	S6	 Storage areas for chemical waste shall: Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and Be arranged so that incompatible materials are appropriately separated. 	Whole Site	During construction and operation	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	√
S8.5	S6 & Table 6.1	General Refuse General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	V
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	√
S8.5	S6	Staff Training At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	√ ·
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	√

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period

Annex G Implementation Schedule for Environmental Protection Measures (1 January to 31 January 2015)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Cultura	al Heritag	ge			
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	No field work in the reporting month.
S3.9.2	S3.3.1	Vibration Monitoring A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	√
S3.9.2	S3.3.3	Compliance of the Approved Measures and Auditing Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	Archival Recording An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of asbuilt drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	General Construction Methods Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be	Whole site	During construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure.			
\$3.7.1 & 3.7.2	-	Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the cross referenced location plans and photo records. One set of updated CMP shall be submitted to the AMO for approval before the operation stage of the project.	Whole site	During detailed design, construction, post-construction and operation	√ - CMP was implemented during the reporting month. There were no updates for the CMP.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status				
	andscape & Visual								
S4.7.27	-	In-situ Tree Protection - Cordon Zone (CZ) Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.	Whole site	During construction	√ - Part of the cordon zone of Tree-5 has been used as a worker storage room. The Contractor was recommended to pay utmost attention to potential land pollution at the worker storage room at all times. Scaffolding has been set up close to Tree-5 within the cordon zone. The Contractor was reminded to perform proper measures to protect Tree-5 during the carrying out of works within the cordon zone.				
S4.7.2	-	In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.	Whole site	During construction	N/A – no root pruning has been conducted yet				
S4.7.2	-	In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the tree or at a suitable location on an adjacent building to provide the	Whole site	During construction	√				

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			
S4.7.2	S4	In-situ Tree Protection - Monthly inspection Monthly inspection of affected trees by an experienced and	Whole site	During construction	√
		appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.			
S4.7.2	-	<u>Light Control</u> Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	√
S4.7.2	S4	A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10. The existing tree site will be enlarged to become a wide tree strip to accommodate at least six trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil underneath so that fertilizers and conditioners could be added on a	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	N/A – Compensatory Tree Planting will be conducted at later stage.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.			
		Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. T10 has a DBH of 20 cm (<i>Table 4.3</i>), and it is proposed that six trees of heavy standard size be planted, each with a DBH of around 10 cm and root balls of not less than 0.75 m diameter and 0.75 m depth,. Since the aggregate DBH of the new trees would be 60 cm, the rate of compensation is equivalent to three times the DBH of T10, far beyond the requirements			
		The six replacement trees should be planted in the new tree strip in two staggered rows, maximising distance between each tree to avoid mutual interference in the future. It is recommended that the species selected should have a small final dimension of less than 10 m height given the proximity to built structures such as the retaining wall and buildings. Two each of the outstanding and related flowering tree species connected to local natural history are suggested::			
		 Bauhinia 'Blakeana' a native evergreen species with deep mauve flowers and an exceptionally long flowering period from late autumn to early spring. 			
		 Bauhinia purpure, a native evergreen with lighter purple flowers from late autumn to early winter. 			
		 Bauhinia variegata, an exotic deciduous species, with pale pinkish flowers in spring to early summer often when the tree has little or no leaves. 			
S4.7.2	S4	Vertical Greening	Inner Southern Wall	During detailed design and	N/A – No vertical greening was conducted during the reporting month.
		Within the limitations of the conservation of the CPS character, greening of vertical structures should be provided where possible.		construction	- 0
		As such it is recommended that the inner southern wall of the Site be planted as a green wall. The plantings should be inserted in between each of the large protruding piers and an offset be made from both the			

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		top and bottom edge so that old and new are equally visible. An independent frame should be strategically positioned in order to ensure minimal disturbance to the original wall, and provide the main structural support and planting surface for the green wall. The frame on to which the new green will be planted should contain its own irrigation system so that moisture for the plants will remain mainly on the planting surface and not the exiting wall behind. The planting chosen should be appropriate to the Hong Kong climate, requiring relatively little maintenance to sustain the quality of both plants and wall.			
S4.7.2	-	New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	N/A – No custom paving was conducted during the reporting month.
S4.7.2	S4	In-situ Tree Protection - Quarterly inspection Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction.	Whole site	During post construction and operation	N/A – The quarterly inspection will be conducted at later stage.
Noise	•			1	
S5.9	-	 The following site practices should be followed during the construction of the Project: Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase; Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase; Mobile plant, if any, will be sited as far away from NSRs as possible; 	Whole Site	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		 Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum; Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 			
S5.9	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	√ ·
S5.9	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps.	Whole Site	During construction	√
S5.9	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	√
S5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	√ ·
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage.	Whole Site	During construction	√ ·
Air Qu S6.8.1		Dust control measures stipulated in the <i>Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	V
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	V
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	√
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	√ ·
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	V
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	V
S6.8.1	-	Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	V
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	V
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if required, from the ground floor level of building for construction of superstructure of the new buildings.	Whole Site	During construction	V
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	N. Control of the con
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	V
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	V
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A – Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	√
Water (Quality		•		
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	V
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A – Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	V
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	V
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	V
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A – Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A – Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	√
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	√
Waste N	Manageme	nt			
S8.5	\$6.3.1 & Table 6.1	General The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	√
S8.5	-	Management of Waste Disposal The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	√
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket system will be included as one of the contractual requirements and implemented by the contractor.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	V
S8.5	S6.3	Reduction of Construction Waste Generation C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	√
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	V
S8.5	S6	 Containers used for storage of chemical waste shall: Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>. 	Whole Site	During construction and operation	V
S8.5	S6	 Storage areas for chemical waste shall: Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and Be arranged so that incompatible materials are appropriately separated. 	Whole Site	During construction and operation	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	√
S8.5	S6 & Table 6.1	General Refuse General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	V
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	√
S8.5	S6	Staff Training At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	√ ·
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	√

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period

Annex H

Noise Monitoring Results

Annex H Noise Monitoring Results

Daytime Noise Monitoring Results

NM6 Chancery Mansion

Date	Start Time	End Time	Weather	Noise	level (dB(A)), 30 min	Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90		Observed		(,		
06-Nov-14	15:22	15:52	Fine	69.7	71.6	66.3	Interior fitting, lifting, handheld breaker (within the project site)	Traffic Noise	-	0.2	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
12-Nov-14	10:16	10:46	Cloudy	68.0	69.4	65.7	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.5	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
18-Nov-14	11:00	11:30	Sunny	64.3	66.1	61.6	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.2	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
24-Nov-14	10:56	11:26	Sunny	68.3	69.5	65.4	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
29-Nov-14	10:50	11:20	Fine	67.6	68.8	65.1	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
	•		Min.	64.3								
			Max.	69.7								

NM2 Ho Fook Building

), 30 min	Major Construction Noise	Other Noise		Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Source(s) Observed	Source(s) Observed	Remarks	(m/s)	Model / ID	Model / ID
06-Nov-14	13:27	13:57	Fine	68.2	70.4	65.7	Interior fitting, lifting (within the project site)	Traffic noise	-	0.2	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
12-Nov-14	8:58	9:28	Cloudy	70.1	71.6	66.9	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.5	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
18-Nov-14	8:57	9:27	Sunny	63.8	66.4	61.4	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
24-Nov-14	9:00	9:30	Sunny	68.1	69.8	65.4	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.2	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
29-Nov-14	8:53	9:23	Fine	69.6	71.3	66.8	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10486660)
			Min.	63.8								

Min. 63.8 Max. 70.1

Annex H Noise Monitoring Results

Daytime Noise Monitoring Results

NM6 Chancery Mansion

Date	Start Time	End Time	Weather	Noise	level (dB(A)), 30 min	Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90		Observed		(,		
05-Dec-14	10:34	11:04	Cloudy	69.9	72.7	66.7	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.9	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)
11-Dec-14	10:35	11:05	Fine	68.0	69.7	65.7	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)
17-Dec-14	11:00	11:30	Sunny	70.6	72.9	67.2	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.8	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)
22-Dec-14	11:00	11:30	Sunny	67.9	69.4	64.8	Interior fitting, lifting (within the project site)	Traffic Noise	-	1.2	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)
27-Dec-14	10:30	11:00	Cloudy	67.1	68.7	64.6	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)
			Min.	67.1								
			Max.	70.6								

NM2 Ho Fook Building

NIVIZ FIO FOO	. Janany											
				Noise	level (dB(A)), 30 min	Major Construction Noise	Other Noise		Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Source(s) Observed	Source(s) Observed	Remarks	(m/s)	Model / ID	Model / ID
05-Dec-14	8:37	9:07	Cloudy	66.1	67.6	63.7	Interior fitting, lifting (within the project site)	Traffic noise	-	0.9	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)
11-Dec-14	8:37	9:07	Fine	71.9	74.2	69.0	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)
17-Dec-14	9:00	9:30	Sunny	68.1	70.4	65.5	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.5	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)
22-Dec-14	9:00	9:30	Sunny	69.6	71.0	66.6	Interior fitting, lifting (within the project site)	Traffic Noise	-	1.0	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)
27-Dec-14	8:27	8:57	Cloudy	69.2	71.3	65.3	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.5	RION- NL52 (S/N 00131627)	RION - NC73 (S/N 10786708)

Min. 66.1 Max. 71.9

Annex H Noise Monitoring Results

Daytime Noise Monitoring Results

NM6 Chancery Mansion


Date	Start Time	End Time	Weather	Noise	level (dB(A)), 30 min	Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90		Observed		()	model/ ib	model/ ib
02-Jan-15	10:45	11:15	Sunny	67.0	68.6	63.5	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
08-Jan-15	10:45	11:15	Sunny	67.6	69.7	63.8	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
14-Jan-15	15:30	16:00	Sunny	66.9	68.4	64.6	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
20-Jan-15	15:30	16:00	Sunny	67.5	69.1	64.6	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
26-Jan-15	10:30	11:00	Sunny	73.7	75.9	70.5	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
31-Jan-15	11:00	11:30	Cloudy	73.5	75.8	69.4	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	66.9								


Max. 73.7

NM2 Ho Fook Building

Start Time	End Time		Noise level (dB(A)), 30 mir), 30 111111	Maria - O Nation	Other Noise		M/2		Calibrator	
		Weather	Leq	L10	L90	Major Construction Noise Source(s) Observed	Source(s) Observed	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Model / ID	
8:47	9:17	Sunny	69.6	72.6	65.2	Interior fitting, lifting (within the project site)	Traffic noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
8:43	9:13	Sunny	70.3	73.2	65.5	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
13:30	14:00	Sunny	71.1	72.7	68.3	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
13:28	13:58	Sunny	64.8	66.6	62.5	Interior fitting, lifting (within the project site)	Traffic Noise	1	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
8:30	9:00	Sunny	71.1	75.0	67.2	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
9:02	9:32	Cloudy	70.5	72.7	67.1	Interior fitting, lifting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
	8:43 13:30 13:28 8:30	8:43 9:13 13:30 14:00 13:28 13:58 8:30 9:00	8:43 9:13 Sunny 13:30 14:00 Sunny 13:28 13:58 Sunny 8:30 9:00 Sunny	8:43 9:13 Sunny 70.3 13:30 14:00 Sunny 71.1 13:28 13:58 Sunny 64.8 8:30 9:00 Sunny 71.1 9:02 9:32 Cloudy 70.5	8:43 9:13 Sunny 70.3 73.2 13:30 14:00 Sunny 71.1 72.7 13:28 13:58 Sunny 64.8 66.6 8:30 9:00 Sunny 71.1 75.0 9:02 9:32 Cloudy 70.5 72.7	8:43 9:13 Sunny 70.3 73.2 65.5 13:30 14:00 Sunny 71.1 72.7 68.3 13:28 13:58 Sunny 64.8 66.6 62.5 8:30 9:00 Sunny 71.1 75.0 67.2 9:02 9:32 Cloudy 70.5 72.7 67.1	8:47 9:17 Sunny 69.6 72.6 65.2 the project site) 8:43 9:13 Sunny 70.3 73.2 65.5 Interior fitting, lifting (within the project site) 13:30 14:00 Sunny 71.1 72.7 68.3 Interior fitting, lifting (within the project site) 13:28 13:58 Sunny 64.8 66.6 62.5 Interior fitting, lifting (within the project site) 8:30 9:00 Sunny 71.1 75.0 67.2 Interior fitting, lifting (within the project site) 9:02 9:32 Cloudy 70.5 72.7 67.1 Interior fitting, lifting (within the project site)	8:43 9:13 Sunny 70.3 73.2 65.5 Interior fitting, lifting (within the project site) 13:30 14:00 Sunny 71.1 72.7 68.3 Interior fitting, lifting (within the project site) 13:28 13:58 Sunny 64.8 66.6 62.5 Interior fitting, lifting (within the project site) 8:30 9:00 Sunny 71.1 75.0 67.2 Interior fitting, lifting (within the project site) 13:28 Traffic Noise 13:58 Traffic Noise	8:43 9:17 Sunny 69.6 72.6 65.2 the project site) Iramic noise - 8:43 9:13 Sunny 70.3 73.2 65.5 Interior fitting, lifting (within the project site) Traffic Noise - 13:30 14:00 Sunny 71.1 72.7 68.3 Interior fitting, lifting (within the project site) Traffic Noise - 13:28 13:58 Sunny 64.8 66.6 62.5 Interior fitting, lifting (within the project site) Traffic Noise - 8:30 9:00 Sunny 71.1 75.0 67.2 Interior fitting, lifting (within the project site) Traffic Noise - 9:02 9:32 Cloudy 70.5 72.7 67.1 Interior fitting, lifting (within the project site) Traffic Noise -	8:47 9:17 Sunny 69.6 72.6 65.2 the project site) Traffic noise - 0.3 8:43 9:13 Sunny 70.3 73.2 65.5 Interior fitting, lifting (within the project site) Traffic Noise - 0.3 13:30 14:00 Sunny 71.1 72.7 68.3 Interior fitting, lifting (within the project site) Traffic Noise - 0.3 13:28 13:58 Sunny 64.8 66.6 62.5 Interior fitting, lifting (within the project site) Traffic Noise - 0.3 8:30 9:00 Sunny 71.1 75.0 67.2 Interior fitting, lifting (within the project site) Traffic Noise - 0.2 9:02 9:32 Cloudy 70.5 72.7 67.1 Interior fitting, lifting (within the project site) Traffic Noise - 0.5	8:47 9:17 Sunny 69.6 72.6 65.2 the project site) Iraffic Noise - 0.3 3521757) 8:43 9:13 Sunny 70.3 73.2 65.5 Interior fitting, lifting (within the project site) Traffic Noise - 0.3 CEL-633A (S/N 3521757) 13:30 14:00 Sunny 71.1 72.7 68.3 Interior fitting, lifting (within the project site) Traffic Noise - 0.3 CEL-633A (S/N 3521757) 13:28 13:58 Sunny 64.8 66.6 62.5 Interior fitting, lifting (within the project site) Traffic Noise - 0.3 CEL-633A (S/N 3521757) 8:30 9:00 Sunny 71.1 75.0 67.2 Interior fitting, lifting (within the project site) Traffic Noise - 0.2 CEL-633A (S/N 3521757) 9:02 9:32 Cloudy 70.5 72.7 67.1 Interior fitting, lifting (within the project site) Traffic Noise - 0.5 CEL-633A (S/N 3521757)	


Min. 64.8 Max. 71.1

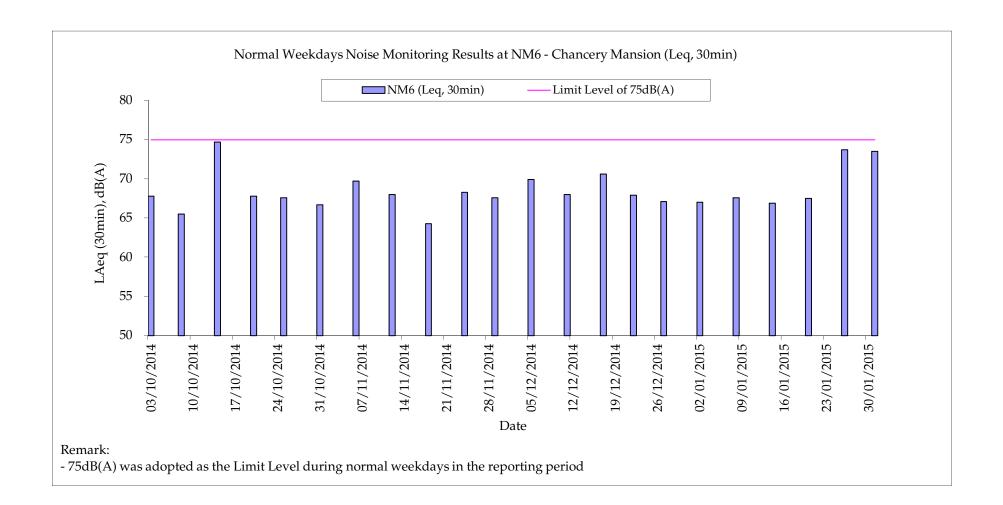

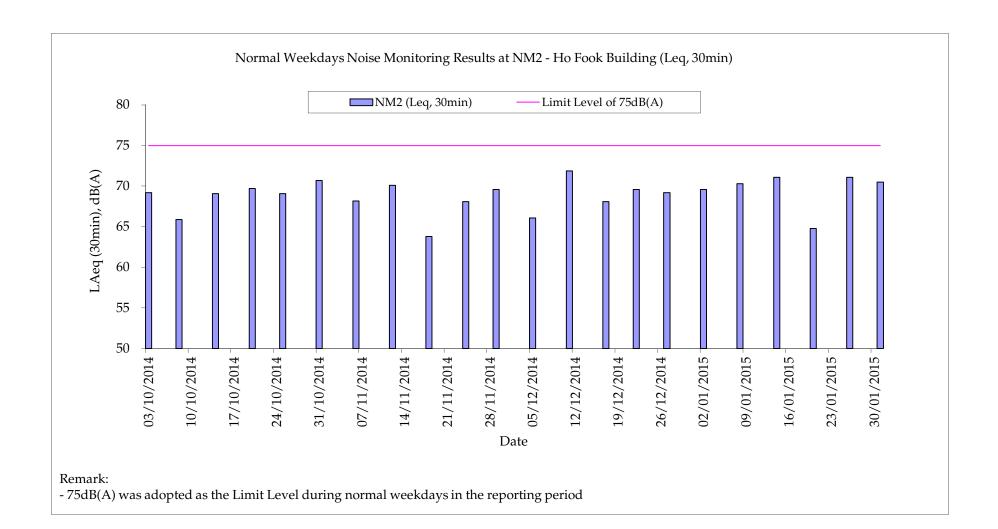

Annex I

Construction Programme of the Project

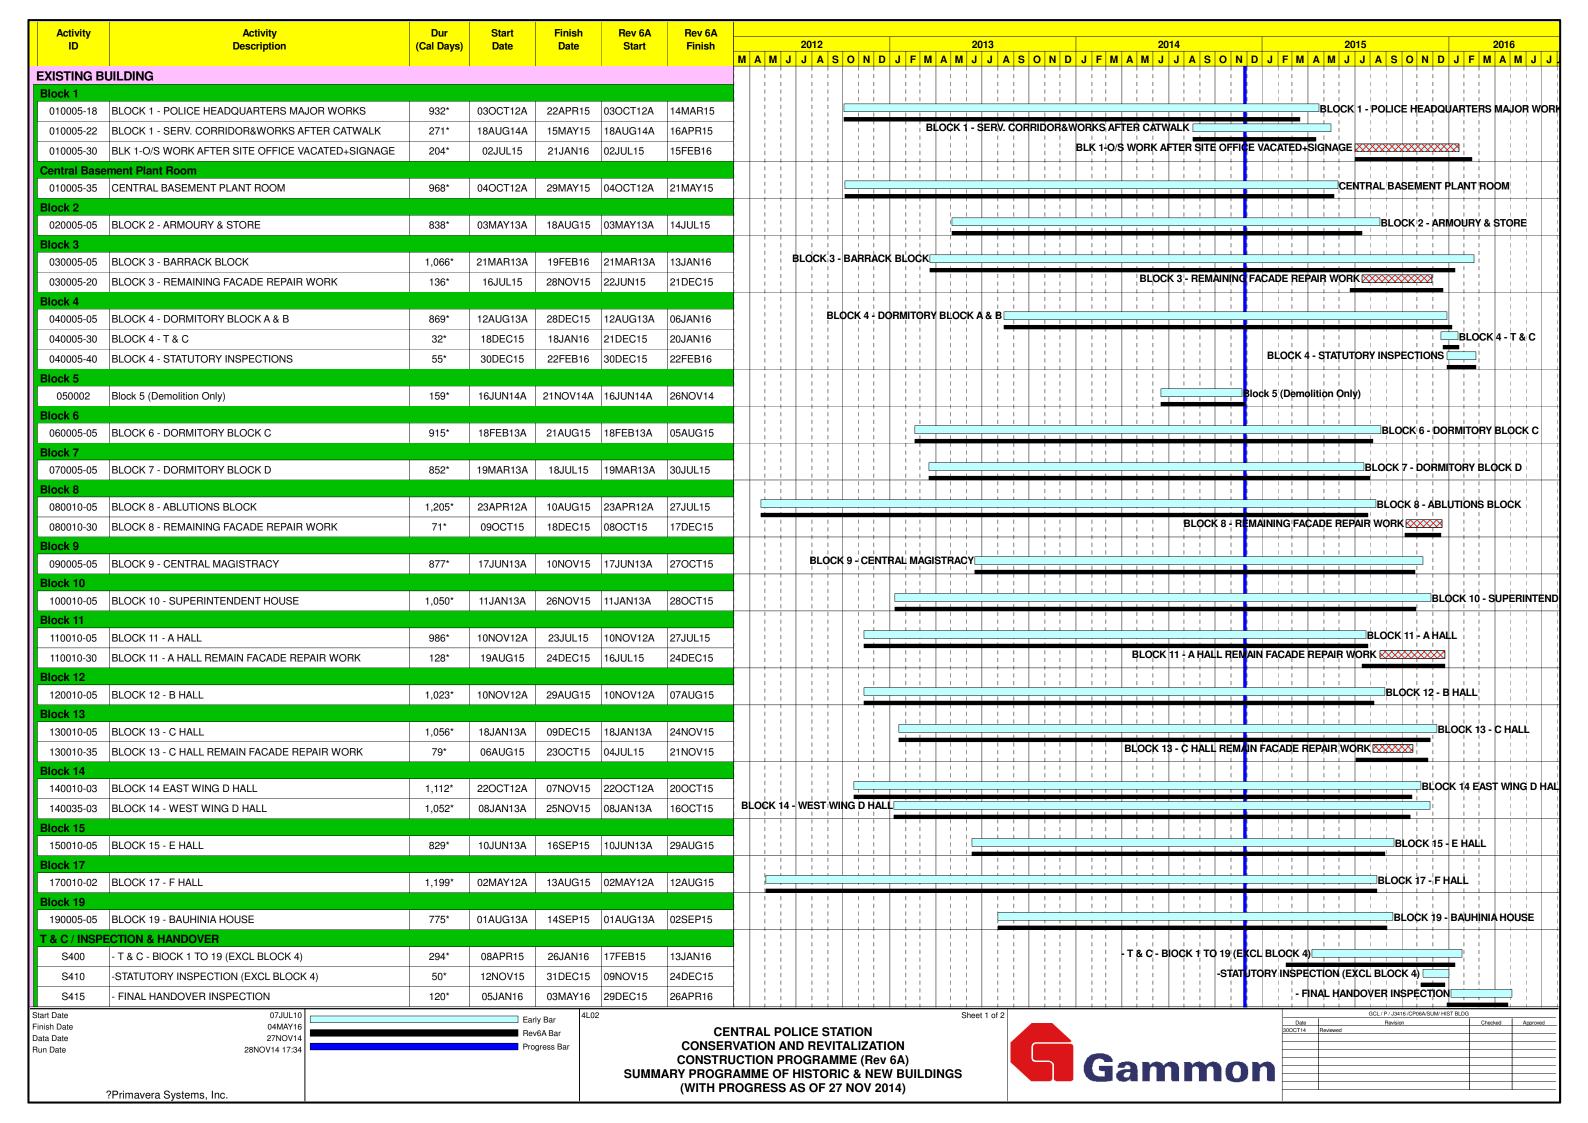

Activity	Activity	Dur	Start	Finish	Rev 6A	Rev 6A		2012		0012		200	11.4		2015	2016
ID	Description	(Cal Days)	Date	Date	Start	Finish	DA A DA I	2012 J A S O N D	1 5 14	2013 A M J J A S O N D	J F M	∠U ∧ № 1)14 J A S O N D	J F M A M	2015	2016 J F M A M J J
NEW BUILD	INGS						IVI A IVI J	J A S O N D	J F W A	A M J J A J J N D	J F W	A W J	J A S O N L	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	J J A J O N D	
OBW																
OBW-0010	OLD BAILEY WING	1,374*	30MAR12A	02JAN16	30MAR12A	24DEC15										OLD BAILEY WING
AW												1 1				
AW-0010	ARBUTHNOT WING	1,291*	08MAY12A	19NOV15	08MAY12A	07NOV15									ARE	BUTHNOT WING
INSPECTION	I & HANDOVER										1 1	1 1			1 1 1	
OBW-0015	- APPLY FOR WATER SUPPLY & CONNECTION	66*	10OCT15	14DEC15	10OCT15	26NOV15	7 ; ;						- APPLY FOR W	ATER SUPPLY &	CONNECTION	
OBW-0020	- STATUTORY INSPECTION (NEW BLDGS)	50*	12NOV15	31DEC15	09NOV15	24DEC15	7				1 1	i i		UTORY INSPECT	ON (NEW BLDGS)	
OBW-0025	- OP ACHIEVED	0		31DEC15		24DEC15	7 ; ;									- OP ACHIEVED
OBW-0030	- HANDOVER INPSECTION (NEW BLDGS)	120*	05JAN16	03MAY16	29DEC15	26APR16	7 ; ;				1 1	i i		- HANDOVER INF	SECTION (NEW BLDGS	
OBW-0035	- PRACTICAL COMPLETION	0		03MAY16		26APR16	1 ; ;								- PRACTICAL (OMPLETION
SIGNAGE						-									i	
SIGNAGE																
SN-0010	-SIGNAGE	92*	10OCT15	09JAN16	02OCT15	31DEC15	7									-SIGNAGE

Start Date 07JUL10 Finish Date 04MAY16 Data Date 27NOV14 Run Date 28NOV14 17:34 Progress Bar

CENTRAL POLICE STATION
CONSERVATION AND REVITALIZATION
CONSTRUCTION PROGRAMME (Rev 6A)
SUMMARY PROGRAMME OF HISTORIC & NEW BUILDINGS
(WITH PROGRESS AS OF 27 NOV 2014)



	GCL / P / J3416 /CP06A/SUM/ HIST BLDG		
Date	Revision	Checked	Approved
30OCT14	Reviewed		

Annex J

Waste Flow Table

Annex J - Waste Flow Table

Month / Year					Qu	antity					
	C&D Materials	Number of Trucks	Volume of C&D	C&D Materials	Number of Trucks for	Volume of C&D	Chemical	Chemical	Recycled materials		
	(inert) (tonnes) (a)	for C&D Materials	Materials (inert)	,	C&D Materials	Materials (non-	Waste (Solid	Waste			
		Disposal (inert)	(m ³) (c)	(tonnes) (b)	Disposal (non-inert)	inert) (m ³) (c)	/kg)	(Liquid/L)	Paper/cardboard (kg)	Plastics (kg)	Metals (kg)
January-14	3813.53	400	1950.00	97.87	36	175.50	0	0	0	0	14110
February-14	3378.16	316	1540.50	37.84	14	68.25	0	0	0	0	9800
March-14	5256.15	516	2515.50	89.39	31	151.13	0	0	6000	0	19030
April-14	3006	299	1457.63	114.31	33	160.88	45	0	0	0	6950
May-14	3195.53	310	1511.25	119.54	37	180.38	0	0	0	0	7000
June-14	2176.81	205	999.38	148.8	45	219.38	0	0	242	0	8830
July-14	1009.96	111	541.13	147.36	49	238.88	0	0	0	0	6680
August-14	379.23	53	258.38	211.86	47	229.13	0	0	0	0	13690
September-14	1216.97	123	599.63	264.83	56	273.00	0	0	0	0	9720
October-14	1162.34	124	604.50	294.33	65	316.88	0	0	0	0	57080
November-14	1249.55	141	687.38	336.57	75	365.63	0	0	0	0	6660
December-14	1177.63	129	628.88	260.33	69	336.38	0	0	68	0	12080
January-15	614.34	69	336.38	222.32	58	282.75	0	0	0	0	3000
Tota	1 55448.55	6168	30069	4972.23	1339	6527.63	7395	57	8713	6	586769

Notes:

⁽a) Inert C&D materials (public fill) include bricks, concrete, building debris, rubble and excavated soil.

⁽b) Non-inert C&D materials include steel, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Steel materials generated from the Project are grouped into construction wastes as the materials were not disposed of with other inert C&D materials and were recycled. The non-inert C&D materials other than steel, plastics and paper / cardboard packaging were disposed of at SENT Landfill.

⁽c) If necessary, use the conversion factor: 3/4 load of dumping truck being equivalent to 6.5 m³ by volume.

Annex K

Environmental Complaint, Environmental Summons and Prosecution Log

Annex K Cumulative Complaint and Summons/Prosecutions Log

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
November 2011	0	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	4	0
April 2012	0	0
May 2012	0	0
June 2012	2	0
July 2012	1	0
August 2012	0	0
September 2012	0	0
October 2012	0	0
November 2012	2	0
December 2012	0	0
January 2013	0	0
February 2013	1	0
March 2013	1	0
April 2013	0	0

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
May 2013	0	0
June 2013	0	0
July 2013	0	0
August 2013	0	0
September 2013	0	0
October 2013	0	0
November 2013	0	0
December 2013	0	0
January 2014	2	0
February 2014	1	0
March 2014	1	0
April 2014	1	0
May 2014	0	0
June 2014	0	0
July 2014	2	0
August 2014	3	0
September 2014	2	0
October 2014	1	0
November 2014	0	0

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
December 2014	0	0
January 2015	0	0
Overall Total	24	0

Annex L

Records of Vibration Monitoring for Trial Piling and Piling Works





Vibration Monitoring Record (November)

		Parade Ground					
Point	VM1-1	VM1-2	VM2-1	VM3-1	VM3-2		
Date	mm/s	mm/s	mm/s	mm/s	mm/s		
01-Nov-14	0.154	0.128	0.156	0.148	0.182		
02-Nov-14			Holiday				
03-Nov-14	0.263	0.106	0.298	0.154	0.131		
04-Nov-14	0.346	0.158	0.179	0.193	0.125		
05-Nov-14	0.191	0.131	0.206	0.167	0.102		
06-Nov-14	0.168	0.108	0.174	0.348	0.179		
07-Nov-14	0.106	0.185	0.156	0.187	0.123		
08-Nov-14	0.398	0.134	0.189	0.204	0.156		
09-Nov-14			Sunday				
10-Nov-14	0.098	0.102	0.314	0.195	0.142		
11-Nov-14	0.156	0.147	0.114	0.286	0.189		
12-Nov-14	0.192	0.120	0.111	0.168	0.175		
13-Nov-14	0.146	0.127	0.177	0.178	0.166		
14-Nov-14	0.114	0.122	0.156	0.169	0.147		
15-Nov-14	0.196	0.159	0.114	0.196	0.162		
16-Nov-14			Sunday				
17-Nov-14	0.165	0.113	0.159	0.209	0.151		
18-Nov-14	0.192	0.102	0.143	0.122	0.149		
19-Nov-14	0.101	0.114	0.138	0.173	0.138		
20-Nov-14	0.191	0.152	0.173	0.129	0.130		
21-Nov-14	0.088	0.078	0.145	0.099	0.109		
22-Nov-14	0.195	0.102	0.165	0.198	0.126		
23-Nov-14			Sunday				
24-Nov-14	0.126	0.114	0.183	0.145	0.192		
25-Nov-14	0.491	0.101	0.151	0.189	0.125		
26-Nov-14	0.119	0.132	0.112	0.156	0.132		
27-Nov-14	0.156	0.105	0.168	0.192	0.122		
28-Nov-14	0.178	0.136	0.122	0.142	0.117		
29-Nov-14	0.162	0.103	0.195	0.241	0.165		
30-Nov-14		_	Sunday	_	_		




Gammon Vibration Monitoring Record (December)

	Parade Ground				
Point	VM1-1	VM1-2	VM2-1	VM3-1	VM3-2
Date	mm/s	mm/s	mm/s	mm/s	mm/s
01-Dec-14	0.165	0.132	0.198	0.351	0.196
02-Dec-14	0.189	0.103	0.151	0.258	0.161
03-Dec-14	0.165	0.128	0.196	0.143	0.185
04-Dec-14	0.113	0.123	0.165	0.198	0.118
05-Dec-14	0.198	0.114	0.127	0.231	0.105
06-Dec-14	0.117	0.165	0.125	0.173	0.151
07-Dec-14			Sunday		
08-Dec-14	0.135	0.156	0.114	0.198	0.113
09-Dec-14	0.168	0.132	0.166	0.143	0.120
10-Dec-14	0.176	0.104	0.137	0.122	0.161
11-Dec-14	0.143	0.111	0.195	0.173	0.124
12-Dec-14	0.147	0.102	0.165	0.165	0.114
13-Dec-14	0.113	0.097	0.130	0.148	0.109
14-Dec-14			Sunday		
15-Dec-14	0.198	0.112	0.175	0.169	0.124
16-Dec-14	0.136	0.105	0.113	0.152	0.108
17-Dec-14	0.155	0.114	0.136	0.159	0.112
18-Dec-14	0.119	0.103	0.154	0.135	0.114
19-Dec-14	0.125	0.117	0.140	0.144	0.132
20-Dec-14	0.110	0.163	0.189	0.183	0.112
21-Dec-14			Sunday		
22-Dec-14	0.143	0.182	0.122	0.149	0.112
23-Dec-14	0.114	0.162	0.103	0.138	0.108
24-Dec-14	0.102	0.122	0.122	0.129	0.170
25-Dec-14		•	Holiday		•
26-Dec-14			Holiday		
27-Dec-14	0.114	0.136	0.135	0.132	0.102
28-Dec-14	Sunday				
29-Dec-14	0.132	0.145	0.159	0.119	0.105
30-Dec-14	0.125	0.114	0.132	0.192	0.119
31-Dec-14	0.113	0.106	0.145	0.153	0.110



Vibration Monitoring Record (Jan 15)

		Parade Ground				
Point	VM1-1	VM1-2	VM2-1	VM3-1	VM3-2	
Date	mm/s	mm/s	mm/s	mm/s	mm/s	
01-Jan-15		J	Public Holida	ıy		
02-Jan-15	0.106	0.109	0.133	0.147	0.115	
03-Jan-15	0.114	0.165	0.144	0.125	0.152	
04-Jan-15			Sunday			
05-Jan-15	0.153	0.114	0.135	0.158	0.120	
06-Jan-15	0.114	0.104	0.139	0.112	0.182	
07-Jan-15	0.161	0.115	0.122	0.169	0.122	
08-Jan-15	0.144	0.120	0.117	0.127	0.130	
09-Jan-15	0.121	0.135	0.107	0.110	0.142	
10-Jan-15	0.111	0.127	0.118	0.162	0.152	
11-Jan-15			Sunday			
12-Jan-15	0.114	0.156	0.138	0.114	0.136	
13-Jan-15	0.168	0.115	0.122	0.183	0.120	
14-Jan-15	0.121	0.120	0.106	0.142	0.128	
15-Jan-15	0.116	0.103	0.110	0.171	0.114	
16-Jan-15	0.150	0.107	0.112	0.193	0.100	
17-Jan-15	0.113	0.108	0.140	0.141	0.128	
18-Jan-15			Sunday			
19-Jan-15	0.148	0.101	0.192	0.156	0.114	
20-Jan-15	0.131	0.105	0.115	0.172	0.120	
21-Jan-15	0.117	0.100	0.114	0.156	0.119	
22-Jan-15	0.163	0.114	0.132	0.128	0.101	
23-Jan-15	0.101	0.112	0.108	0.114	0.122	
24-Jan-15	0.161	0.108	0.121	0.169	0.135	
25-Jan-15			Sunday			
26-Jan-15	0.145	0.103	0.132	0.183	0.118	
27-Jan-15	0.121	0.107	0.108	0.150	0.121	
28-Jan-15	0.136	0.219	0.188	0.194	0.103	
29-Jan-15	0.136	0.105	0.113	0.152	0.108	
30-Jan-15	0.149	0.109	0.098	0.167	0.125	
31-Jan-15	0.159	0.103	0.151	0.158	0.161	

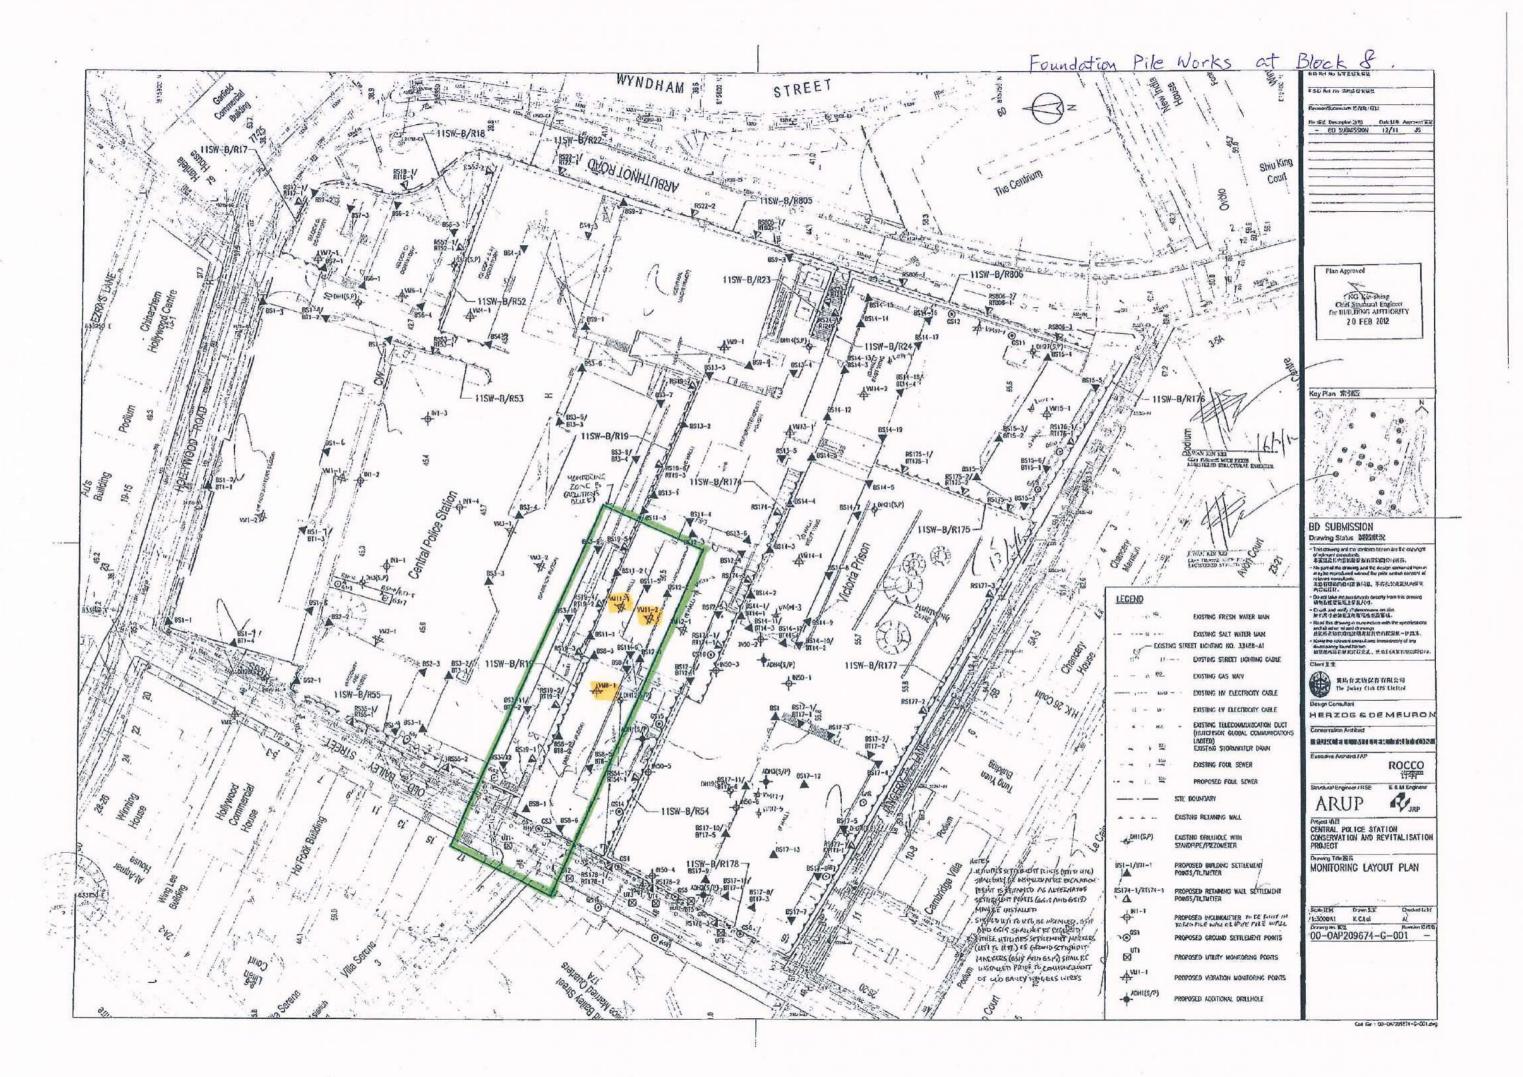

(Block 8 Foundation)



Monitoring Check Pts.	Trigger Levels			
Momentus eneck 1 to	Alert level	Alarm level	Action level	
Vibrating Monitoring	2mm/s	2.5mm/s	3mm/s	
#Vibration at largest span of highest Structural level	5.0mm/s	6.0mm/s	7.5mm/s	

Project Title:	Central Pol	lice Station C	Conservation &	Revitalization	Project No: WP201	1-Nov-2014	to	30-Nov-2014
POINT		VM8-1	VM11-1#	VM11-2				
DATE	PD/(m)	mm/s	mm/s	mm/s				
19-Jun-2012 (Initial)	0.56	0.13	0.19				
1-Nov-2014		0.20	0.18	0.10				
2-Nov-2014					Sunday			
3-Nov-2014		0.37	0.16	0.11				
4-Nov-2014		0.32	0.19	0.13				
5-Nov-2014		0.14	0.19	0.15				
6-Nov-2014		0.17	0.17	0.11				
7-Nov-2014		0.17	0.18	0.13				
8-Nov-2014		0.19	0.17	0.12				
9-Nov-2014					Sunday			
10-Nov-2014		0.22	0.14	0.14				
11-Nov-2014		0.19	0.20	0.17				
12-Nov-2014		0.13	0.19	0.19				
13-Nov-2014		0.14	0.16	0.17				
14-Nov-2014		0.17	0.13	0.17				
15-Nov-2014		0.17	0.20	0.19				
16-Nov-2014					Sunday			
17-Nov-2014		0.20	0.15	0.16				
18-Nov-2014		0.13	0.17	0.11				
19-Nov-2014		0.12	0.14	0.13				
20-Nov-2014		0.19	0.16	0.13				
21-Nov-2014		0.18	0.13	0.16				
22-Nov-2014		0.17	0.17	0.11				
23-Nov-2014					Sunday			
24-Nov-2014		0.14	0.20	0.15				
25-Nov-2014		0.12	0.17	0.13				
26-Nov-2014		0.17	0.11	0.16				
27-Nov-2014		0.14	0.20	0.11				
28-Nov-2014		0.16	0.15	0.10				
29-Nov-2014		0.20	0.13	0.21				
30-Nov-2014					Sunday			

(Block 8 Foundation)



Monitoring Check Pts.	Trigger Levels			
Monitoring Check Fts.	Alert level	Alarm level	Action level	
Vibrating Monitoring	2mm/s	2.5mm/s	3mm/s	
#Vibration at largest span of highest Structural level	5.0mm/s	6.0mm/s	7.5mm/s	

Project Title: Centi	et Title: Central Police Station Conservation & Revitalization		Project No: WP201	1-Dec-2014 to	31-Dec-2014	
POINT	VM8-1	VM11-1#	VM11-2			
DATE PD	D/(m) mm/s	mm/s	mm/s			
19-Jun-2012 (Initial	0.560	0.130	0.190			
1-Dec-2014	0.322	0.147	0.132			
2-Dec-2014	0.156	0.132	0.111			
3-Dec-2014	0.212	0.113	0.103			
4-Dec-2014	0.165	0.180	0.123			
5-Dec-2014	0.148	0.122	0.168			
6-Dec-2014	0.216	0.193	0.147			
7-Dec-2014				Sunday		
8-Dec-2014	0.331	0.152	0.106			
9-Dec-2014	0.182	0.115	0.103			
10-Dec-2014	0.192	0.114	0.132			
11-Dec-2014	0.152	0.216	0.138			
12-Dec-2014	0.131	0.130	0.105			
13-Dec-2014	0.168	0.166	0.115			
14-Dec-2014				Sunday		
15-Dec-2014	0.151	0.136	0.104			
16-Dec-2014	0.182	0.136	0.112			
17-Dec-2014	0.135	0.114	0.165			
18-Dec-2014	0.166	0.114	0.133			
19-Dec-2014	0.165	0.121	0.127			
20-Dec-2014	0.117	0.196	0.154			
21-Dec-2014				Sunday		
22-Dec-2014	0.168	0.111	0.165			
23-Dec-2014	0.196	0.116	0.162			
24-Dec-2014	0.124	0.126	0.113			
25-Dec-2014				Holiday		
26-Dec-2014				Holiday		
27-Dec-2014	0.135	0.146	0.108			
28-Dec-2014		_		Sunday		
29-Dec-2014	0.159	0.118	0.103			
30-Dec-2014	0.121	0.165	0.121			
31-Dec-2014	0.192	0.123	0.125			

WW 恆誠建築工程有限公司 Win Win Way Construction Company Ltd.

(Block 8 Foundation)	
(Block 8 Foundation)	

Monitoring Check Pts.	Trigger Levels				
Transcring Check I to	Alert level	Alarm level	Action level		
Vibrating Monitoring	2mm/s	2.5mm/s	3mm/s		
#Vibration at largest span of	5.0mm/s	6.0mm/s	7.5mm/s		
highest Structural level	J.OHIII/S	O.OHIII/S	7.311111/8		

Project Title: Central Police Station Conservation & Revitalization			Project No: WP201	1-Jan-2015	to 31-Jan-2015		
POINT		VM8-1	VM11-1#	VM11-2			
DATE	PD/(m)	mm/s	mm/s	mm/s			
19-Jun-2012 (Init	tial)	0.56	0.13	0.19			
1-Jan-2015					Public Holiday		
2-Jan-2015		0.13	0.13	0.11			
3-Jan-2015		0.16	0.14	0.12			
4-Jan-2015					Sunday		
5-Jan-2015		0.14	0.11	0.10			
6-Jan-2015		0.12	0.15	0.17			
7-Jan-2015		0.20	0.12	0.19			
8-Jan-2015		0.14	0.16	0.15			
9-Jan-2015		0.11	0.12	0.12			
10-Jan-2015		0.13	0.15	0.13			
11-Jan-2015					Sunday		
12-Jan-2015		0.12	0.14	0.14			
13-Jan-2015		0.16	0.11	0.16			
14-Jan-2015		0.13	0.13	0.17			
15-Jan-2015		0.11	0.18	0.13			
16-Jan-2015		0.13	0.11	0.13			
17-Jan-2015		0.11	0.13	0.12			
18-Jan-2015					Sunday		<u> </u>
19-Jan-2015		0.10	0.14	0.11			
20-Jan-2015		0.11	0.13	0.16			
21-Jan-2015		0.14	0.11	0.12			
22-Jan-2015		0.11	0.11	0.12			
23-Jan-2015		0.11	0.13	0.10			
24-Jan-2015		0.14	0.11	0.11			
25-Jan-2015					Sunday	<u>.</u>	
26-Jan-2015		0.10	0.18	0.13			
27-Jan-2015		0.11	0.15	0.10			
28-Jan-2015		0.17	0.17	0.12			
29-Jan-2015		0.15	0.14	0.10			
30-Jan-2015		0.14	0.16	0.15			
31-Jan-2015		0.11	0.16	0.17			

Mini-piles with post-pressurized grout in CDG and Steel Shear H-piles at Block 1, STREET 11SW-B/R18 11SW-B/R17-Shirt King The Centrium CONT 11SW-B/R806 11SW-B/R23-11SW-B/R52 NG Kin-shing Chief Successal Engineer for BUILING AITHORD 11SW-B/R24 ₩ 1 5 MAR 2012 11SW-B/R53 11SW-B/R19-115W-B/R174 / bH21(5,P) 11SW-B/R175-BD SUBMISSION wing Status 影腦狀況 LEGEND Sympletic representations. 设设路梯设施场上景度代寸 Check Art 406% id directores to sar 再發尺寸必能加工地链增有多益量核 EXISTING STREET LICHTING NO. 33488-AL BSS-2/ 11SW-B/R19-11SW-B/R177 115W-B/R55 HERZOG & DE MEURON EXISTING TELECOMMUNICATION DUCT (HISTORISION OF DEAL COMMUNICATIONS LAMITED) EXISTING STOPHWATER DRAIN ROCCO R. JRP ARUP Proper PATE CENTRAL POLICE STATION CONSERVATION AND REVITALISATION PROJECT EXISTING DRILLHOLE WITH 11SW-B/R54 STANDPIPE/PIEZOMETER Descring Tells 重包 MONITORING LAYOUT PLAN 11SW-B/R178 PROPOSED BUILDING SETTLEMENT POINTS/TRUTMETER RS\$74-1/RT174-PROPOSED INCLINOMETER TO BE BUILT IN BORIED PILE WALL OR PIPE PILE WALL INJUST.

J. UTRITIES SETTLEMENT POINTS (UTI TO UTIS)

SHALL ONLY BE HISTALLED AFTER ETCANATION
PERMIT IS OBTAINED, AS ALTERNATIVE.
SETTLEMENT POINTS (CS18 AND CS19) MAY BE
INSTALLED.

Z. SHOULD UTI TO UTIS BE HISTALLED, GS18 AND
CS18 SHALL NOT BE REQUIRED. 00-0AP209674-G-001 PROPOSED GROUND SETTLEMENT POINTS ⊠ uni PROPOSED UTILITY MONITORING POINTS CSTO SAAL NOT BE BEQUIRED.

JETHER UTLINES SETTLEMENT MARKERS (UT1 TO

UT5) OR GROUND SETTLEMENT MARKETS (CSTB
AND GST0) SHALL BE INSTALLED PROP TO

COMMENCEMENT OF OLD BALLY WING ELS

WORKS. PROPOSED MERATION MONITORING POINTS MONITORING ZONE A PROPOSED ADDITIONAL DRIFLIHOLE



(Block 17 Foundation Works)							
Monitoring Check Pts.	Trigger Levels						
Monitoring Check Fts.	Alert level	Alarm level	Action level				
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s				
# Vibration at largest span of	5.0mm/s	6.0mm/s	7.5mm/s				
highest Structural level	J.OHHII/S	O.OHIIII/S	7.511111/8				

Project Title: Central Police Station Conservation & Revitalization				lization	Project No: WP201	1-Nov-2014	to	30-Nov-2014			
POINT		VM17-1	VM17-3 #								
DATE	PD/(m)	mm/s	mm/s								
19-Jun-2012 (I	(nitial)	0.13	0.37								
Surveying Date											
1-Nov-2014		0.09	0.10								
2-Nov-2014					Sunday						
3-Nov-2014		0.12	0.10								
4-Nov-2014		0.10	0.08								
5-Nov-2014		0.10	0.10								
6-Nov-2014		0.11	0.09								
7-Nov-2014		0.09	0.07								
8-Nov-2014		0.12	0.10								
9-Nov-2014					Sunday						
10-Nov-2014		0.10	0.10								
11-Nov-2014		0.12	0.09								
12-Nov-2014		0.11	0.09								
13-Nov-2014		0.14	0.07								
14-Nov-2014		0.14	0.07								
15-Nov-2014		0.11	0.10								
16-Nov-2014	•		•	•	Sunday	•					
17-Nov-2014		0.10	0.09								
18-Nov-2014		0.11	0.12								
19-Nov-2014		0.10	0.11								
20-Nov-2014		0.17	0.16								
21-Nov-2014		0.15	0.13								
22-Nov-2014		0.12	0.11								
23-Nov-2014				•	Sunday			•			
24-Nov-2014		0.16	0.16								
25-Nov-2014		0.10	0.10								
26-Nov-2014		0.10	0.12								
27-Nov-2014		0.14	0.13								
28-Nov-2014		0.14	0.17								
29-Nov-2014		0.15	0.11								
30-Nov-2014	1		ļ		Sunday	 		-			



(Block 17 Foundation Works)							
Monitoring Check Pts.	Trigger Levels						
Monitoring Check Fts.	Alert level	Alarm level	Action level				
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s				
# Vibration at largest span of	5.0mm/s	6.0 mm/s	7.5mm/s				
highest Structural level	5.0mm/s	0.0ilili/s					

Project Title: C	entral Pol	ice Station Co	onservation &	Revitalization	Project No: WP201	1-Dec-2014	to	31-Dec-201
POINT		VM17-1	VM17-2	VM17-3 #				
DATE	PD/(m)	mm/s	mm/s	mm/s				
19-Jun-2012 (I	nitial)	0.130	0.370	0.370				
Surveying Date								
1-Dec-2014		0.111	0.102	0.105				
2-Dec-2014		0.103	0.093	0.101				
3-Dec-2014		0.141	0.105	0.082				
4-Dec-2014		0.132	0.097	0.116				
5-Dec-2014		0.113	0.143	0.097				
6-Dec-2014		0.106	0.098	0.087				
7-Dec-2014					Sunday			
8-Dec-2014		0.103	0.085	0.110				
9-Dec-2014		0.103	0.108	0.095				
10-Dec-2014		0.117	0.102	0.095				
11-Dec-2014		0.106	0.157	0.107				
12-Dec-2014		0.155	0.134	0.115				
13-Dec-2014		0.125	0.116	0.107				
14-Dec-2014					Sunday			
15-Dec-2014		0.138	0.114	0.182				
16-Dec-2014		0.153	0.141	0.120				
17-Dec-2014		0.114	0.129	0.109				
18-Dec-2014		0.113	0.142	0.185				
19-Dec-2014		0.201	0.157	0.158				
20-Dec-2014		0.126	0.114	0.102				
21-Dec-2014					Sunday			
22-Dec-2014		0.120	0.114	0.103				
23-Dec-2014		0.106	0.141	0.112				
24-Dec-2014		0.099	0.141	0.133				
25-Dec-2014					Holiday			
26-Dec-2014					Holiday			
27-Dec-2014		0.103	0.126	0.110				
28-Dec-2014	1		•	-	Sunday			-
29-Dec-2014		0.123	0.108	0.101				
30-Dec-2014		0.111	0.152	0.105				
31-Dec-2014		0.150	0.103	0.120				



(Block 17 Foundation Works)							
Monitoring Check Pts.		Trigger Levels					
Monitoring Check Pts.	Alert level	Alarm level	Action level				
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s				
# Vibration at largest span of	5.0mm/s	6.0 mm/s	7.5mm/s				
highest Structural level	5.0iiiii/s	o.omm/s					

				Violati	on Record			
Project Title: Central Police Station Conservation & Revitalization			evitalization	Project No: WP20	1 1-Jan-2015	to	31-Jan-2015	
POINT		VM17-1	VM17-3 #					
DATE	PD/(m)	mm/s	mm/s					
19-Jun-2012 (In	nitial)	0.13	0.37					
Surveying Date								
1-Jan-2015					Public Holiday			
2-Jan-2015		0.10	0.09					
3-Jan-2015		0.12	0.10					
4-Jan-2015			•	•	Sunday	•		•
5-Jan-2015		0.10	0.10					
6-Jan-2015		0.12	0.09					
7-Jan-2015		0.11	0.11					
8-Jan-2015		0.15	0.15					
9-Jan-2015		0.16	0.12					
10-Jan-2015		0.17	0.11					
11-Jan-2015					Sunday			•
12-Jan-2015		0.13	0.10					
13-Jan-2015		0.16	0.17					
14-Jan-2015		0.12	0.12					
15-Jan-2015		0.11	0.12					
16-Jan-2015		0.14	0.11					
17-Jan-2015		0.11	0.14					
18-Jan-2015					Sunday			•
19-Jan-2015		0.11	0.11					
20-Jan-2015		0.14	0.10					
21-Jan-2015		0.10	0.11					
22-Jan-2015		0.11	0.10					
23-Jan-2015		0.14	0.11					
24-Jan-2015		0.10	0.09					
25-Jan-2015			· '	<u>'</u>	Sunday	•		•
26-Jan-2015		0.11	0.09					
27-Jan-2015		0.13	0.09					
28-Jan-2015		0.13	0.07					
29-Jan-2015		0.14	0.18					
30-Jan-2015		0.15	0.15					
31-Jan-2015		0.14	0.07					

Bored Pile Walls / Pipe Pile Walls at Block 50 WYNDHAM 3 B.D. Ref No. 度字書稿本編堂 3/3053/11 (B1とけるちゃ) (Hg入(タ) STREET 11SW-B/R18 No 編集 Description 設用 Date日期 Approved宮 - BD SUBMISSION 12/11 JS 11SW-B/R22 Shiu King The Centrium Court 11SW-B/R805 11SW-B/R806 11SW-B/R23 11SW-B/R52 Plan Approved NG Kin shing Chief Structural Engineer for BUILDING AUTHORITY 11SW-B/R24 V 2 0 FEB 2012 RS19-7 BS3-7 11SW-B/R53 11SW-B/R176 **→**N1-3 BS3-5/ BT3-3 **A**^{VM13−1} 1SW-B/R19 BS3-8/ BT3-4 ▼ 11SW-B/R174 BS14-7 W1-2# 11SW-B/R175 BD SUBMISSION Drawing Status 製鋼狀況 482 LEGEND Check and serily all dimensions on six 所有尺寸必能在下地型環境改改資料。 EXISTING FRESH WATER MAIN Read this drawing in consention with the specificatio and all other related drawings. 此图想必须是双格证明者及其它有图图是一值图道。 EXISTING SALT WATER MAIN EXISTING STREET LIGHTING NO. 33488-A1 iscrepancy found ficient. 加發現內古有任何這樣之處,應立到通知有難顧問公 852-3 853-2/ 11SW-B/R19 EXISTING STREET LIGHTING CARLE 11SW-B/R177 賽馬會文物保育有限公司 1SW-B/R55 BS17-BT17-EXISTING LV ELECTRICITY CABLE HERZOG & DE MEURON EXISTING TELECOMMUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATION LIMITED)
EXISTING STORNWATER DRAIN ROCCO 许李严 EXISTING FOUL SEWER DH19(B\$17-11/ PROPOSED FOUL SEWER E & M Engine JRP SITE BOUNDARY ARUP 11SW-B/R54 EXISTING RETAINING WALL CENTRAL POLICE STATION
CONSERVATION AND REVITALISATION
PROJECT →DHI (S,P) NI N EXISTING DRILLHOLE WITH STANDPIPE/PIEZOMETER Drawing Title MES.
MONITORING LAYOUT PLAN UT2 ₹5178-17 ⊠ ₹5178-17 BS1-1/BT1-1 PROPOSED BUILDING SETTLEMENT POINTS/TILTMETER DEC 23 P 2:09 HOTES

LATTLETES SOFTEMENT HONTS LITE TO LITE

SHALL DAYS BE INSTRUCTO A PARK EXCHANDIN

PECHATY IS RETAINED AS RETEINATION

SOFTEMENT, POINTS (AS IN TO SO SO) MAY

BE INSTRUCTOR OF WHATALED, AS IN

AND AS IN STAIL NOT BE UNDINOUSED.

SHALL TO LITELY SO TOTAL MEN HAPKERS

SINT TO LITELY SO MEMORY SOFT I LUBRAT PROPOSED RETAINING WALL SET EMENT POINTS/FILTMETER RS174-1/RT174-1 →IN1-PROPOSED INCLINOMETER TO BE EAST IN BORED PILE OR PIPE PILE WALL 1:300941 K.C.Lai AL
Driveing No. IROK Player
00-OAP209674-G-001 ⊚^{GS1} PROPOSED GROUND SETTLEMENT POINTS ⊠ UT1 Loon PROPOSED UTILITY MONITORING POINTS ENTITO ITE OF ECONO SET LEMENT WHEREAS (DOSE TENSIFY SHALLEF INSTALLED PRICE TO THE CHMENCHAM OF OLD BRILLEY WITH THE WIGHES **₩**1-1 PROPOSED VIBRATION MONITORING POINTS → ACH1(S/P) PROPOSED ADDITIONAL DRILLHOLE Ged Hit: : 00-0X-209674-G-001.dwg



(Bored Pile Walls / Pipe Pile Walls at Block 50)

Monitoring Check Pts.	Trigger Levels					
Monitoring Check Fts.	Alert level	Alarm level	Action level			
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s			
# Vibration at largest span of	5.0mm/s	6.0mm/s	7.5mm/s			
highest Structural level	5.011111/5	0.011111/3				

Project Title:	Central P	Police Station	Conservation of	& Revitalization	on	Project No: W	/P201	1-Nov-2014	to	30-Nov-2014
POINT	Γ	VM8-1	VM11-1#	VM11-2	VM12-1#	VM12-2	VM14-3	VM17-1	VM17-2	VM17-3 #
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
19-Jun-2012	(Initial)	0.56	0.13	0.19	0.22	0.13	0.21	0.13	0.13	0.37
Surveying Date	;									
1-Nov-2014		0.20	0.18	0.10	0.20	0.16	0.17	0.09	0.10	0.10
2-Nov-2014			•			Sunday				
3-Nov-2014		0.37	0.16	0.11	0.32	0.15	0.56	0.12	0.07	0.10
4-Nov-2014		0.32	0.19	0.13	0.16	0.14	0.18	0.10	0.10	0.08
5-Nov-2014		0.14	0.19	0.15	0.20	0.16	0.25	0.10	0.11	0.10
6-Nov-2014		0.17	0.17	0.11	0.18	0.15	0.22	0.11	0.12	0.09
7-Nov-2014		0.17	0.18	0.13	0.21	0.14	0.31	0.09	0.10	0.07
8-Nov-2014		0.19	0.17	0.12	0.19	0.16	0.17	0.12	0.10	0.10
9-Nov-2014			•			Sunday				
10-Nov-2014		0.22	0.14	0.14	0.13	0.15	0.14	0.10	0.08	0.10
11-Nov-2014		0.19	0.20	0.17	0.19	0.20	0.19	0.12	0.10	0.09
12-Nov-2014		0.13	0.19	0.19	0.32	0.13	0.16	0.11	0.12	0.09
13-Nov-2014		0.14	0.16	0.17	0.25	0.12	0.16	0.14	0.12	0.07
14-Nov-2014		0.17	0.13	0.17	0.20	0.12	0.18	0.14	0.12	0.07
15-Nov-2014		0.17	0.20	0.19	0.13	0.17	0.19	0.11	0.12	0.10
16-Nov-2014			•	-	•	Sunday	•	•		•
17-Nov-2014		0.20	0.15	0.16	0.18	0.13	0.18	0.10	0.10	0.09
18-Nov-2014		0.13	0.17	0.11	0.14	0.12	0.15	0.11	0.09	0.12
19-Nov-2014		0.12	0.14	0.13	0.20	0.11	0.20	0.10	0.09	0.11
20-Nov-2014		0.19	0.16	0.13	0.16	0.10	0.18	0.17	0.11	0.16
21-Nov-2014		0.18	0.13	0.16	0.21	0.12	0.16	0.15	0.14	0.13
22-Nov-2014		0.17	0.17	0.11	0.19	0.12	0.18	0.12	0.12	0.11
23-Nov-2014						Sunday				
24-Nov-2014		0.14	0.20	0.15	0.15	0.18	0.20	0.16	0.11	0.16
25-Nov-2014		0.12	0.17	0.13	0.18	0.12	0.13	0.10	0.15	0.10
26-Nov-2014		0.17	0.11	0.16	0.13	0.15	0.15	0.10	0.10	0.12
27-Nov-2014		0.14	0.20	0.11	0.19	0.16	0.16	0.14	0.10	0.13
28-Nov-2014		0.16	0.15	0.10	0.14	0.10	0.17	0.14	0.14	0.17
29-Nov-2014		0.17	0.13	0.19						
30-Nov-2014				<u> </u>	-	Sunday	-			



(Bored Pile Walls / Pipe Pile Walls at Block 50)

Monitoring Check Pts.	Trigger Levels					
Monitoring Check Pts.	Alert level	Alarm level	Action level			
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s			
# Vibration at largest span of	5.0mm/s	6.0mm/s	7.5mm/s			
highest Structural level	5.011111/3	O.OHHII/S				

Project Title:	Central l	Police Station	Conservation	& Revitalizatio	n	Project No: W	/P201	1-Dec-2014	to	31-Dec-2014
POINT	Γ	VM8-1	VM11-1#	VM11-2	VM12-1#	VM12-2	VM14-3	VM17-1	VM17-2	VM17-3 #
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
19-Jun-2012	(Initial)	0.560	0.130	0.190	0.220	0.130	0.210	0.130	0.130	0.370
Surveying Date	e									
1-Dec-2014		0.322	0.147	0.132	0.198	0.121	0.132	0.111	0.102	0.105
2-Dec-2014		0.156	0.132	0.111	0.198	0.132	0.182	0.103	0.093	0.101
3-Dec-2014		0.212	0.113	0.103	0.151	0.120	0.192	0.141	0.105	0.082
4-Dec-2014		0.165	0.180	0.123	0.164	0.154	0.147	0.132	0.097	0.116
5-Dec-2014		0.148	0.122	0.168	0.121	0.198	0.136	0.113	0.143	0.097
6-Dec-2014		0.216	0.193	0.147	0.122	0.103	0.146	0.106	0.098	0.087
7-Dec-2014						Sunday				
8-Dec-2014		0.331	0.152	0.106	0.135	0.133	0.126	0.103	0.085	0.110
9-Dec-2014		0.182	0.115	0.103	0.172	0.114	0.134	0.103	0.108	0.095
10-Dec-2014		0.192	0.114	0.132	0.152	0.103	0.151	0.117	0.102	0.095
11-Dec-2014		0.152	0.216	0.138	0.115	0.108	0.125	0.106	0.157	0.107
12-Dec-2014		0.131	0.130	0.105	0.168	0.111	0.118	0.155	0.134	0.115
13-Dec-2014		0.168	0.166	0.115	0.172	0.132	0.182	0.125	0.116	0.107
14-Dec-2014						Sunday				
15-Dec-2014		0.151	0.136	0.104	0.120	0.183	0.114	0.138	0.114	0.182
16-Dec-2014		0.182	0.136	0.112	0.103	0.154	0.119	0.153	0.141	0.120
17-Dec-2014		0.135	0.114	0.165	0.112	0.130	0.162	0.114	0.129	0.109
18-Dec-2014		0.166	0.114	0.133	0.182	0.145	0.149	0.113	0.142	0.185
19-Dec-2014		0.165	0.121	0.127	0.162	0.149	0.119	0.201	0.157	0.158
20-Dec-2014		0.117	0.196	0.154	0.152	0.114	0.192	0.126	0.114	0.102
21-Dec-2014						Sunday				
22-Dec-2014		0.168	0.111	0.165	0.132	0.103	0.171	0.120	0.114	0.103
23-Dec-2014		0.196	0.116	0.162	0.106	0.153	0.126	0.106	0.141	0.112
24-Dec-2014		0.124	0.126	0.113	0.102	0.149	0.131	0.099	0.141	0.133
25-Dec-2014						Holiday				
26-Dec-2014						Holiday				
27-Dec-2014		0.135	0.146	0.108	0.171	0.155	0.116	0.103	0.126	0.110
28-Dec-2014			• ———			Sunday	·			· ————
29-Dec-2014		0.159	0.118	0.103	0.136	0.158	0.116	0.123	0.108	0.101
30-Dec-2014		0.121	0.165	0.121	0.103	0.165	0.152	0.111	0.152	0.105
31-Dec-2014		0.192	0.123	0.125	0.136	0.114	0.123	0.150	0.103	0.120



(Bored Pile Walls / Pipe Pile Walls at Block 50)

Monitoring Check Pts.	Trigger Levels					
Wolltoning Check Pts.	Alert level	Alarm level	Action level			
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s			
# Vibration at largest span of	5.0mm/s	6.0mm/s	7.5mm/s			
highest Structural level	5.011111/8	0.0IIIII/S				

Project Title:	Central I	Police Station	Conservation of	& Revitalizatio	n	Project No: W	P201	1-Jan-2015	to	31-Jan-2015
POIN	Г	VM8-1	VM11-1#	VM11-2	VM12-1#	VM12-2	VM14-3	VM17-1	VM17-2	VM17-3 #
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
19-Jun-2012	(Initial)	0.56	0.13	0.19	0.22	0.13	0.21	0.13	0.13	0.37
Surveying Date	е									
1-Jan-2015					Pi	ıblic Holiday				
2-Jan-2015		0.13	0.13	0.11	0.10	0.13	0.15	0.10	0.11	0.09
3-Jan-2015		0.16	0.14	0.12	0.12	0.17	0.17	0.12	0.10	0.10
4-Jan-2015	·		•			Sunday	•	•		
5-Jan-2015		0.14	0.11	0.10	0.12	0.12	0.13	0.10	0.12	0.10
6-Jan-2015		0.12	0.15	0.17	0.11	0.12	0.11	0.12	0.10	0.09
7-Jan-2015		0.20	0.12	0.19	0.10	0.17	0.13	0.11	0.11	0.11
8-Jan-2015		0.14	0.16	0.15	0.10	0.14	0.11	0.15	0.13	0.15
9-Jan-2015		0.11	0.12	0.12	0.14	0.13	0.13	0.16	0.16	0.12
10-Jan-2015		0.13	0.15	0.13	0.12	0.18	0.14	0.17	0.15	0.11
11-Jan-2015						Sunday				
12-Jan-2015		0.12	0.14	0.14	0.10	0.16	0.13	0.13	0.12	0.10
13-Jan-2015		0.16	0.11	0.16	0.11	0.14	0.14	0.16	0.12	0.17
14-Jan-2015		0.13	0.13	0.17	0.10	0.11	0.12	0.12	0.11	0.12
15-Jan-2015		0.11	0.18	0.13	0.11	0.13	0.15	0.11	0.13	0.12
16-Jan-2015		0.13	0.11	0.13	0.10	0.10	0.15	0.14	0.11	0.11
17-Jan-2015		0.11	0.13	0.12	0.09	0.11	0.18	0.11	0.11	0.14
18-Jan-2015						Sunday				
19-Jan-2015		0.10	0.14	0.11	0.11	0.10	0.17	0.11	0.11	0.11
20-Jan-2015		0.11	0.13	0.16	0.10	0.11	0.20	0.14	0.11	0.10
21-Jan-2015		0.14	0.11	0.12	0.11	0.12	0.12	0.10	0.11	0.11
22-Jan-2015		0.11	0.11	0.12	0.10	0.15	0.16	0.11	0.14	0.10
23-Jan-2015		0.11	0.13	0.10	0.11	0.14	0.14	0.14	0.10	0.11
24-Jan-2015		0.14	0.11	0.11	0.11	0.16	0.12	0.10	0.11	0.09
25-Jan-2015						Sunday				
26-Jan-2015		0.10	0.18	0.13	0.11	0.12	0.14	0.11	0.10	0.09
27-Jan-2015		0.11	0.15	0.10	0.11	0.11	0.12	0.13	0.10	0.09
28-Jan-2015		0.17	0.17	0.12	0.11	0.18	0.20	0.13	0.12	0.07
29-Jan-2015		0.15	0.14	0.10	0.12	0.18	0.11	0.14	0.11	0.18
30-Jan-2015		0.14	0.16	0.15	0.10	0.14	0.11	0.15	0.13	0.15
31-Jan-2015		0.11	0.16	0.17	0.15	0.12	0.16	0.14	0.12	0.07

Shaft Granted Pre-boved H-piles at Block 51 (Arbithnot Wing) WYNDHAM & STREET 115W-B/R18 11SW-B/R17-Shiu King The Centrium Court 11SW-B/R23-11SW-B/R52 (NG Kin-shing Chief Streetwal Engineer for BUILDING AUTHOUT) -11SW-B/R24 N BS13-4 13 JUL 2012 - 11SW-B/R53 -11SW-B/R176 11SW-B/R19-851-14 871-7 11SW-B/R174-MONITORING ZONE/A 11SW-B/R175 BD SUBMISSION Drawing Status 製鑑狀況 Do net take measurements d 以內質持续關係上無違決寸。 DECK and usely at Developions on M 形式可含混合工物化模模包含温度 Head this answing in conjunction with the injunification and all other related showings.
此類版史包含與此類由的代表了以下的新聞版一樣開議。 EXISTING SALT WATER WAIN EXISTING STREET LICHTING NO. 33488-AT Sacrepancy found below, 如我認內存在在科學協之處。無点於這級有數學所否則 115W-8/R19-11SW-B/R177 EXISTING STREET LIGHTING CABLE 電路音 東京語 20 47年(2 47 The Joseph Class CTS Linkspi 11SW-B/R55-HERZOG & DE MEURON EXISTING FOUL SEWER R. JRP ARUP EXISTING RETAINING WALL Project FIEE
CENTRAL POLICE STATION
CONSERVATION AND REVITALISATION
PROJECT 11SW-B/R54 MONITORING LAYOUT PLAN BS1-1/BI1-1 PROPOSED BUILDING SETTLEMENT FORTS/TICINETER RS174-1/RT174-1 PROPOSED RETAINING WALL SETTLEMENT POINTS/TILLIMETER PROPOSED GROUND SETTLEMENT POINTS E III PROPOSED UTILITY MONITORING POINTS ₩1-1 PROPOSED VERATION MONITORING POINTS CREATER ASSOCIATION PROPOSED ADDITIONAL ORILHOLE Historia Marinary operate With

(Shaft Grouted Pre-bored H-piles at Block 51)



Manitanina Chaela Dto	Trigger Levels				
Monitoring Check Pts.	Alert level	Alarm level	Action level		
Vibrating Monitoring	2mm/s	2.5mm/s	3mm/s		

Project Title:	Central	Police Station	Conservation	& Revitalization	Project No: WP201	1-Nov-2014	to	30-Nov-2014
POINT	,	VM14-4	VM15-2	VM51-1				
DATE	PD/(m)	mm/s	mm/s	mm/s				
03-Dec-2012	(Initial)	0.14	0.21	0.3				
1-Nov-2014		0.31	0.18	0.16				
2-Nov-2014					Sunday			
3-Nov-2014		0.15	0.11	0.13				
4-Nov-2014		0.17	0.14	0.20				
5-Nov-2014		0.30	0.16	0.16				
6-Nov-2014		0.25	0.12	0.18				
7-Nov-2014		0.20	0.11	0.16				
8-Nov-2014		0.16	0.18	0.33				
9-Nov-2014					Sunday			
10-Nov-2014		0.20	0.13	0.19				
11-Nov-2014		0.16	0.14	0.17				
12-Nov-2014		0.14	0.21	0.19				
13-Nov-2014		0.13	0.20	0.17				
14-Nov-2014		0.14	0.19	0.14				
15-Nov-2014		0.19	0.15	0.20				
16-Nov-2014					Sunday			
17-Nov-2014		0.17	0.16	0.17				
18-Nov-2014		0.20	0.15	0.15				
19-Nov-2014		0.17	0.19	0.17				
20-Nov-2014		0.20	0.13	0.18				
21-Nov-2014		0.19	0.16	0.20				
22-Nov-2014		0.20	0.15	0.15				
23-Nov-2014					Sunday			
24-Nov-2014		0.24	0.18	0.16				
25-Nov-2014		0.15	0.21	0.17				
26-Nov-2014		0.15	0.15	0.19				
27-Nov-2014		0.13	0.19	0.11				
28-Nov-2014		0.16	0.14	0.17				
29-Nov-2014		0.13	0.14	0.13				
30-Nov-2014		·			Sunday			

(Shaft Grouted Pre-bored H-piles at Block 51)



Manitonina Chaols Dta	Trigger Levels				
Monitoring Check Pts.	Alert level	Alarm level	Action level		
Vibrating Monitoring	2mm/s	2.5mm/s	3mm/s		

Project Title:	Central 1	Police Station	Conservation &	& Revitalization	Project No: WP201	1-Dec-2014	to	31-Dec-201
POINT		VM14-4	VM15-2	VM51-1				
DATE	PD/(m)	mm/s	mm/s	mm/s				
03-Dec-2012	(Initial)	0.140	0.210	0.300				
1-Dec-2014		0.161	0.133	0.125				
2-Dec-2014		0.139	0.121	0.165				
3-Dec-2014		0.116	0.166	0.147				
4-Dec-2014		0.131	0.15	0.311				
5-Dec-2014		0.157	0.204	0.135				
6-Dec-2014		0.112	0.135	0.172				
7-Dec-2014					Sunday			
8-Dec-2014		0.137	0.103	0.149				
9-Dec-2014		0.119	0.138	0.125				
10-Dec-2014		0.125	0.162	0.173				
11-Dec-2014		0.125	0.153	0.114				
12-Dec-2014		0.167	0.155	0.132				
13-Dec-2014		0.115	0.193	0.121				
14-Dec-2014					Sunday			
15-Dec-2014		0.141	0.15	0.143				
16-Dec-2014		0.125	0.114	0.129				
17-Dec-2014		0.121	0.134	0.111				
18-Dec-2014		0.155	0.193	0.166				
19-Dec-2014		0.139	0.174	0.129				
20-Dec-2014		0.113	0.127	0.182				
21-Dec-2014					Sunday			
22-Dec-2014		0.147	0.163	0.175				
23-Dec-2014		0.123	0.128	0.124				
24-Dec-2014		0.162	0.138	0.134				
25-Dec-2014					Holiday			
26-Dec-2014					Holiday			
27-Dec-2014		0.116	0.165	0.162				
28-Dec-2014					Sunday			
29-Dec-2014		0.131	0.12	0.114				
30-Dec-2014		0.165	0.112	0.166				
31-Dec-2014		0.12	0.135	0.117				

WW 恆誠建築工程有限公司

Win Win Way Construction Company Ltd.

(Shaft Grouted Pre-bored H-piles at Block 51)

Manitonina Chaols Dta	Trigger Levels						
Monitoring Check Pts.	Alert level	Alarm level	Action level				
Vibrating Monitoring	2mm/s	2.5mm/s	3mm/s				

Project Title:	Central l	Police Station	Conservation of	& Revitalization	Project No: WP201	1-Jan-2015	to	31-Jan-2015
POINT		VM14-4	VM15-2	VM51-1				
DATE	PD/(m)	mm/s	mm/s	mm/s				
03-Dec-2012	(Initial)	0.14	0.21	0.3				
1-Jan-2015					Public Holiday			
2-Jan-2015		0.15	0.11	0.12				
3-Jan-2015		0.12	0.17	0.15				
4-Jan-2015	•		•	•	Sunday			•
5-Jan-2015		0.13	0.19	0.17				
6-Jan-2015		0.17	0.14	0.14				
7-Jan-2015		0.11	0.17	0.15				
8-Jan-2015		0.16	0.16	0.15				
9-Jan-2015		0.12	0.14	0.13				
10-Jan-2015		0.15	0.14	0.12				
11-Jan-2015					Sunday			
12-Jan-2015		0.13	0.13	0.12				
13-Jan-2015		0.11	0.16	0.14				
14-Jan-2015		0.12	0.13	0.17				
15-Jan-2015		0.18	0.17	0.13				
16-Jan-2015		0.16	0.12	0.11				
17-Jan-2015		0.15	0.12	0.14				
18-Jan-2015			•		Sunday			
19-Jan-2015		0.13	0.14	0.14				
20-Jan-2015		0.13	0.17	0.16				
21-Jan-2015		0.15	0.12	0.11				
22-Jan-2015		0.12	0.15	0.15				
23-Jan-2015		0.13	0.13	0.14				
24-Jan-2015		0.13	0.17	0.18				
25-Jan-2015					Sunday			
26-Jan-2015		0.14	0.13	0.15				
27-Jan-2015		0.14	0.12	0.12				
28-Jan-2015		0.11	0.15	0.12				
29-Jan-2015		0.13	0.13	0.13				
30-Jan-2015		0.12	0.11	0.19				
31-Jan-2015		0.11	0.11	0.15				

Annex M

Records of Vibration Monitoring for Other Construction Works





	(Block 14 Sti	ructural A&A)						
Manitanina Charle Dto	Trigger Levels							
Monitoring Check Pts.	Alert level	Alarm level	Action level					
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s					
# Vibration at largest span of	5.0mm/s	6.0mm/s	7.5mm/s					
highest Structural level	5.0mm/s	0.0mm/s	7.3mm/s					

Project Title:	Central	Police Station	n Conservation	& Revitalizati	on Proje	ect No: WP201	1-Nov-2014	to	30-Nov-201
POINT		VM14-1#	VM14-2 #	VM14-3	VM14-4				
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s				
19-Nov-12 (In	nitial)	0.103	0.112	0.147	0.136				
1-Nov-2014		0.14	0.14	0.17	0.31				
2-Nov-2014						Sunday			
3-Nov-2014		0.20	0.13	0.56	0.15				
4-Nov-2014		0.17	0.11	0.18	0.17				
5-Nov-2014		0.10	0.18	0.25	0.30				
6-Nov-2014		0.13	0.15	0.22	0.25				
7-Nov-2014		0.16	0.14	0.31	0.20				
8-Nov-2014		0.13	0.19	0.17	0.16				
9-Nov-2014						Sunday			
10-Nov-2014		0.19	0.13	0.14	0.20				
11-Nov-2014		0.16	0.15	0.16	0.19				
12-Nov-2014		0.15	0.12	0.16	0.14				
13-Nov-2014		0.14	0.19	0.16	0.13				
14-Nov-2014		0.14	0.20	0.18	0.14				
15-Nov-2014		0.17	0.16	0.19	0.19				
16-Nov-2014	•					Sunday			·
17-Nov-2014		0.19	0.12	0.18	0.17				
18-Nov-2014		0.12	0.13	0.15	0.20				
19-Nov-2014		0.12	0.11	0.20	0.21				
20-Nov-2014		0.11	0.14	0.18	0.20			·	
21-Nov-2014		0.10	0.19	0.16	0.19				
22-Nov-2014		0.12	0.18	0.18	0.20			<u> </u>	
23-Nov-2014						Sunday			
24-Nov-2014		0.12	0.13	0.20	0.24			·	
25-Nov-2014		0.20	0.12	0.13	0.15			·	
26-Nov-2014		0.13	0.16	0.15	0.15				
27-Nov-2014		0.12	0.19	0.16	0.13				
28-Nov-2014		0.14	0.18	0.17	0.16				
29-Nov-2014		0.17	0.12	0.17	0.13				
30-Nov-2014						Sunday			




	(Block 14 Sti	ructural A&A							
Manitanina Chaola Dta	Trigger Levels								
Monitoring Check Pts.	Alert level	Alarm level	Action level						
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s						
# Vibration at largest span of	5.0mm/s	6.0mm/s	7.5mm/s						
highest Structural level	5.011111/5	0.011111/5	7.311111/8						

Project Title: C	Central Po	olice Station	Conservation	& Revitalizati	on Proje	ect No: WP201	1-Dec-2014	to	31-Dec-201
POINT		VM14-1#	VM14-2 #	VM14-3	VM14-4				
DATE P	D/(m)	mm/s	mm/s	mm/s	mm/s				
19-Nov-12 (Init	ial)	0.103	0.112	0.147	0.136				
1-Dec-2014		0.154	0.115	0.132	0.161				
2-Dec-2014		0.198	0.151	0.182	0.139				
3-Dec-2014		0.113	0.104	0.192	0.116				
4-Dec-2014		0.103	0.112	0.147	0.131				
5-Dec-2014		0.107	0.114	0.136	0.157				
6-Dec-2014		0.130	0.153	0.146	0.112				
7-Dec-2014	•					Sunday			•
8-Dec-2014		0.107	0.133	0.126	0.137				
9-Dec-2014		0.129	0.105	0.134	0.119				
0-Dec-2014		0.107	0.135	0.151	0.125				
1-Dec-2014		0.104	0.122	0.125	0.125				
2-Dec-2014		0.132	0.112	0.118	0.167				
3-Dec-2014		0.113	0.104	0.182	0.115				
4-Dec-2014						Sunday			
5-Dec-2014		0.103	0.153	0.114	0.141				
6-Dec-2014		0.114	0.123	0.119	0.125				
7-Dec-2014		0.122	0.132	0.149	0.155				
8-Dec-2014		0.144	0.152	0.119	0.139				
9-Dec-2014		0.147	0.122	0.119	0.139				
0-Dec-2014		0.103	0.149	0.192	0.113				
1-Dec-2014	•					Sunday			
2-Dec-2014		0.123	0.125	0.171	0.147				
3-Dec-2014		0.102	0.112	0.126	0.123				
4-Dec-2014		0.119	0.127	0.131	0.162				
5-Dec-2014	-					Holiday			
6-Dec-2014						Holiday			
7-Dec-2014		0.102	0.121	0.116	0.116				
8-Dec-2014	•					Sunday			
9-Dec-2014		0.112	0.160	0.116	0.131				
30-Dec-2014	İ	0.120	0.186	0.152	0.165				
31-Dec-2014		0.089	0.132	0.123	0.120				



	(Block 14 Sti	ructural A&A)						
Manitanina Chaola Dta	Trigger Levels							
Monitoring Check Pts.	Alert level	Alarm level	Action level					
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s					
# Vibration at largest span of	5.0mm/s	6.0mm/s	7.5mm/s					
highest Structural level	J.OHIII/S	O.Oinm/s	7.5mm/s					

Project Title: Cent	ral Police Station	n Conservation	& Revitalizati	on Proje	ect No: WP201	1-Jan-2015	to	31-Jan-2015
POINT	VM14-1#	VM14-2 #	VM14-3	VM14-4				
DATE PD/(r	m) mm/s	mm/s	mm/s	mm/s				
19-Nov-12 (Initial)	0.103	0.112	0.147	0.136				
1-Jan-2015				P	ublic Holiday			
2-Jan-2015	0.10	0.11	0.15	0.15				
3-Jan-2015	0.11	0.14	0.17	0.12				
4-Jan-2015					Sunday			
5-Jan-2015	0.10	0.13	0.13	0.13				
6-Jan-2015	0.09	0.16	0.11	0.17			· · · · · · · · · · · · · · · · · · ·	
7-Jan-2015	0.12	0.16	0.13	0.11				
8-Jan-2015	0.14	0.13	0.11	0.16				
9-Jan-2015	0.12	0.11	0.13	0.12				
10-Jan-2015	0.14	0.16	0.14	0.15				
11-Jan-2015	•	•		•	Sunday	•		•
12-Jan-2015	0.11	0.13	0.13	0.13				
13-Jan-2015	0.12	0.13	0.14	0.11				
14-Jan-2015	0.10	0.11	0.12	0.12				
15-Jan-2015	0.10	0.12	0.15	0.18				
16-Jan-2015	0.09	0.14	0.15	0.16				
17-Jan-2015	0.10	0.12	0.18	0.15				
18-Jan-2015					Sunday			
19-Jan-2015	0.13	0.12	0.17	0.13				
20-Jan-2015	0.10	0.15	0.20	0.13				
21-Jan-2015	0.09	0.12	0.12	0.15				
22-Jan-2015	0.11	0.14	0.16	0.12				
23-Jan-2015	0.12	0.14	0.14	0.13				
24-Jan-2015	0.09	0.12	0.15	0.14				
25-Jan-2015					Sunday			
26-Jan-2015	0.11	0.13	0.14	0.14				
27-Jan-2015	0.09	0.11	0.12	0.14			· · · · · · · · · · · · · · · · · · ·	
28-Jan-2015	0.11	0.13	0.20	0.11				
29-Jan-2015	0.12	0.19	0.11	0.13				
30-Jan-2015	0.09	0.13	0.11	0.12				
31-Jan-2015	0.08	0.13	0.16	0.11				

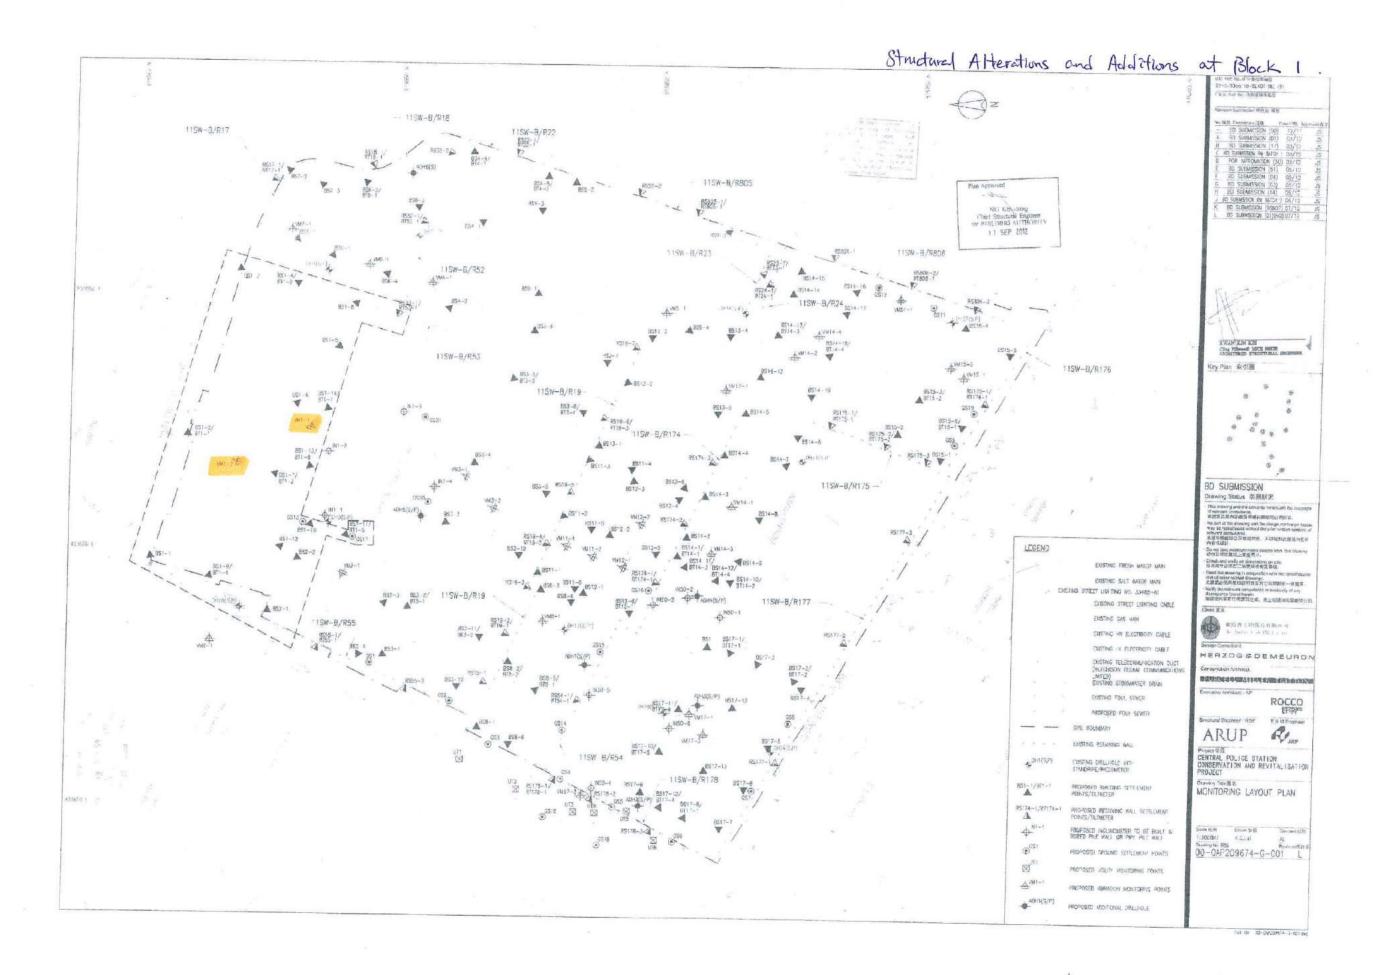

Structural Additions and Alterations at Block 11 WYNDHAM \$ STREET 22-3/3066/10/BLR11 (HU) (5) 11SW-B/R17 Shiu King The Centrium Court BO SUBMISSION (14) 05/12 BO SUBMISSION RW BATCH 7 06/12 - 11SW-B/R806 11SW-B/R23-11SW-B/R52 11SW-B/R24 8514-17 CHIONS Kam-yueng Jack) Chief Structural Engineers for BUILDING AUTHORITY - 3 OCT 2612 11SW-B/R53 11SW-B/R176 11SW-B/R19 BS1-14/ BT1-7 WII-LA 115W-B/R174 ₩BS14-6 DH21(S,P) BD SUBMISSION 115W-B/R175-Drawing Status 製肥狀況 GS20 of reterant consultants. 本職就及其內容的版析展均數數對公司所引 No part of the drawing and the design contain may be reproduced without the prior written o rdevani consultatis。 未經有精體開公司養而回复,不可認對此區底內部同 LEGEND Do not take measurements directly from th 切勿直接设备纸上量度尺寸。 Check and worthy and mensions on site 筋物尺寸还器在工地规划控度及套接。 EXISTING FRESH WATER MAIN Read this drawing in conjunction with the specification and all other related drawings.
此關某的發射契約投票數其它有關關係一件問題。 EXISTING STREET LIGHTING NO. 33488-A1 INS0-2 -3 - ADH4(S/F) description found berein, 约号现为存存任何建筑之高,建立到透加有魏朝商企 11SW-B/R19 EXISTING STREET LIGHTING CABLE 11SW-B/R177-Client 英主 EXISTING CAS MAIN 11SW-B/R55 EXISTING MY ELECTRICITY CABLE Design Consulter EXISTING IV FLECTRICITY CABLE HERZOG & DEMEURON EXISTING TELECOMMUNICATION DUCT (HUTCHISON GLOBAL COUMUNICATIONS **を表現している。中国は25回中国 中部の18回路** LIMITED)
EXISTING STORWWATER DRAIN Executive Architect / AP EXISTING FOUL SEWER ROCCO PROPOSED FOUL SEWER inuctural Engineer / RSE E & M Engineer RUJRP ARUP EXISTING RETAINING WALL Project 되면 CENTRAL POLICE STATION CONSERVATION AND REVITALISATION PROJECT DH1(SP) EXISTING DRILLHOLE WITH 11SW-B/R54 BS17-13 - 11SW-B/R178 STANDPIPE/PIEZOMETER Drawing Tale 關名 BS1-1/BT1-1 PROPOSED BUILDING SETTLEMENT POINTS/TILTMETER MONITORING LAYOUT PLAN RS174-1/RT174-PROPOSED RETAINING WALL SETTLEMENT POINTS/TILTMETER PROPOSED INCLINOMETER TO BE BUILT IN BORED PILE WALL OR PIPE PILE WALL K.G.Lai Drawling No. 國班 Revision 所改 00 — OAP 209 674 — G — 00 1 M PROPOSED GROUND SETTLEMENT POINTS UT1 PROPOSED UTILITY MONITORING POINTS _____VM1−1 PROPOSED VIBRATION MONITORING POINTS ADH1(S/P) PROPOSED ADDITIONAL DRILLHOLE Cod Re - 00-6AP2096/A-G-601.deg



Vibration Monitoring Record (November)

	Blo	ck 1	Block 2	Bloc	ck 3	Block 4	Block	6 & 7	Block 9	Bloc	k 11	Bloc	k 12	Block 13	Bloc	k 15
Point	VM1-1	VM1-2	VM2-1	VM3-1	VM3-2	VM4-1	VM6-1	VM7-1	VM9-1	VM11-1	VM11-2	VM12-1	VM12-2	VM13-1	VM15-1	VM15-2
Date	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
01-Nov-14	0.154	0.128	0.156	0.148	0.182	0.137	0.204	0.187	0.122	0.182	0.103	0.198	0.156	0.126	0.158	0.181
02-Nov-14								Hol	iday							
03-Nov-14	0.263	0.106	0.298	0.154	0.131	0.199	0.189	0.265	0.198	0.156	0.106	0.320	0.146	0.138	0.129	0.110
04-Nov-14	0.346	0.158	0.179	0.193	0.125	0.124	0.168	0.191	0.127	0.187	0.132	0.160	0.136	0.142	0.198	0.135
05-Nov-14	0.191	0.131	0.206	0.167	0.102	0.096	0.181	0.129	0.156	0.193	0.154	0.201	0.159	0.165	0.163	0.156
06-Nov-14	0.168	0.108	0.174	0.348	0.179	0.131	0.122	0.176	0.121	0.172	0.109	0.182	0.149	0.207	0.175	0.122
07-Nov-14	0.106	0.185	0.156	0.187	0.123	0.165	0.198	0.132	0.155	0.184	0.132	0.206	0.143	0.137	0.163	0.105
08-Nov-14	0.398	0.134	0.189	0.204	0.156	0.118	0.203	0.174	0.132	0.165	0.123	0.186	0.161	0.158	0.334	0.180
09-Nov-14	Sunday															
10-Nov-14	0.098	0.102	0.314	0.195	0.142	0.192	0.172	0.195	0.168	0.135	0.139	0.126	0.149	0.192	0.189	0.126
11-Nov-14	0.156	0.147	0.114	0.286	0.189	0.198	0.113	0.125	0.126	0.199	0.165	0.193	0.204	0.164	0.171	0.139
12-Nov-14	0.192	0.120	0.111	0.168	0.175	0.163	0.159	0.198	0.135	0.188	0.189	0.318	0.125	0.159	0.192	0.206
13-Nov-14	0.146	0.127	0.177	0.178	0.166	0.145	0.116	0.184	0.102	0.155	0.166	0.245	0.119	0.167	0.177	0.203
14-Nov-14	0.114	0.122	0.156	0.169	0.147	0.188	0.120	0.168	0.128	0.127	0.170	0.201	0.123	0.135	0.153	0.188
15-Nov-14	0.196	0.159	0.114	0.196	0.162	0.126	0.189	0.149	0.152	0.198	0.185	0.125	0.174	0.109	0.198	0.153
16-Nov-14								Sur	nday							
17-Nov-14	0.165	0.113	0.159	0.209	0.151	0.192	0.142	0.193	0.121	0.147	0.158	0.181	0.132	0.138	0.174	0.162
18-Nov-14	0.192	0.102	0.143	0.122	0.149	0.138	0.156	0.114	0.108	0.169	0.114	0.141	0.123	0.161	0.149	0.146
19-Nov-14	0.101	0.114	0.138	0.173	0.138	0.103	0.118	0.128	0.119	0.141	0.125	0.196	0.112	0.204	0.117	0.188
20-Nov-14	0.191	0.152	0.173	0.129	0.130	0.189	0.193	0.152	0.107	0.157	0.132	0.158	0.103	0.182	0.181	0.129
21-Nov-14	0.088	0.078	0.145	0.099	0.109	0.176	0.140	0.119	0.091	0.128	0.155	0.206	0.116	0.148	0.112	0.163
22-Nov-14	0.195	0.102	0.165	0.198	0.126	0.194	0.135	0.143	0.137	0.168	0.106	0.187	0.123	0.182	0.145	0.154
23-Nov-14								Sur	nday							
24-Nov-14	0.126	0.114	0.183	0.145	0.192	0.126	0.195	0.204	0.136	0.198	0.152	0.145	0.177	0.199	0.155	0.183
25-Nov-14	0.491	0.101	0.151	0.189	0.125	0.149	0.128	0.165	0.161	0.169	0.132	0.181	0.121	0.125	0.169	0.206
26-Nov-14	0.119	0.132	0.112	0.156	0.132	0.135	0.152	0.179	0.149	0.112	0.158	0.132	0.154	0.103	0.193	0.148
27-Nov-14	0.156	0.105	0.168	0.192	0.122	0.195	0.169	0.132	0.102	0.198	0.114	0.189	0.156	0.155	0.114	0.193
28-Nov-14	0.178	0.136	0.122	0.142	0.117	0.183	0.091	0.188	0.095	0.152	0.103	0.136	0.102	0.191	0.174	0.144
29-Nov-14	0.162	0.103	0.195	0.241	0.165	0.191	0.163	0.165	0.121	0.132	0.211	0.125	0.133	0.198	0.132	0.136
30-Nov-14								Sui	nday							



Vibration Monitoring Record (December)

	Bloc	ck 1	Block 2	Bloc	ck 3	Block 4	Block	6 & 7	Block 9	Bloc	k 11	Bloc	k 12	Block 13	Bloc	:k 15
Point	VM1-1	VM1-2	VM2-1	VM3-1	VM3-2	VM4-1	VM6-1	VM7-1	VM9-1	VM11-1	VM11-2	VM12-1	VM12-2	VM13-1	VM15-1	VM15-2
Date	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
01-Dec-14	0.165	0.132	0.198	0.351	0.196	0.135	0.198	0.165	0.102	0.147	0.132	0.198	0.121	0.112	0.125	0.133
02-Dec-14	0.189	0.103	0.151	0.258	0.161	0.123	0.155	0.131	0.109	0.132	0.111	0.198	0.132	0.198	0.165	0.121
03-Dec-14	0.165	0.128	0.196	0.143	0.185	0.192	0.182	0.157	0.128	0.113	0.103	0.151	0.120	0.164	0.147	0.166
04-Dec-14	0.113	0.123	0.165	0.198	0.118	0.175	0.137	0.172	0.105	0.180	0.123	0.164	0.154	0.155	0.311	0.150
05-Dec-14	0.198	0.114	0.127	0.231	0.105	0.152	0.174	0.140	0.158	0.122	0.168	0.121	0.198	0.133	0.135	0.204
06-Dec-14	0.117	0.165	0.125	0.173	0.151	0.133	0.198	0.115	0.102	0.193	0.147	0.122	0.103	0.247	0.172	0.135
07-Dec-14								Sur	nday							
08-Dec-14	0.135	0.156	0.114	0.198	0.113	0.098	0.114	0.153	0.237	0.152	0.106	0.135	0.133	0.168	0.149	0.103
09-Dec-14	0.168	0.132	0.166	0.143	0.120	0.152	0.173	0.140	0.114	0.115	0.103	0.172	0.114	0.139	0.125	0.138
10-Dec-14	0.176	0.104	0.137	0.122	0.161	0.107	0.155	0.138	0.102	0.114	0.132	0.152	0.103	0.175	0.173	0.162
11-Dec-14	0.143	0.111	0.195	0.173	0.124	0.139	0.170	0.162	0.119	0.216	0.138	0.115	0.108	0.158	0.114	0.153
12-Dec-14	0.147	0.102	0.165	0.165	0.114	0.150	0.213	0.126	0.105	0.130	0.105	0.168	0.111	0.119	0.132	0.155
13-Dec-14	0.113	0.097	0.130	0.148	0.109	0.113	0.176	0.193	0.101	0.166	0.115	0.172	0.132	0.235	0.120	0.193
14-Dec-14								Su	nday							
15-Dec-14	0.198	0.112	0.175	0.169	0.124	0.162	0.202	0.135	0.117	0.136	0.104	0.120	0.183	0.159	0.143	0.150
16-Dec-14	0.136	0.105	0.113	0.152	0.108	0.114	0.175	0.162	0.133	0.136	0.112	0.103	0.154	0.176	0.129	0.114
17-Dec-14	0.155	0.114	0.136	0.159	0.112	0.143	0.219	0.146	0.105	0.114	0.165	0.112	0.130	0.184	0.111	0.134
18-Dec-14	0.119	0.103	0.154	0.135	0.114	0.174	0.205	0.114	0.109	0.114	0.133	0.182	0.145	0.231	0.166	0.193
19-Dec-14	0.125	0.117	0.140	0.144	0.132	0.167	0.198	0.122	0.120	0.121	0.127	0.162	0.149	0.218	0.177	0.174
20-Dec-14	0.110	0.163	0.189	0.183	0.112	0.113	0.167	0.209	0.101	0.196	0.154	0.152	0.114	0.176	0.182	0.127
21-Dec-14								Su	nday							
22-Dec-14	0.143	0.182	0.122	0.149	0.112	0.162	0.193	0.114	0.113	0.111	0.165	0.132	0.103	0.125	0.175	0.163
23-Dec-14	0.114	0.162	0.103	0.138	0.108	0.105	0.136	0.105	0.096	0.116	0.162	0.106	0.153	0.120	0.124	0.128
24-Dec-14	0.102	0.122	0.122	0.129	0.170	0.117	0.108	0.115	0.113	0.126	0.113	0.102	0.149	0.131	0.119	0.138
25-Dec-14	Holiday															
26-Dec-14	Holiday															
27-Dec-14	0.114	0.136	0.135	0.132	0.102	0.113	0.165	0.153	0.099	0.146	0.108	0.171	0.155	0.112	0.162	0.165
28-Dec-14								Sur	nday							
29-Dec-14	0.132	0.145	0.159	0.119	0.105	0.166	0.114	0.139	0.150	0.118	0.103	0.136	0.158	0.185	0.114	0.120
30-Dec-14	0.125	0.114	0.132	0.192	0.119	0.128	0.162	0.105	0.135	0.165	0.121	0.103	0.165	0.132	0.166	0.112
31-Dec-14	0.113	0.106	0.145	0.153	0.110	0.156	0.123	0.137	0.112	0.123	0.125	0.136	0.114	0.146	0.117	0.135



Vibration Monitoring Record (Jan 15)

	Blo	ck 1	Block 2	Bloc	ck 3	Block 4	Block	6 & 7	Block 9	Bloc	k 11	Bloc	k 12	Block 13	Bloc	k 15
Point	VM1-1	VM1-2	VM2-1	VM3-1	VM3-2	VM4-1	VM6-1	VM7-1	VM9-1	VM11-1	VM11-2	VM12-1	VM12-2	VM13-1	VM15-1	VM15-2
Date	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
01-Jan-15								Public	Holiday							
02-Jan-15	0.106	0.109	0.133	0.147	0.115	0.139	0.172	0.163	0.163	0.128	0.112	0.104	0.134	0.105	0.116	0.107
03-Jan-15	0.114	0.165	0.144	0.125	0.152	0.121	0.116	0.109	0.108	0.142	0.115	0.123	0.165	0.151	0.149	0.173
04-Jan-15								Sur	nday							
05-Jan-15	0.153	0.114	0.135	0.158	0.120	0.106	0.114	0.108	0.114	0.114	0.102	0.122	0.117	0.139	0.173	0.191
06-Jan-15	0.114	0.104	0.139	0.112	0.182	0.112	0.173	0.142	0.108	0.146	0.169	0.105	0.115	0.172	0.138	0.138
07-Jan-15	0.161	0.115	0.122	0.169	0.122	0.109	0.125	0.139	0.127	0.122	0.188	0.103	0.167	0.124	0.151	0.169
08-Jan-15	0.144	0.120	0.117	0.127	0.130	0.125	0.117	0.177	0.131	0.162	0.152	0.098	0.141	0.174	0.114	0.158
09-Jan-15	0.121	0.135	0.107	0.110	0.142	0.112	0.114	0.135	0.101	0.122	0.118	0.136	0.129	0.120	0.126	0.144
10-Jan-15	0.111	0.127	0.118	0.162	0.152	0.122	0.144	0.148	0.107	0.151	0.129	0.124	0.177	0.118	0.121	0.139
11-Jan-15								Sur	nday							
12-Jan-15	0.114	0.156	0.138	0.114	0.136	0.113	0.158	0.174	0.128	0.141	0.138	0.103	0.156	0.153	0.117	0.125
13-Jan-15	0.168	0.115	0.122	0.183	0.120	0.102	0.119	0.143	0.141	0.114	0.158	0.112	0.143	0.125	0.135	0.162
14-Jan-15	0.121	0.120	0.106	0.142	0.128	0.119	0.143	0.132	0.105	0.128	0.167	0.104	0.114	0.133	0.173	0.130
15-Jan-15	0.116	0.103	0.110	0.171	0.114	0.151	0.138	0.120	0.109	0.175	0.125	0.106	0.129	0.110	0.128	0.173
16-Jan-15	0.150	0.107	0.112	0.193	0.100	0.175	0.165	0.113	0.102	0.114	0.128	0.103	0.104	0.116	0.109	0.124
17-Jan-15	0.113	0.108	0.140	0.141	0.128	0.139	0.147	0.128	0.110	0.128	0.117	0.093	0.112	0.151	0.143	0.115
18-Jan-15								Sur	nday							
19-Jan-15	0.148	0.101	0.192	0.156	0.114	0.162	0.133	0.115	0.106	0.143	0.114	0.108	0.101	0.123	0.135	0.141
20-Jan-15	0.131	0.105	0.115	0.172	0.120	0.145	0.114	0.106	0.094	0.126	0.155	0.102	0.112	0.115	0.162	0.165
21-Jan-15	0.117	0.100	0.114	0.156	0.119	0.128	0.125	0.123	0.109	0.105	0.119	0.108	0.122	0.114	0.113	0.120
22-Jan-15	0.163	0.114	0.132	0.128	0.101	0.151	0.113	0.109	0.105	0.114	0.119	0.102	0.145	0.120	0.149	0.152
23-Jan-15	0.101	0.112	0.108	0.114	0.122	0.121	0.128	0.106	0.111	0.126	0.104	0.113	0.139	0.127	0.112	0.132
24-Jan-15	0.161	0.108	0.121	0.169	0.135	0.109	0.115	0.108	0.102	0.109	0.114	0.106	0.158	0.117	0.175	0.165
25-Jan-15			•		•	•		Sur	nday		•	•	•			
26-Jan-15	0.145	0.103	0.132	0.183	0.118	0.165	0.165	0.114	0.089	0.182	0.131	0.105	0.115	0.115	0.147	0.131
27-Jan-15	0.121	0.107	0.108	0.150	0.121	0.141	0.109	0.101	0.105	0.150	0.103	0.109	0.114	0.108	0.120	0.115
28-Jan-15	0.136	0.219	0.188	0.194	0.103	0.105	0.136	0.149	0.105	0.173	0.116	0.113	0.179	0.120	0.124	0.150
29-Jan-15	0.136	0.105	0.113	0.152	0.108	0.117	0.108	0.198	0.110	0.136	0.104	0.120	0.183	0.158	0.134	0.131
30-Jan-15	0.149	0.109	0.098	0.167	0.125	0.197	0.176	0.162	0.096	0.162	0.152	0.098	0.141	0.119	0.189	0.109
31-Jan-15	0.159	0.103	0.151	0.158	0.161	0.093	0.194	0.146	0.113	0.155	0.166	0.145	0.119	0.109	0.145	0.111

Annex N

A Summary of Current Condition of Character Defining Elements

Schedule of Character Defining Elements

CENTRAL POLICE STATION, HONG KONG

SCHEDULE OF CHARACTER DEFINING ELEMENTS

This Schedule of Character Defining Elements has been prepared at the request of the Antiquities and Monuments Office (AMO) to support applications for S.6 approval under the Antiquities and Monuments Ordinance and the Environmental Impact assessment Ordinance. The levels of significance and their meanings are derived from the work of James Semple Kerr.

For each element, the level of significance is stated, together with the planned outcome and associated mitigation measure, where applicable, and the resultant impact upon the significance. Generally, only those items subject to change are noted, and the impacts should be read as negative. Where elements are deemed currently to be adverse, the impact of the changes should be read as positive.

The levels of significance and definitions as defined by Kerr are stated below. The criteria used to assess the significance of each element are, as directed by AMO: (i) the association with the operation of the Central Police Station Compound; and (ii) its architectural quality. Where these criteria conflict, the resultant assessment score is aggregated.

Each entry in the schedule is accompanied by a photograph of a sample of the item described. The location of each photograph is noted on the floor plans attached in the appendix to the schedule. Similar examples of each item can be seen by observation.

Schedule of Character Defining Elements

	Level of significance	Meaning							
	Exceptional	Where an individual space or element is assessed as displaying a strong contribution to the overall significance of the place. Spaces, elements or fabric exhibit a high degree of intactness and quality, though minor alterations or degradation may be evident.							
	High	Where an individual space or element is assessed as making a substantial contribution to the overall significance of the place. Spaces, elements or fabric originally of substantial quality, yet may have undergone considerable alteration or adaption resulting in presentation which is either incomplete or ambiguous. The category also includes spaces, elements or fabric of average quality in terms of design and materials, but which exhibit a high degree of intactness.							
Positive	Where an individual space or element is assessed as making a mode contribution to the overall significance of the place. Spaces, element fabric originally of some intrinsic quality, and may have undergone or degradation. In addition, elements of relatively new construction the assessment of significance is difficult, may be included. This cat includes original spaces, elements or fabric of any quality which have undergone extensive alteration or adaption.								
	Low	Where an individual space or element is assessed as making a minor contribution to the overall significance of the place, especially when compared to other features. Spaces, elements or fabric originally of little intrinsic quality, any may have undergone alteration or degradation. This category also includes original spaces, elements or fabric of any quality which have undergone extensive alteration or adaption to the extent that only isolated remnants survive (resulting in a low degree of intactness and quality of presentation).							
	Neutral	Where an individual space or element is assessed as having an unimportant relationship with the overall significance of the place. Spaces, elements or fabric are assessed as having little or no significance.							
	Adverse	Where an individual space or element detracts from the appreciation of cultural significance, by adversely affecting or obscuring other significant areas, elements or items.							

Central Police Station

Schedule of Character Defining Elements

Central Police Station

Addendum	Date
Item no. 10.029 edited entry	18 June 2013
Item no. 10.030 added	18 June 2013

01 Police Headquarters

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.001	Flat plywood ceiling lining with plain rectangular cover battens		Adverse	Replace with T&G boarding to match existing	Not applicable	High
01.002	Plaster coving at abutments of walls and ceilings		Low	Remove in exceptional cases eg, where adjacent new lift shaft	Cut back neatly to a square edge and ensure remaining section is secure.	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.003	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
01.004	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.005	Plaster box cornice		Moderate	Remove in exceptional cases eg. where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate
01.006	Panelled doors		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where element cannot be re- used.	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.007	External shutters		High	Reinstate to match existing pattern	Not applicable	High
01.008	External terraces at 1/F		High	Overlay existing concrete paving with timber deck to provide level access	New deck to be reversible	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.009	Plaster ceilings on GF and LG1		Moderate	Install cloud ceilings to accommodate new services	Install fixed grid to minimise damage to ceiling	High
01.010	Timber door frames and architraves		Moderate	Conceal in exceptional cases eg. where adjacent new lift shaft	Retain architrave and door frame in situ. Avoid damage to joinery.	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.011	Concrete floor		Low	Replace where new kitchens and plant rooms to be installed	Carefully remove and retain existing floorboards for re-use. Ensure controlled demolition of concrete structure and removal of debris from building to avoid damage to adjacent surfaces. Protect or carefully remove and set aside adjacent elements such as skirting boards	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.012	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.013	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.014	Existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non-combustible sheet linings to block opening.	Moderate
01.015	Existing walls		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.016	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High
01.017	Mezzanine floor in room 01/LG1/13		Adverse	Remove floor and supporting columns to re-create original double-height space	Not applicable	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.018	Cast iron grilles above Service Corridor 01/LG1/35		High	Remove existing steel sheet covering [alterations to grilles awaiting confirmation from HdM]		
01.019	Perforated concrete deck above lightwell		Adverse	Remove deck and make good brickwork at abutments	Not applicable	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.020	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
01.021	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate non-compliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.022	Main corridors		High	Install new lighting, fire sprinklers, fire doors to comply with Fire Services Code	New fittings to be mounted in a manner that is of its time and reversible. Avoid physical intervention with existing plaster box cornices, architraves, dado rails	High
01.023	Painted signs	之 LOOKLEFT	High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.024	Fixed signs	The state of the s	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.025	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material in a neutral mid-tone.	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.026	Enclosure at First Floor landing of main stair		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.027	Steel railing enclosure at FF level	Service of the servic	Low	Remove	Record on measured drawings and photographs	Low
01.028	Tongued and grooved flat and sloped timber boarded ceilings		Moderate	Repair where necessary and reinstate where missing	Not applicable	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.029	Modern partitions		Adverse	Remove	Not applicable	High
01.030	Tiled dado		High	Cut away for enlargement of existing windows to form new doorways	Cut back to joint line and adjust tiling pattern to suit new opening. New tiles to match existing sizes and colours.	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.031	Reinforced concrete canopy and sash windows		Moderate	Remove canopy and replace sash windows with new windows to match original	Make good brickwork where canopy removed, Reinstate rendered architraves around new window to match similar window facing on West wing	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.032	Arched opening in brick wall above ceiling line		Low	Retain insitu and use to pass through future services. Infill only where opening is within a fire compartment	Use non-combustible material to block opening.	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.033	Ceiling void service installation (Cast Iron Water Tank and pipework)		Low	Remove and make good adjacent surfaces	N/A	Low

02 Armoury

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
02.002	Modern internal doors	-	Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.003	Modern partitions		Adverse	Remove	Not applicable	High
02.004	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High

Schedule of Character Defining Elements

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.005	Brickwork walls enclosing rooms at GF and FF East side		Low	Remove and reinstate verandah	Not applicable	High
02.006	Concrete floors		Low	Selected removal to accommodate new stairs and lift shaft	Carefully form openings to ensure structural stability	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.007	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.008	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.009	Concrete stairs		Adverse	Remove stairs	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.010	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts to reduce impact. Finish ducts in a non-reflective material that is neutral in colour and mid-tone.	High
02.011	Roof structure and tiled soffit		High	Repair and retain.	N/A	Neutral

03 Barracks Block

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
3.002	Panelled doors		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where item cannot be re-used.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.003	External shutters		High	Reinstate to match existing pattern	Not applicable	High
03.004	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.005	Timber spandrel panels below windows		Low	Conceal in exceptional cases eg. where adjacent new lift shaft	Retain frame and spandrel panel where possible. Remove only where necessary in connection with replanning of interiors. Record on measured survey drawings.	Low
03.006	Timber floors		High	Replace where new kitchens and plant rooms to be installed	Limit extent of removal as much as possible. Carefully remove and retain existing floorboards for re-use. Ensure controlled dismantling of timber structure and set aside for possible re-use. Protect or carefully remove and set aside adjacent elements such as skirting boards	Medium

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.007	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.008	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High
03.009	Block existing door openings		Low	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.010	Form new door openings		Low	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance. Re-open original openings where possible. Retain original reveals and arches.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.011	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.012	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
03.013	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.014	Painted signs	NO VISITOR WILL BE ADMITTED WITHOUT THE PERMISSION OF THE D.O. OR FORMATION COMMANDER 或官管主律未知者珍様 进榜 得不可許官警位當	High	Protect in situ	Not applicable	N/A
03.015	Fixed signs	NO. 3 PLATOON R. & F CHANGING ROOM 第三隊更衣室	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.016	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High
03.017	Lean-to structure adjacent North wall		Moderate	Remove	Record on measured survey drawings. Make good walls where roof structure abuts	Moderate

Schedule of Character Defining Elements

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.018	Metal-frames windows at GF North elevation		Adverse	Remove window frames, masonry spandrel panels below and reinstate verandah	Not applicable	High
03.019	Internal walls at Ground Floor level		Moderate	Remove selected internal walls where strictly necessary as part of replanning of interiors	Walls of early or original date to be retained in part eg. by leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not rebonded. Record walls on measured survey dwgs.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.020	Assembly rooms at centre of building (all floors)		Moderate	Sub-divide two rooms on each floor to provide service core, comprising: lifts, toilets, plant rooms, stores	Form new sub-visions using lightweight partitions to achieve reversibility. Form straight joints at abutments with existing retained walls. Notch new partitions around existing brick corbels at high level as a reminder of current condition.	Moderate
03.021	Exposed soffits of timber floors		Moderate	Underline existing floors to achieve specified fire resistance stated in Code	Avoid unnecessary damage to existing structure. New lining will reduce extent of intervention into existing structure. Keep level of new linings well clear of window heads.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.022	Existing window frames/openings		High	Open up selected openings to form new fire escape doors	Retain any salvageable material for possible reuse elsewhere. Retain existing window jambs intact. Cut away masonry to form door openings along same line as window jamb; do not re-bind cut brickwork. Record existing condition on measured survey drawings.	Low
03.023	Single storey outbuildings on south side		Adverse	Demolish	Check for evidence of early route from Magistracy to Prison.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.024	Bridge at east end		Moderate	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.025	Chimneypiece on Ground Floor		Low	Repair and retain in current location	Not applicable	Neutral
03.026	Window in south wall; original dormitory space		Moderate	Remove window and take down brickwork spandrel; subdivide space to form new fire-protected escape route.	Record existing condition on measured survey drawings. New partition wall to be reversible.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.027	Clay-tiled floor in store room adjacent stairs		Low	Remove as part of replanning of interiors	Record on measured survey drawings	Low

04 Dormitory Block A & B

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
04.002	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.003	Plaster box cornice		Moderate	Remove in exceptional cases where eg. where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.004	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.005	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.006	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.007	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.008	Altered doors and windows	BLOOK B	Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.009	Window frames in arcades of North and East elevations		Adverse	Remove window frames and make good masonry reveals and reinstate verandah	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.010	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.011	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.012	Stair from First to Second Floor		High	Replace stair to improve safety	New stair to be built of steel to comply with Code and to distinguish it as being "of its time".	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.013	External verandahs		High	Install new lighting, fire sprinklers, fire doors to comply with Fire Services Code, extract ducting to external walls	New fittings to be mounted in a manner that is of its time and reversible. Avoid physical intervention with existing plaster box cornices in rooms, architraves, dado rails. Position outlet grilles in extneral walls on centreline of arcade arches and above structural arch	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.014	Painted signs	BLOCK A	High	Protect in situ	Not applicable	N/A
04.015	Fixed signs		Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.016	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.017	Toilets at ends of verandahs		Adverse	Remove and make good finishes	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.018	Partitions at GF Dormitory A		High	Remove to make way for Interpretation	Prepare measured drawings and photographs before removal.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.019	Switchgear in old porch 04/G/13		Adverse	Open up porch, remove electrical switchgear and make good	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.020	Flat plywood ceiling lining with plain rectangular cover battens		Adverse	Replace with T&G boarding to match existing	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.021	Steps up to doorway on FF verandah	EXIT HIS	Moderate	Remove steps and doorway to form new fore escape route	Record steps and doorway on measured drawings	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.022	Timber boarded floors with moulded skirtings		High	Retain all boarded floors and skirtings	Reinstate floor boards and skirtings after fire proofing works	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.023	Cantilever balconies		High	Retain and repair as necessary. Reinstate balcony on west elevation.	Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.024	Clay tile floor		Low	Retain and repair as necessary	Not applicable	Neutral
04.025	Matched- boarded ceiling with perforated border		Moderate	Repair and retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.026	Ceiling rose		Low	Repair and retain insitu	Not applicable	Neutral

06 Dormitory C

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.001	Granite thresholds at external doors		Low	Retain; install timber deck flush with level of step where necessary	Avoid alteration to step.	Low
06.002	Pitched roof		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.003	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High
06.004	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.005	Altered doors and windows		Adverse	Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable
06.006	External airconditioning units and other external services		Adverse	Adverse	Remove and make good brickwork	Not applicable

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.007	Painted signs	C. CC.	High	Protect in situ	Not applicable	N/A
06.008	Fixed signs	衛生署 DEPARTMENT OF HEALTH 中央警署診疫所 POLICE MEDICAL POST CENTRAL POLICE STATUS	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.009	Cantilever balconies		High	Retain and repair as necessary.	Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective.	Low
06.010	Iron balustrades		High	Retain and repair as necessary.	Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.011	Perforated margin at perimeter of ceiling	EUTED	Low	Repair and retain.	Where fire-proofing of floor is required, use a product that can be installed within the floor void, leaving the ceiling lining intact.	Low
06.012	Block existing door openings	EXIT	Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.013	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate
06.014	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.015	Timber floors		High	Retain all boarded floors and skirtings	Reinstate floor boards and skirtings after fire proofing works	Low
06.016	Vinyl tile floor		Adverse	Remove tiles; renew boarded floor boards if necessary	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.017	Batten and panel ceiling lining		Low	Replace with lath and plaster ceiling	Not applicable	Low
06.018	Exposed roof covering		Moderate	Retain as existing	Consider insulating between upper and lower layers of roof tiles to provide thermal insulation and vapour barrier	Low

07 Dormitory D

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.001	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High
07.002	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.003	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High
07.004	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.005	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
07.006	Clothes drying racks		Adverse	Remove	Not applicable	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.008	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
07.009	Corbelled brickwork at perimeter of room		Low	Remove in exceptional cases where eg. where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.010	Plywood floor		Adverse	Replace with hardwood floor boards	Not applicable	High
07.011	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.012	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate
07.013	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.014	Fixed signs	The state of the s	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.015	Exposed roof tiling		Moderate	Retain as existing	Consider insulating between upper and lower layers of roof tiles to provide thermal insulation and vapour barrier	Low
07.016	Concrete floor		Adverse	Overlay with hardwood floor boards	Not applicable	Moderate

08 Ablutions Block

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.001	Panelled doors		Low	Replace where necessary to achieve compliance with Building Code	Re-use where possible. Record design on survey drawings where element cannot be re-used.	Moderate
08.002	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.003	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High
08.004	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.005	Timber roof structure		High	Retain	Not applicable	Neutral
08.006	External stair at west end		Moderate	Retain	Repair as necessary. Alter balustrade to achieve reasonable level of operational safety. Restrict access to repairs and maintenance and means of escape.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.007	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
08.008	Painted signs	MO VISITOR WILL BE ADMITTED WITHOUT THE PERMISSION OF THE D.O. OR FORMALION COMMADER 支管工業等計算可以 进程件不可計算型值數	High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.009	Wire mesh screens		Adverse	Remove	Not applicable	Low
08.010	Internal walls and concrete floors		Low	Remove and rebuild in new configuration to suit new use	Ensure retained facades are fully supported during construction operations. Protect retained walls against damage during demolition works. Install new walls and floors to respect fenestration; avoid	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
					clashes.	
08.011	Cantilever balconies on north side		Moderate	Repair and retain insitu	Not applicable	

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.012	Bridge access to Barrack Block		Moderate	Retain	Repair as necessary. Alter balustrade to achieve reasonable level of operational safety. Restrict access to repairs and maintenance and means of escape.	Low
08.013	Balcony balustrades		Low	Repair as necessary and retain. Remove selected sections to enable installation of new bridge connections to Barrack Block.	Avoid removal of associated iron columns. Form interventions at selected positions so as to maintain the rhythm of the balustrades and ensure proper support at ends.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.014	Single-storey outbuilding with pitched roof over		Low	Demolish to make way for new loading bay.	Record on measured survey drawings. Infill existing internal opening leaving reveals exposed. Tooth-in new brickwork at abutments after existing walls removed. Salvage cast iron columns for possible re-use.	Low
08.015	Corrugated steel sheet on balcony balustrades		Adverse	Remove	Not applicable	Low

Schedule of Character Defining Elements

Central Police Station

09 Magistracy

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
09.002	Modern partitions		Adverse	Remove	Not applicable	N/A

Schedule of Character Defining Elements

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.003	Internal walls		Moderate	Remove selected internal walls where strictly necessary as part of replanning of interiors	Walls or early or original date to be retained in part eg. By leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not rebonded, as evidence of the current condition.	Moderate
09.004	Plaster box cornice		Moderate	Remove in exceptional cases eg. Where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.005	Panelled doors		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where element cannot be re-used.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.006	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Moderate
09.007	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.008	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate
09.009	Fixed signs	SECTION OF	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.010	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
09.011	Pitched roofs	Boo	High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.012	Rainwater goods		Moderate	Replace with larger sizes/closer spacing to improve performance	Use cast iron to match original pattern Make good all redundant fixing holes	High
09.013	Metal walkways across lightwell		Adverse	Remove walkways and make good brickwork at abutments	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.014	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High
09.015	Sloping canopy over external stair on west side		Adverse	Remove canopy and supporting structure	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.016	Single storey secure shelter at North West corner		Low	Demolish	Make good brickwork at abutments.	Low
09.017	Iron railing adjacent south side of item 09.016 above		Moderate	Retain; including remains of bars (now removed) between existing railings and east side of Barracks Block.	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.018	Public toilets in 09/LG1/17, 24		Adverse	Strip out sanitaryware, and fit-out for pottery display/service access. Form new door openings in east walls.	Retain existing door openings and metal- barred gates. Retain external granite steps and existing ground level.	Low
09.019	Cell doors		High	Re-open to provide access to Retail space	Retain existing iron gate	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.020	Meeting room at G/02-05		Moderate	Remove timber panelling from walls and sub divide to form new toilets and lift shaft	Record existing wall linings, and any earlier lining behind, on measured survey drawings.	Moderate
09.021	Lobbies within entrance hall G/12		Adverse	Remove	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.022	Public galleries on FF		Adverse	Strip out plant, remove partition walls and restore galleries	Not applicable	High
09.023	Chimney piece		Moderate	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.024	Lanterns above entrance hall		Adverse	Remove existing lanterns and install single lantern	Not applicable	Moderate
09.025	Boarded ceilings on Second Floor		High	Repair and retain where possible	Limit extent of penetrations as far as practicable. Record on measured survey drawings where ceilings have exceptionally to be removed.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.026	Iron gates at top of external stair		Moderate	Retain	No applicable	Neutral
09.027	Iron balustrade adjacent terrace at First Floor east side		High	Retain; install structural glass balustrade inboard of ironwork to provide compliance with Building Codes	Avoid penetration of existing tiled pavement when fixing glass balustrade.	Low

10 Assistant Superintendent's Office

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
10.002	Plaster box cornice		Moderate	Remove in exceptional cases eg. Where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.003	Panelled doors and linings		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where element cannot be re-used.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.004	Timber boarded floor with moulded skirtings		High	Repair as necessary and retain	Lift carefully and refix upon completion of fire- proofing and services installation	Low
10.005	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.006	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Moderate
10.007	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.008	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High
10.009	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.010	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.011	Fixed signs	「「「「「」」」」「「」」」「「」」」「「」」」「「」」」「「」」」「「」	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A
10.012	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.013	Internal walls		Moderate	Remove selected internal walls where strictly necessary as part of replanning of interiors	Walls or early or original date to be retained in part eg. By leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not rebonded, as evidence of the current condition.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.014	Partitions on SF		Moderate	Remove partitions	Record partitions on measured drawings	Moderate
10.015	Blocked windows on south elevation of south-east wing		Adverse	Re-open window openings and reinstate window frames and glazing	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.016	Open-joisted ceiling on Ground Floor of south- east wing		Moderate	Underline floor to provide fire protection.	Avoid intrusive alteration. Use fire-proofing products and methods that enable existing structure and boarding to be retained.	Low
10.017	Moulded timber picture rail		Low	Repair and retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.018	Timber roof structure above south-east wing		Moderate	Repair as necessary and retain	Avoid intrusive alteration. Retain open appearance/	Low
10.019	Timber stair		Moderate	Underline with fire- resisting lining	Repair as necessary and retain.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.020	Clay/terrazzo tile floor on Ground Floor and steps		Adverse	Adjust levels to enable level access and replace floor finish	Not applicable	Low
10.024	Granite wall on North elevation		High	Construct new external steps adjacent wall	Keep new stair clear of wall; avoid any physical connection between steps and wall.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.025	Single storey outbuilding at South East corner		Moderate	Demolish outbuilding and make good at abutments	Record outbuilding on measured drawings	Low
10.026	Blocked archway on East elevation		Adverse	Demolish infilling and reopen archway	Protect original arch and jambs against damage during demolition	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.027	Chimney on east elevation		Low	Retain	Not applicable	Neutral
10.028	Cantilever balconies		High	Repair as necessary and retain	Avoid intrusive interventions. Restrict access if necessary to retain existing appearance.	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.029	Steps on east elevation		Moderate	Repair as necessary and retain	Not applicable	Neutral
10.030	Decorative metal screen (See also item 10.026)		Low	Repair and retain	Not applicable	Positive

11 A Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.001	Form new door openings		Low	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.002	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
11.003	Painted signs		High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.004	Fixed signs	AL 地灣 CAUTION SLIPPERY FLOOR	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A
11.005	Concrete stairs		Low	Remove and rebuild as part of re-planning of interiors	None	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.006	Flat roof		Low	Form new rooftop extension at West end to accommodate fire escape stair	Form straight joint at abutment with building 08 Ablutions Block	Low
11.007	Security screen at roof level		Low	Remove	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.008	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.009	Rainwater goods		Low	Remove embedded cast iron pipework set into wall to reduce long term maintenance burden	Record on measured survey drawings. Make good cavity.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.010	Timber doors		Low	Repair and retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.011	Security screen and door at First Floor	C ENTHED	Low	Remove	Record on measured survey drawings	Low
11.012	Door thresholds and plinth		Low	Retain; remove paint media from plinth and brickwork	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.013	Metal louvres on window openings		Adverse	Remove	Not applicable	Low

12 B Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.001	Flat roof		Moderate	Repair and retain	Avoid roof penetrations as far as possible	Low
12.002	Cells at GF level		High	Remove cells in selected locations to accommodate new North-South route across site	Record existing layout on measured survey drawings. Limit number of cells affected to the minimum necessary. Retain floor structure above. Retain remainder of cells at this level for interpretation	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.003	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
12.004	Painted signs		High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.005	Fixed signs	Control of the contro	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A
12.006	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High

Schedule of Character Defining Elements

Central Police Station

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.007	Corbelled brickwork at high level in cells		Low	Retain	Not applicable	Neutral
12.008	Barbed wire		Moderate	Remove	Record wire on measured drawings	Low

Schedule of Character Defining Elements

Central Police Station

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.009	External walls		Moderate	Form openings in North and South walls in conjunction with new North-South route across site	Cut brickwork to form openings in North and South walls; do not re-bond brickwork.	Moderate

13 C Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.001	External airconditioning units and other external services		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.002	Door to Ladder Store		Low	Retain	Not applicable	Neutral
13.003	Security bars at window openings		Low	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.004	Flat roof		Low	Retain	Avoid roof penetrations as far as possible.	Low
13.005	Eaves detail		Low	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.006	Cantilever reinforced concrete canopy		Low	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.007	Internal partition walls		Low	Remove as part of replanning of interiors	Record on measured survey drawings	Low
13.008	Fixed signs	The second secon	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.009	Metal window frames		Moderate	Repair and retain	Not applicable	Neutral
13.010	Internal security screens		Moderate	Retain where possible	Where necessary record on measured survey drawings prior to removal	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.011	Coving at abutments between RC beams and walls		Low	Avoid penetrations for services installations as far as possible.	Cut away neatly for services penetrations and make good at abutments.	Low
13.012	Communal cells at Ground Floor		Moderate	Remove as part of replanning of interiors	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.013	Rooflight and security bars over communal cells		Moderate	Remove as part of replanning of interiors	Record on measured survey drawings	Low
13.014	Granite threshold at external door openings		Low	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.015	Timber boarded doors with fanlight over		Low	Repair as necessary and retain	Not applicable	Neutral
13.015	Vinyl tile floor		Adverse	Replace	Not applicable	Low

Schedule of Character Defining Elements

Central Police Station

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact

14 D Hall East Wing

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.001	West entrance at Lower Ground Floor		Moderate	Retain as public entrance at this level.	Retain security gate and granite threshold. Adjust adjacent ground level as necessary to achieve barrier-free access. Pin gate back against adjacent wall in the open position if necessary.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.002	Half-round headed doorway and side lights		Moderate	Retain	Remove air duct and make good masonry above arch.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.003	Granite surround to cells (generally north side, alternating with brick surrounds – see next item)	3	Moderate	Retain door surround and gate wherever possible.	Pin back gate against wall. Remove paint media to expose granite material.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.004	Brick reveals with bull-nosed arrisses and segmental arch over (generally north side, alternating with granite surrounds – see previous item)		High	Retain door surround and gate wherever possible	Pin back gate against wall	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.005	Arched opening at East end First Floor		Low	Retain as existing	Not applicable	Low
14.006	Concrete floor generally at Lower Ground Floor		Low	Excavate entire floor to install piled underpinning	Record levels on measured survey drawings. Install new floor at the same level.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.007	Part-blocked windows at Lower Ground Floor - extent of blocking varies.		Moderate	Open up window opening to full extent.	Record existing condition on measured survey drawings. Add further detail during demolition works.	Low
14.008	External granite stair from Lower Ground to Ground Floor level		Moderate	Remove stair to make way for new stair in similar position	Review design proposals to see whether existing stair can be retained.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.009	Ashlar pattern on external walls		Moderate	Form new openings for entrance/exit to building	Set out new openings to cause minimum disruption to ashlar pattern. Record existing pattern on measured survey drawings.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.010	Blocked doorway at south-east corner		Low	Preserve blocked opening intact.	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.011	Metal security gate and screen		Low	Retain insitu	Pin gate in open position if necessary	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.012	Half-round headed doorway and side lights at Ground Floor west end		Moderate	Retain insitu	Not applicable	Neutral
14.013	Structural steelwork bracing and temporary access stair		Adverse	Remove upon completion of underpinning	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.014	RC staircase at north-east corner		Low	Remove	Record on measured drawings	Low
14.015	Vinyl tile floor on suspended timber floor		Adverse	Remove vinyl tiles and restore boards if possible; alternatively, replace boards with new timber to match other boarded floors elsewhere on the site.	Not applicable	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.016	Cell walls at Ground Floor		Moderate	Retain insitu	Use existing door openings wherever possible. Avoid further alteration to existing altered openings where feasible.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.017	Mortuary		High	Preserve insitu	Avoid any service penetrations from adjacent spaces	Neutral
14.018	Brickwork surrounds to doorways with segmental arches over		Moderate	Increase width in selected locations to allow wheelchairs to pass	Record on measured survey drawings. Limit interventions as far as possible.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.019	Granite surrounds to doorways with lintels over		Moderate	Increase width in selected locations to allow wheelchairs to pass	Record on measured survey drawings. Limit interventions as far as possible.	Low
14.020	Flat ceilings at Ground Floor	A	Low	Form penetrations for services installations where necessary	Avoid disruption of beams.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.021	Arched opening at east end		Low	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.022	Top-lit central hall		High	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.023	Arches across central hall at First Floor		Moderate	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.024	Inset security gate and screen in First Floor cells		Low	Remove to suit new use	Remove where necessary. Record on measured drawings.	Low

14 D Hall West Wing

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.030	Main stair		High	Remove wire mesh and framing	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.031	Brick vault over central hall at Ground Floor		High	Retain insitu	Not applicable	Neutral
14.032	Terrazzo floor in central hall at Ground floor		Moderate	Remove to enable piled underpinning	Record on measured survey drawings	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.033	Brick vaults above cells		High	Retain insitu	Avoid penetrations for services	Neutral
14.034	Cell walls (later additions)		Moderate	Remove where necessary to accommodate new cafe	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.035	Brickwork spandrels below cell windows on south side at Ground Floor		Moderate	Remove to accommodate new cafe	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.036	Cell walls flanking central hall		High	Remove to accommodate new cafe	Record on measured survey drawings. Retain selected cells for interpretation purposes.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.037	Cell floors		Low	Remove to enable piled underpinning	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.038	Partition wall across central hall at Ground Floor		Low	Remove to accommodate new cafe	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.039	Granite pavement in cross-passage between East and West Wings		Moderate	Repair as necessary and retain insitu	Not applicable	Neutral
14.040	Granite threshold at doorway between cross- passage and East Wing		Moderate	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.041	Brick vault over cross-passage		High	Retain insitu	Avoid any services penetrations	Neutral
14.042	Granite floor in central hall at First Floor		Moderate	Retain insitu	Repair where necessary	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.043	Cell walls flanking central hall at First Floor		High	Retain insitu	Not applicable	Neutral
14.044	Brickwork spandrels below cell windows at Second Floor		Moderate	Remove to enable new use	Record on measured drawings. Confine changes to one elevation, north or south.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.045	Metal security screen adjacent main stair		Moderate	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.046	Double-height central hall at Second Floor		High	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.047	View ports adjacent entrance doors		Moderate	Retain insitu	Not applicable	Neutral
14.048	Services installations		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.049	Metalwork and structural steel framing on exterior (typical)		Adverse	Remove	Not applicable	High
14.050	Blind arcade, south elevation		Low	Remove infill brickwork within arched openings at ground level to enable new cafe	Record on measured survey drawings. Observe and record any evidence that brickwork infills were built at the same time as the arched openings or added later	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.051	Blind arcade, north elevation		Low	Retain insitu	Not applicable	Neutral
14.052	Fence wall, east end of D Hall Yard		Low	Remove to reinstate access to granite stair to Lower Ground Floor level	Record on measured drawings	Low

15 E Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.001	Dividing walls at Lower Ground Floor		Moderate	Remove to enable multi- purpose use	Record on measured survey drawings	Low
15.002	Dividing walls at Lower Ground Floor		Moderate	Remove to enable multi- purpose use	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.003	Staircase within Laundry Yard		Moderate	Remove to enable construction of Arbuthnot Wing	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.004	Services installations		Adverse	Remove	Not applicable	Moderate
15.005	Metal louvres over cell window openings		Low	Remove	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.006	Raised ground level adjacent entrance		Low	Remove to enable level access	Record on measured survey drawings	Low
15.007	Access balconies and apertures		Moderate	Retain apertures	Provide temporary closure as required for operational reasons	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.008	Central staircase		High	Retain	Provide secondary staircase within cell blocks to achieve code compliance	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.009	Cell walls flanking central hall		High	Retain	Pin back cell doors against walls.	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.010	Services installations	38.000.00	Adverse	Remove	Not applicable	Moderate
15.011	Balcony balustrades		Moderate	Retain	Install wire net across aperture to avoid need to upgrade balustrade to meet Building Code requirements	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.012	Second Floor central hall		High	Retain	Not applicable	Neutral

17 F Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.002	Rainwater goods		Low	Remove existing RWPs and install new RWPs externally on North and South Elevations	Improve roof drainage to avoid ponding	Low
17.003	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.004	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
17.005	Fixed signs	PRISONERS' PRIVATE CLOTHING STORE 犯人私家衣服儲藏室	Moderate	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.006	Security screen at First Floor entrance		Low	Remove	Record on measured drawings	Low
17.007	Metal windows		Moderate	Remove at First Floor to accommodate gallery space and block structural openings with blockwork	Record on measured drawings.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.008	Fixed furniture		Moderate	Remove to accommodate gallery space	None	Low
17.009	Security screens		Moderate	Remove to accommodate gallery space	Record on measured drawings	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.010	Timber windows		Moderate	Remove at First Floor to accommodate gallery space and block structural openings with blockwork	Record on measured drawings	Moderate
17.011	Communal washing/lavatory facilities		Moderate	Remove to accommodate gallery space	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.012	Blocked up lantern light		Low	Unblock lantern and fit glazing	Record on measured drawings	Low
17.013	Security gates at Ground openings		Moderate	Remove to enable access to Ground Floor gallery space	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.014	Interview booths		High	Remove to accommodate new gallery	Rebuild in new location	Moderate
17.015	External stair to First Floor		Moderate	Upgrade balustrade to comply with Building Code	Record on measured drawings. Supplement existing balustrade elements with minimal elements if necessary.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.016	Ground Floor main entrance		Low	Retain as existing.	Keep fixed shut if not required for operational use.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.017	Security screen at Ground Floor main entrance	The desire of the second secon	Low	Remove to accommodate gallery space	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.018	Blue Entrance Gate (facing Old Bailey Street)		High	Retain in situ	Maintain in working order	Neutral
17.019	Blue Entrance Gate (inner) and enclosed yard		Moderate	Retain gate and enclosing walls and roof in situ; remove cupboards.	Repair and maintain gate in working order	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.020	Blue Entrance Gate (inner) facing Prison Yard		Moderate	Retain gate and enclosing frame	Repair and maintain in working order	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.021	Barbed wire		Moderate	Remove	Record on measured drawings. Make good fixing points where attached to brickwork.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.022	Metal security bars at windows		Moderate	Remove as part of blocking up window openings to accommodate gallery space at First Floor	Record on measured drawings	Low
17.023	External toilets at Ground Floor adjacent East elevation		Low	Remove	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.024	Open Visit Room		Low	Space reallocated to other uses	Record on measured drawings. Salvage entrance sign and re-use in new layout of interview booths.	Low

19 Bauhinia House

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.001	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High
19.002	Chimney		High	Repair and retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.003	Rainwater goods and other external services		Adverse	Remove and make good wall surface. Replace defective and non-matching rainwater goods with cast iron fittings to match original.	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.004	External stone wall facing		High	Carry out close inspection of painted areas to determine extent of original granite facing and remove paint media where applicable.	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.005	Gun loops		High	Remove concrete infilling and make good stonework where necessary.	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.006	Look-out turret		High	Repair and retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.007	Windows		Moderate	Remove and make good stonework as necessary	Record existing windows on measured survey drawings	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.008	Modern partitions		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.009	Electrical services		Adverse	Remove	Not applicable	Moderate
19.010	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.011	Exposed timber roof structure		High	Repair and retain insitu	Not applicable	Neutral
19.012	Timber stair		Moderate	Remove	Record on measured surveys drawings	Low
